


## Occupant Impact Statement

Project Name: OMD Anderson Readiness Center  
 Project Address: 3225 State Street, Salem, OR 97309  
 OMD Project Number: 209996D001  
 Date: August 14, 2023 through September 15, 2023  
 Point Of Contact: Dan Loreto

### Construction Work Hours

Ausland Group proposes the following work schedule for the **ROOF WORK** on the dates referred to above


- Work hours for Area F will be M - F: 7:00 AM to 3:30 PM
- No nighttime or weekend work is planned
- The work is expected to begin Monday, August 14, 2023.

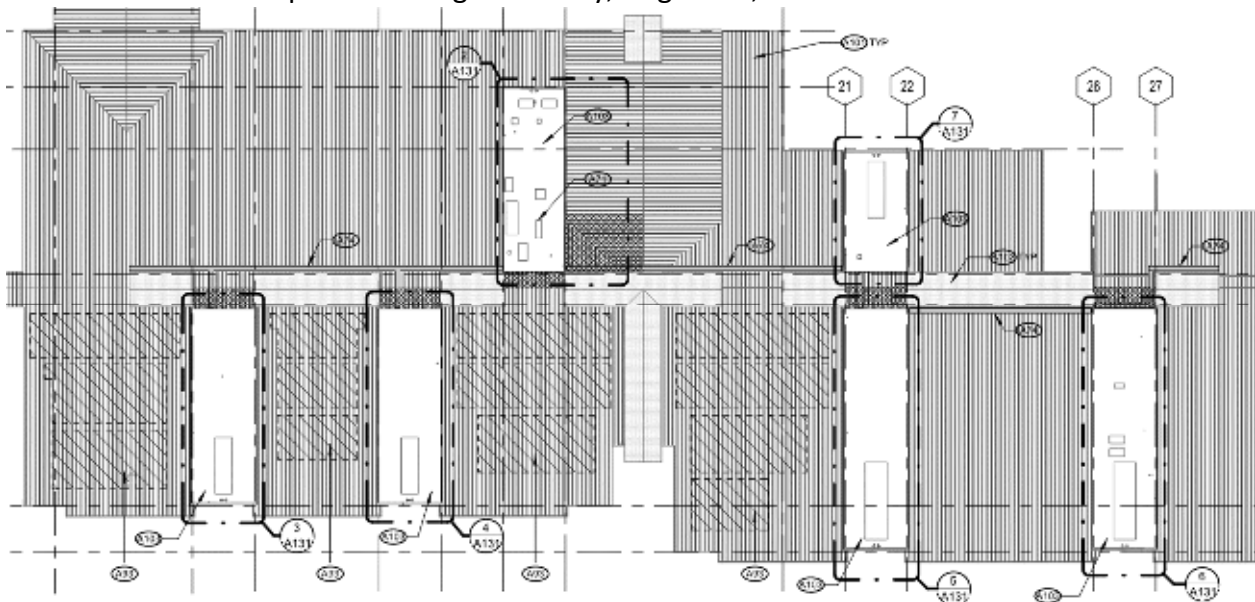

The sequence of construction activities for the ROOF WORK will be as follows:

- Demo existing roofing at each mechanical well
- Install new roofing. A crane will be brought on site to load materials onto roof for each mechanical well.
- Providing flashing as required around mechanical equipment curbs.
- Dispose of construction debris off site

- Work area cleanup and final punch walk.

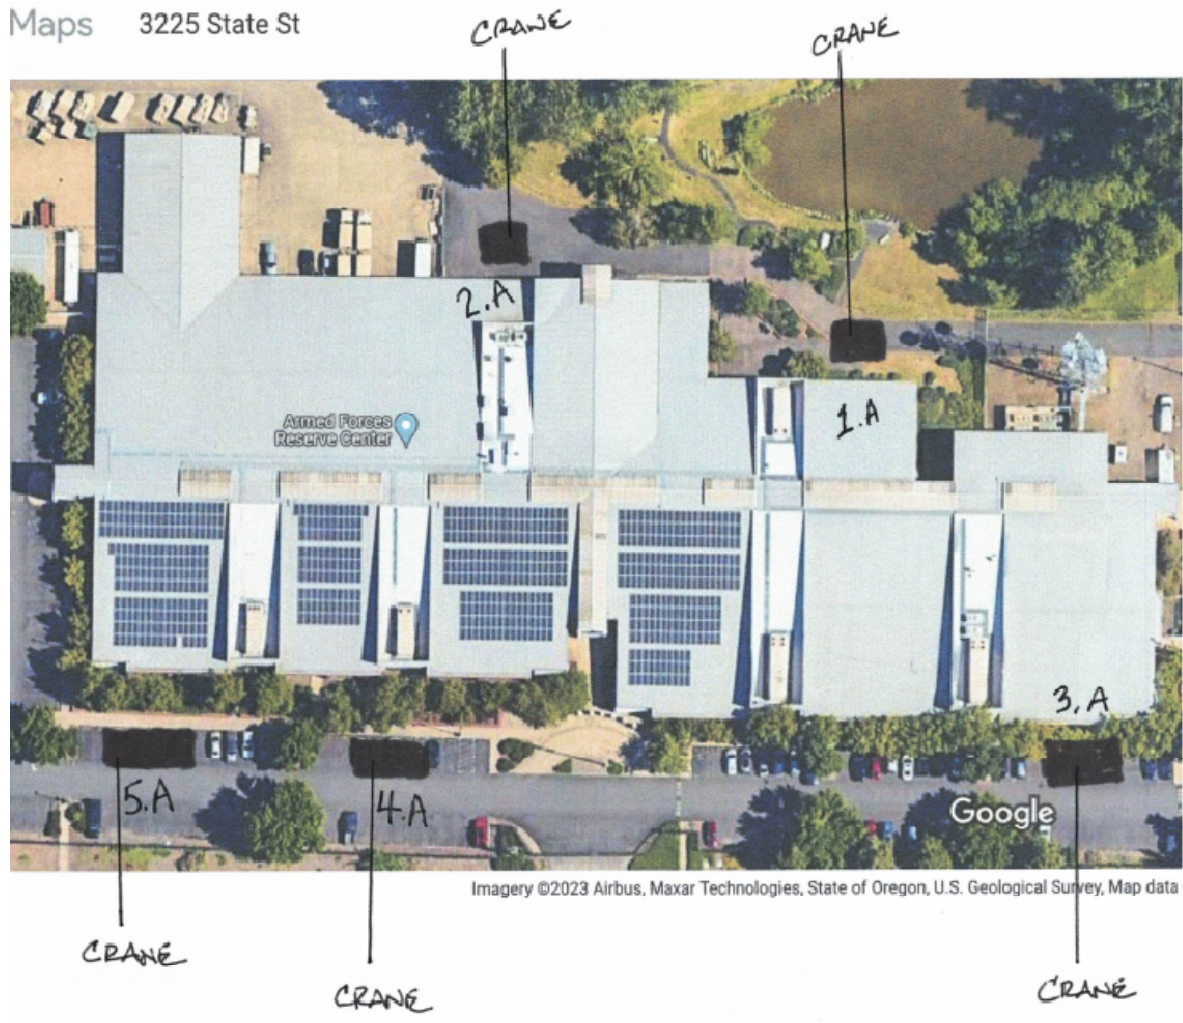

### **Impact To Occupants**

The impacts to building occupants should be minimal since the work will be occurring on the exterior of the building. Noise from mechanical equipment for demolition and material handling will contribute to noise near the building. When the crane is being utilized, portions of the parking lot may be cordoned off for safe loading of materials to Roof(see below image of crane locations).

The schedule for the crane will be as follows:

1.A: 8/15

2.A: 8/22

3.A: 8/29

4.A: 9/6

5.A: 9/12

**Work Area Impact**

Ausland Group anticipates that impact will be typical of roof work. The above dates identify dates when portions of the parking lot will be utilized for construction purposes. These locations will be cordoned off the day before with cones and caution tape to ensure the crane will have access to operate.

**Odor Mitigation** none anticipated

**Portable Facilities:** none anticipated

**Material Storage Containers:** none anticipated

**Work Safety Zone:** as identified on the drawings.
