



# **SB 338 Progress Report on Oregon's Stimulus Package**

Putting Oregonians to work on projects  
across the state

June 17, 2009  
Progress Report #2



<http://oregon.gov/recovery/GoOregon.shtml>

## TABLE OF CONTENTS

### Overview

Executive Summary .....	1
Overview of Jobs.....	2
Project Detail.....	3
Project Dates.....	3
Project Status and Completion Dates .....	4
Expenditures and Jobs Created.....	5
Construction Hours and Oregon Residents .....	6
Oregon Products and MWESB .....	7
Energy Efficiency .....	8
Jobs and Expenditures by County .....	9

### Agency Summary

Department of Administrative Services (DAS) .....	11
Department of Corrections (DOC).....	12
Oregon Department of Fish and Wildlife (ODFW).....	13
Oregon Department of Forestry (ODF) .....	14
Oregon University System (OUS) .....	15
Oregon Judicial Department (OJD).....	18
Oregon Military Department (OMD) .....	19
Oregon Parks and Recreation Department (OPRD) .....	20
Department of State Lands (DSL).....	21
Oregon Department of Transportation (ODOT) .....	22
Oregon Youth Authority (OYA).....	26
Community College Workforce Development.(CCWD).....	27

<b>Project Notes</b> .....	<b>32</b>
----------------------------	-----------

<b>Agency Point of Contacts</b> .....	<b>60</b>
---------------------------------------	-----------

## Executive Summary

The Oregon Legislature enacted Senate Bill 338 in February 2009, to stimulate Oregon's economy. The bill authorized 547 deferred-maintenance projects to create new jobs by infusing \$175 million into the market. Known as the "Go Oregon! Economic Stimulus Recovery Package," the bill placed the Department of Administrative Services (DAS) in the lead role to coordinate, oversee and report on the projects, managed by 12 state agencies.

This report represents a summary view of the status of Go Oregon! projects. A more in-depth report of agency-level data and source documents appears online: [www.oregon.gov/recovery](http://www.oregon.gov/recovery).

### Statistics in Brief (Data as of May 31, 2009)

Planned and Actual Project Start Dates	Total started projects = <b>477</b> Thru May, <b>468</b> projects planned to start; <b>477</b> actually started.
Project Status	Of the projects started, <b>357</b> are on schedule; <b>13</b> are behind schedule; and <b>107</b> are complete.
Project Completion Date (or scheduled completion date if ongoing)	<ul style="list-style-type: none"> <li>• <b>167</b> projects are scheduled for completion by July, 2009.</li> <li>• Another <b>200</b> projects are scheduled to be completed between July and December 2009.</li> <li>• The remaining projects are larger, more complicated projects; some will last until 2011.</li> </ul>
Expenditures to Date	<b>\$ 13,463,996</b>
Number of Jobs Created or Retained	<b>542</b> jobs created; <b>2,694</b> jobs retained ( <b>3,236</b> total)
Number of Construction Hours Worked	<b>89,164</b>
Percentage of Jobs Filled by Oregon Residents	<b>81 percent.</b> Oregon residents filled <b>2,614</b> of the <b>3,236</b> total jobs.
Extent to Which Oregon Products, Vendors, Contractors and Sub-Contractors Used	<b>88 percent.</b> Of the <b>2,875</b> companies that supply materials and labor to complete Go Oregon! projects, <b>2,532</b> are based in Oregon.
Extent to Which Minority, Women, and Emerging Small Businesses Used	<b>8 percent.</b> Of the <b>4,375</b> total firms contracted, <b>350</b> hold an MWESB certificate in Oregon.
Savings on Energy Costs for Energy Efficient Projects	<b>\$12,063,890</b>

## Overview of Jobs

### Go Oregon! Jobs

#### **New vs. Sustained -- What they are and how they are measured.**

Oregon workers have benefited from *Go Oregon!* projects in two ways. They have either gotten work as new hires (**New Jobs**), or they have stayed on their companies' payrolls to help complete *Go Oregon!* projects (**Sustained Jobs**). A "New Job" is a *Go Oregon!* job on a project for which a contractor hires additional workers who are not already on the payroll. A "Sustained Job" is one that a worker already on the payroll would likely have lost, if not for the *Go Oregon!* project.

#### **Example of New Jobs:**

If Acme Construction hires two new workers in April for work on a *Go Oregon!* project, the company's New Job for April count is 2. If, in May, Acme decides it needs even more workers for the project and hires three more, its New Jobs count for May is 3. For the *Go Oregon!* report prepared in June, which summarized all activity through the end of May, the Total New Jobs for the Acme Construction will be 5 (two in April plus three in May).


When a company receives contracts for a *Go Oregon!* project and puts a person already on its payroll to work on the project, this is an example sustaining an existing job. Jobs retained in this way are included in the Sustained Jobs count. The Sustained Job count reflects the total number of workers that worked for a company before it received the *Go Oregon!* contract.

#### **Example of Sustained Jobs:**

If the state awards Case Construction a contract for a *Go Oregon!* project in April, and the company assigns four of its employees to work on the project, these four employees are included in the Sustained Jobs count for April. If the project nears completion in May, and Case finds it needs to keep only two at work on that project, the Sustained Jobs count for the project remains at 4. This is because the *Go Oregon!* project did keep four workers employed for a period of time. If the project concludes during the first week of June, the Sustained Jobs count remains at 4.

## Project Detail


### Planned project start date

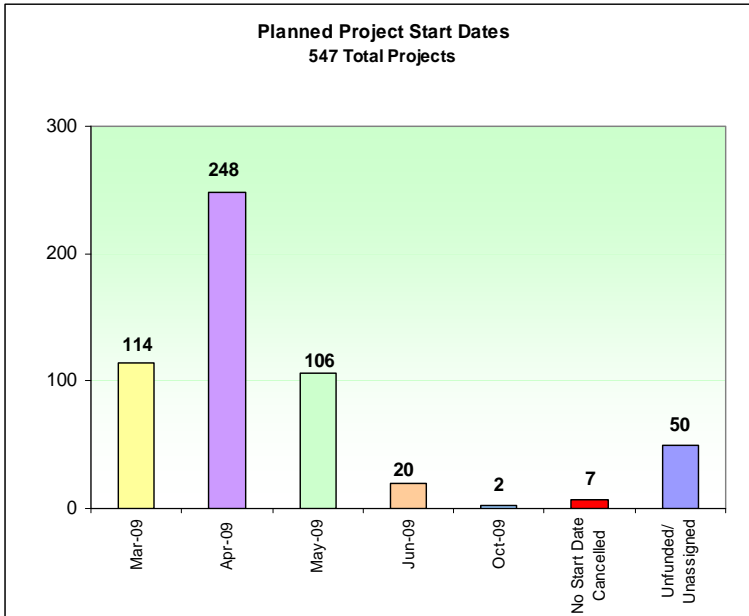

	Mar-09	Apr-09	May-09	Jun-09	Oct-09	No Start Date Cancelled	Unfunded/Unassigned	Total
DAS	6	2	0	0	0	0	2	10
DOC	6	4	0	0	0	0	0	10
ODFW	5	19	0	0	0	0	0	24
ODF	1	5	5	4	0	2	2	19
OUS	18	48	12	12	0	2	13	105
OJD	0	1	0	0	0	0	0	1
OMD	0	4	13	1	0	0	0	18
OPRD	1	7	0	0	0	0	0	8
DSL	3	0	0	1	0	0	0	4
ODOT	34	53	10	0	2	3	32	134
OYA	0	0	26	0	0	0	1	27
CCWD	40	105	40	2	0	0	0	187
<b>Total</b>	<b>114</b>	<b>248</b>	<b>106</b>	<b>20</b>	<b>2</b>	<b>7</b>	<b>50</b>	<b>547</b>

The “planned project start date” represents the date when the responsible agency *anticipated* that people would begin to work on projects regardless of whether that meant architects or electricians. Every aspect of a project provides people with employment.



### Actual project start date

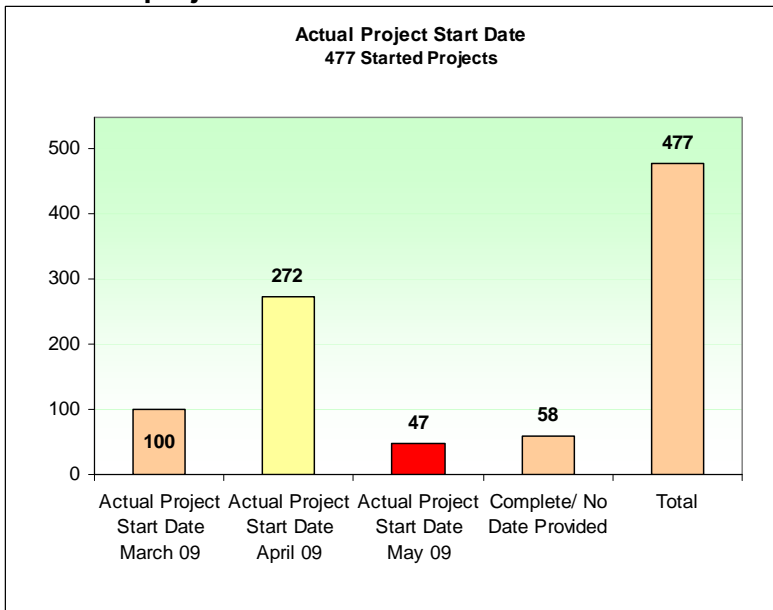

	Actual Project Start Date March 09	Actual Project Start Date April 09	Actual Project Start Date May 09	Complete/ No Date Provided	Total
DAS	4	2	0	2	8
DOC	0	1	4	2	7
ODFW	0	3	12	3	18
ODF	1	6	7	0	14
OUS	14	70	5	2	91
OJD	0	1	0	0	1
OMD	0	15	2	0	17
OPRD	6	0	0	2	8
DSL	0	3	0	0	3
ODOT	3	34	13	47	97
OYA	26	0	0	0	26
CCWD	46	137	4	0	187
<b>Total</b>	<b>100</b>	<b>272</b>	<b>47</b>	<b>58</b>	<b>477</b>

The “actual project start date” represents the date when the responsible agency first employed people to work on the project in any capacity.


**Project status**

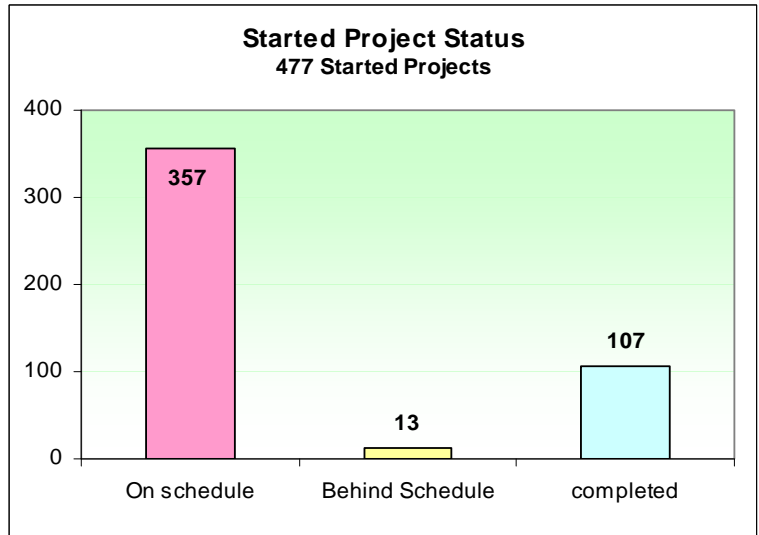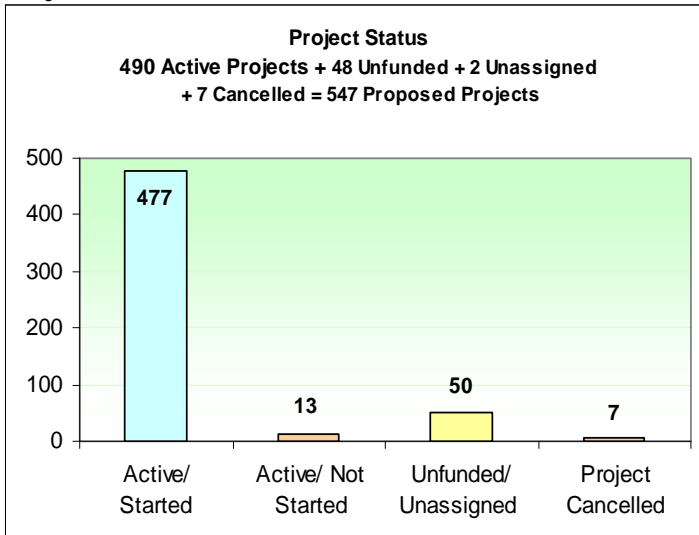

To simplify tracking, DAS established seven status levels:

1. Started – people have been employed to support the project
2. Not Started – no one has been employed in support of the project
3. On Schedule – the project is on track with the agency's expected timing for the project
4. Behind Schedule – the project has fallen behind the agency's expected schedule
5. Completed – the agency has successfully completed the project
6. Project Cancelled – the agency stopped the project before completion
7. Undefined Status – an agency has not provided sufficient information for DAS to determine the appropriate status level (DAS will attempt to get further information)


**Project completion date (or scheduled completion date if still ongoing)**

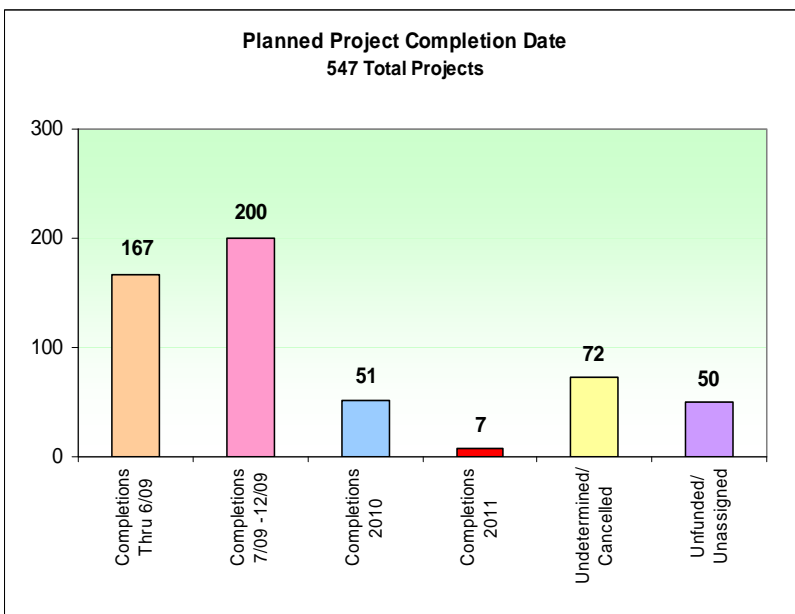

	Completions Thru 6/09	Completions 7/09 -12/09	Completions 2010	Completions 2011	Undetermined/Cancelled	Unfunded/Unassigned	Total
DAS	2	6	0	0	0	2	10
DOC	0	6	1	3	0	0	10
ODFW	6	15	3	0	0	0	24
ODF	9	7	0	1	0	2	19
OUS	39	40	9	2	2	13	105
OJD	0	1	0	0	0	0	1
OMD	7	10	0	0	1	0	18
OPRD	8	0	0	0	0	0	8
DSL	2	1	1	0	0	0	4
ODOT	47	3	0	0	52	32	134
OYA	3	19	4	0	0	1	27
CCWD	44	92	33	1	17	0	187
<b>Total</b>	<b>167</b>	<b>200</b>	<b>51</b>	<b>7</b>	<b>72</b>	<b>50</b>	<b>547</b>

Estimated completion dates through June 2009, represent *completed* and *anticipated* project completion dates. Completion dates signify the date on which the responsible agency grants "final acceptance" of the project.


Expenditures to date

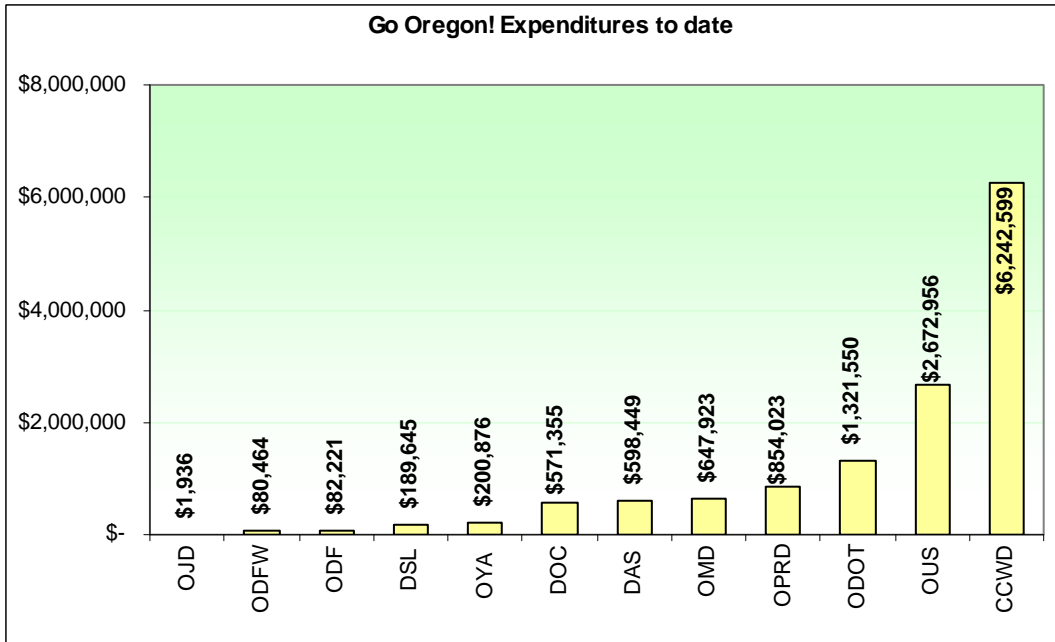

	Expenditures to date
OJD	\$ 1,936
ODFW	\$ 80,464
ODF	\$ 82,221
DSL	\$ 189,645
OYA	\$ 200,876
DOC	\$ 571,355
DAS	\$ 598,449
OMD	\$ 647,923
OPRD	\$ 854,023
ODOT	\$ 1,321,550
OUS	\$ 2,672,956
CCWD	\$ 6,242,599
Total	\$ 13,463,996

“Expenditures to date” reflects the amount of money paid by the State to individuals, contractors or materials-suppliers. Total = \$13,463,996


Number of jobs created or retained

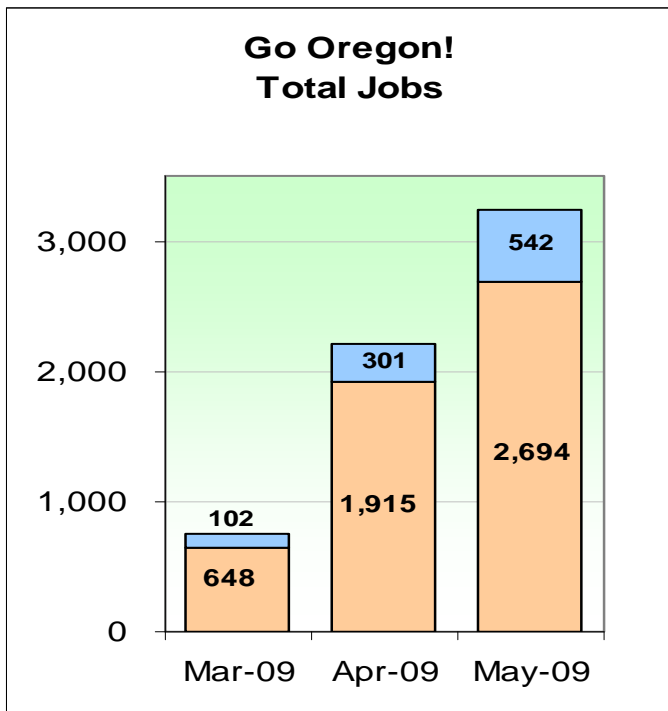

	Total New Jobs	Total Sust. Jobs	Total Jobs
DAS	4	39	43
DOC	0	0	0
ODFW	37	37	74
ODF	0	44	44
OUS	107	658	765
OJD	0	18	18
OMD	37	259	296
OPRD	0	145	145
DSL	2	22	24
ODOT	49	288	337
OYA	76	48	124
CCWD	230	1,136	1,366
Total	542	2,694	3,236

The “number of jobs created or retained” reflects individual people (one person = one job) working on Go Oregon! projects.


**Number of construction hours worked**

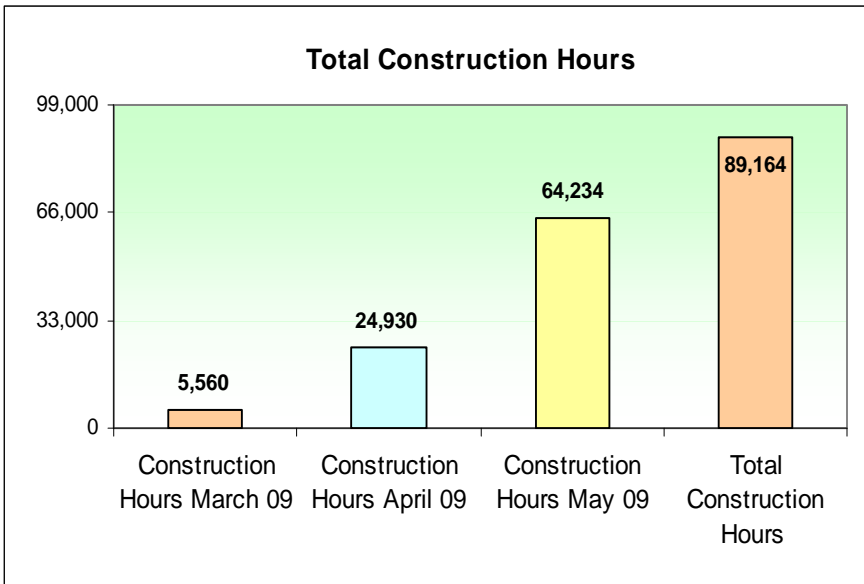

	Construction Hours March 09	Construction Hours April 09	Construction Hours May 09	Total Construction Hours
DAS	612	1805	2055	3860
DOC	0	0	0	0
ODFW	22	146	1117	1263
ODF	54	0	490	490
OUS	1597	2292	8242	10534
OJD	0	4	958	962
OMD	0	858	2967	3824
OPRD	0	3944	4100	8044
DSL	0	0	0	0
ODOT	970	5321	10948	16269
OYA	0	68	68	136
CCWD	2305	10494	33289	43783
Total	5,560	24,930	64,234	89,164

Although Go Oregon! projects involve other types of work, “construction hours” best reflects the most significant labor pool affected.


**Percentage of jobs filled by Oregon residents**

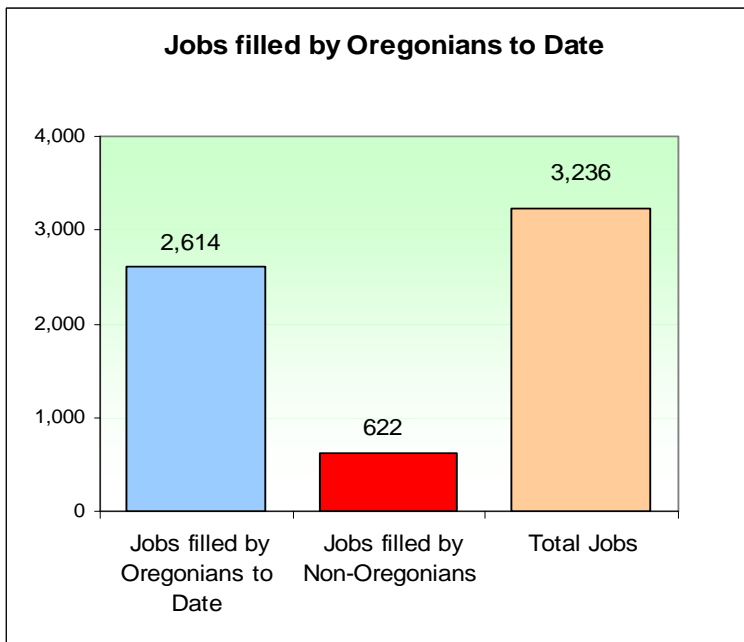

	Jobs filled by Oregonians to Date	Jobs filled by Non-Oregonians	Total Jobs
DAS	38	5	43
DOC	0	0	0
ODFW	68	6	74
ODF	44	0	44
OUS	586	179	765
OJD	18	0	18
OMD	225	71	296
OPRD	72	73	145
DSL	23	1	24
ODOT	298	39	337
OYA	101	23	124
CCWD	1141	225	1366
Total	2,614	622	3,236

Rather than delay the economic benefits of Go Oregon! projects, contractors and businesses supplemented a predominantly Oregonian workforce with non-Oregonians.


**Extent to which Oregon products, vendors, contractors, and sub-contractors used**

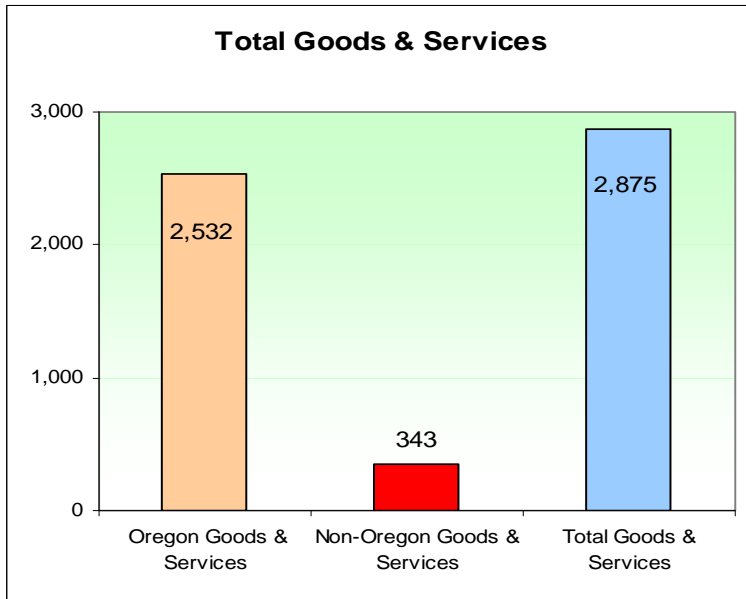

	Total Oregon	Total Non-Oregon Goods & Services	Total Goods & Services
DAS	84	6	90
DOC	0	0	0
ODFW	95	0	95
ODF	22	6	28
OUS	465	85	550
OJD	17	2	19
OMD	270	63	333
OPRD	26	6	32
DSL	13	0	13
ODOT	239	30	269
OYA	59	11	70
CCWD	1242	134	1376
<b>Total</b>	<b>2,532</b>	<b>343</b>	<b>2,875</b>

DAS made a strong effort to ensure that Oregon companies knew about Go Oregon! opportunities. By relying on a few non-Oregon companies (8 percent), agencies launched, and in some cases, completed projects in a timely manner.


**Extent to which minority, women, and emerging small businesses used**

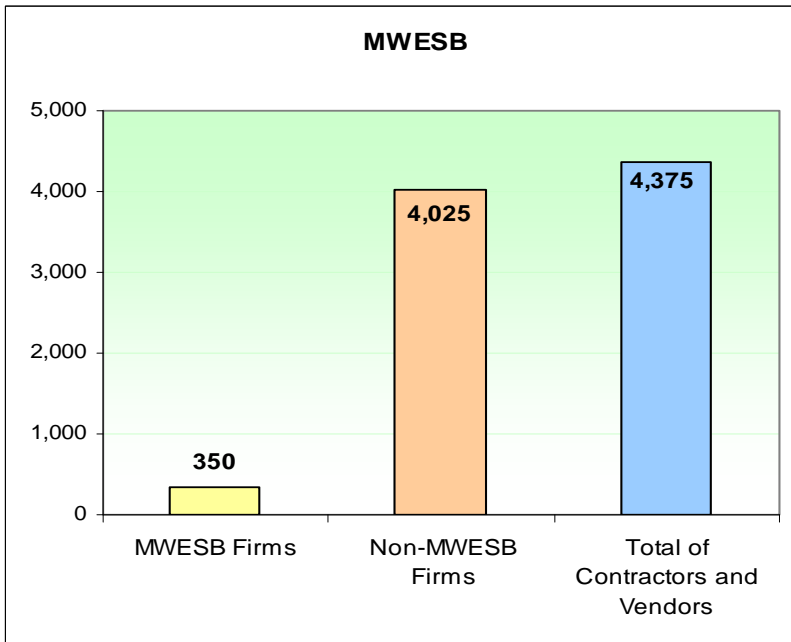

	MWESB Firms	Non-MWESB Firms	Total of Contractors and Vendors
DAS	0	87	87
DOC	0	0	0
ODFW	6	87	93
ODF	6	68	74
OUS	86	897	983
OJD	0	25	25
OMD	21	446	467
OPRD	0	49	49
DSL	4	22	26
ODOT	100	381	481
OYA	2	210	212
CCWD	125	1,753	1,878
<b>Total</b>	<b>350</b>	<b>4,025</b>	<b>4,375</b>

DAS worked closely with the Governor’s advocate for Minority, Women, and Emerging Small Business to promote Go Oregon! project opportunities among the firms registered in Oregon as MWESB.

Savings on energy costs for energy efficiency projects

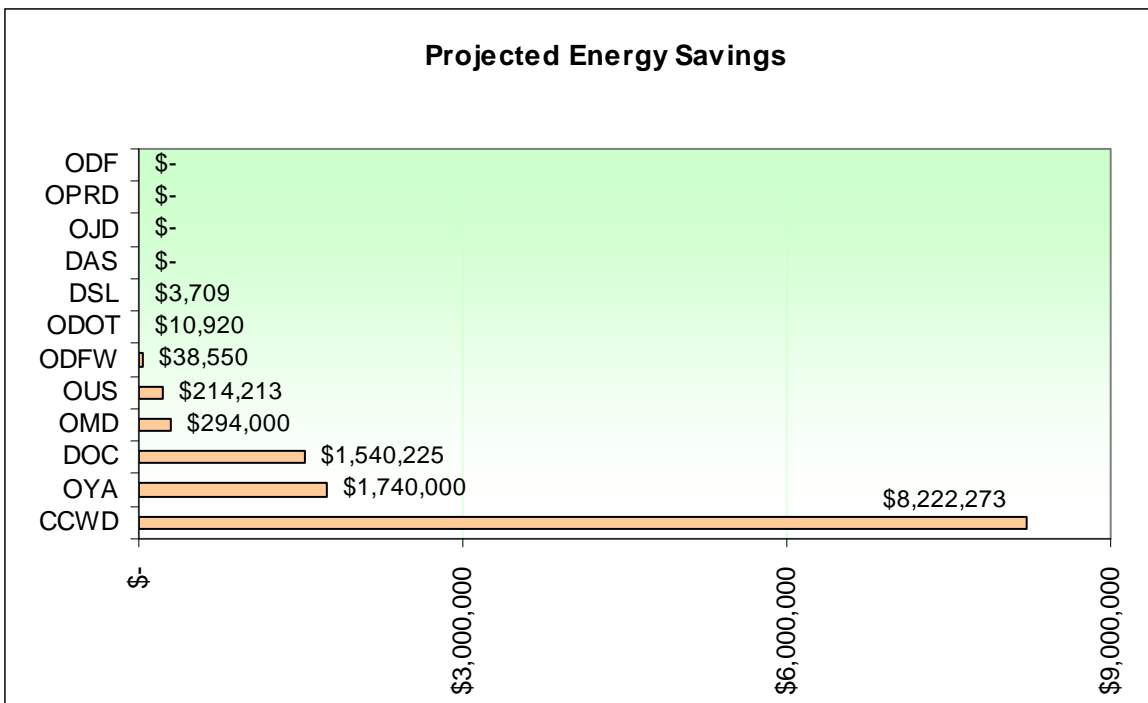


	Savings on Energy Costs for Energy Efficient Projects
CCWD	\$ 8,222,273
OYA	\$ 1,740,000
DOC	\$ 1,540,225
OMD	\$ 294,000
OUS	\$ 214,213
ODFW	\$ 38,550
ODOT	\$ 10,920
DSL	\$ 3,709
DAS	\$ -
OJD	\$ -
OPRD	\$ -
ODF	\$ -
Total	\$12,063,890

“Savings on energy costs for energy efficiency projects” represents reported savings for all agencies performing energy efficiency projects. “Savings” represents estimated energy savings over the life of the project.

Jobs by County


Jobs by County

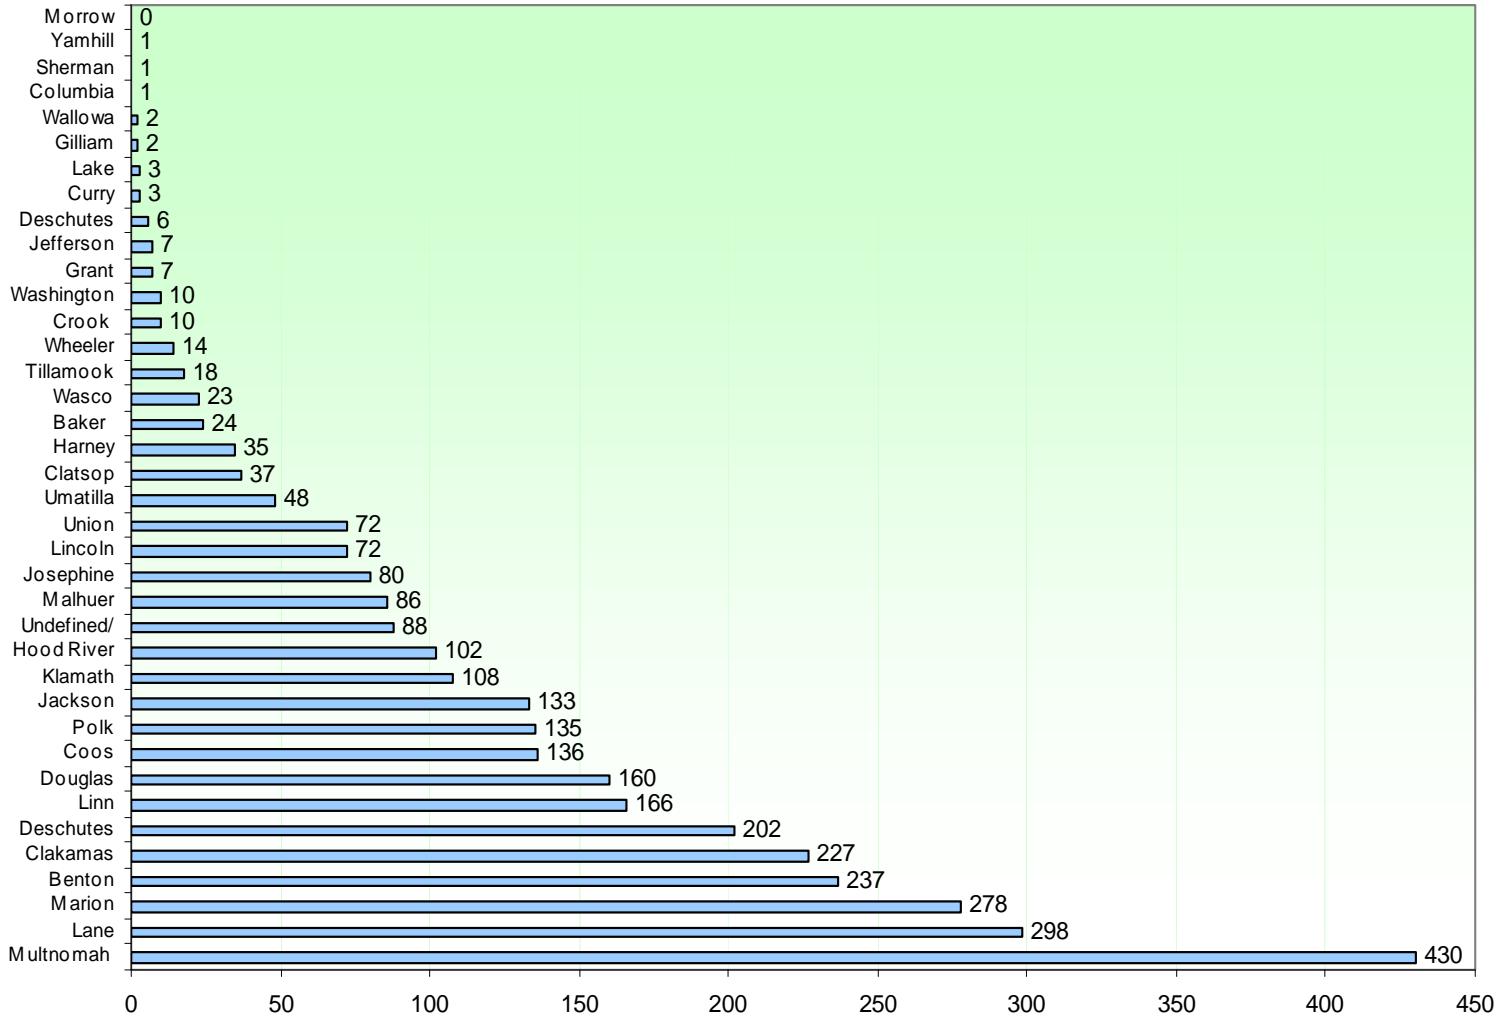

County	Jobs
Multnomah	430
Lane	298
Marion	278
Benton	237
Clackamas	227
Deschutes	202
Linn	166
Douglas	160
Coos	136
Polk	135
Jackson	133
Klamath	108
Hood River	102
Undefined/ Various	88
Malheur	86
Josephine	80
Lincoln	72
Union	72
Umatilla	48
Clatsop	37
Harney	35
Baker	24
Wasco	23
Tillamook	18
Wheeler	14
Crook	10
Washington	10
Grant	7
Jefferson	7
Deschutes & Harney	6
Curry	3
Lake	3
Gilliam	2
Wallowa	2
Columbia	1
Sherman	1
Yamhill	1
Morrow	0
<b>Total</b>	<b>3,262</b>

Expenditures by County

Expenditures by County

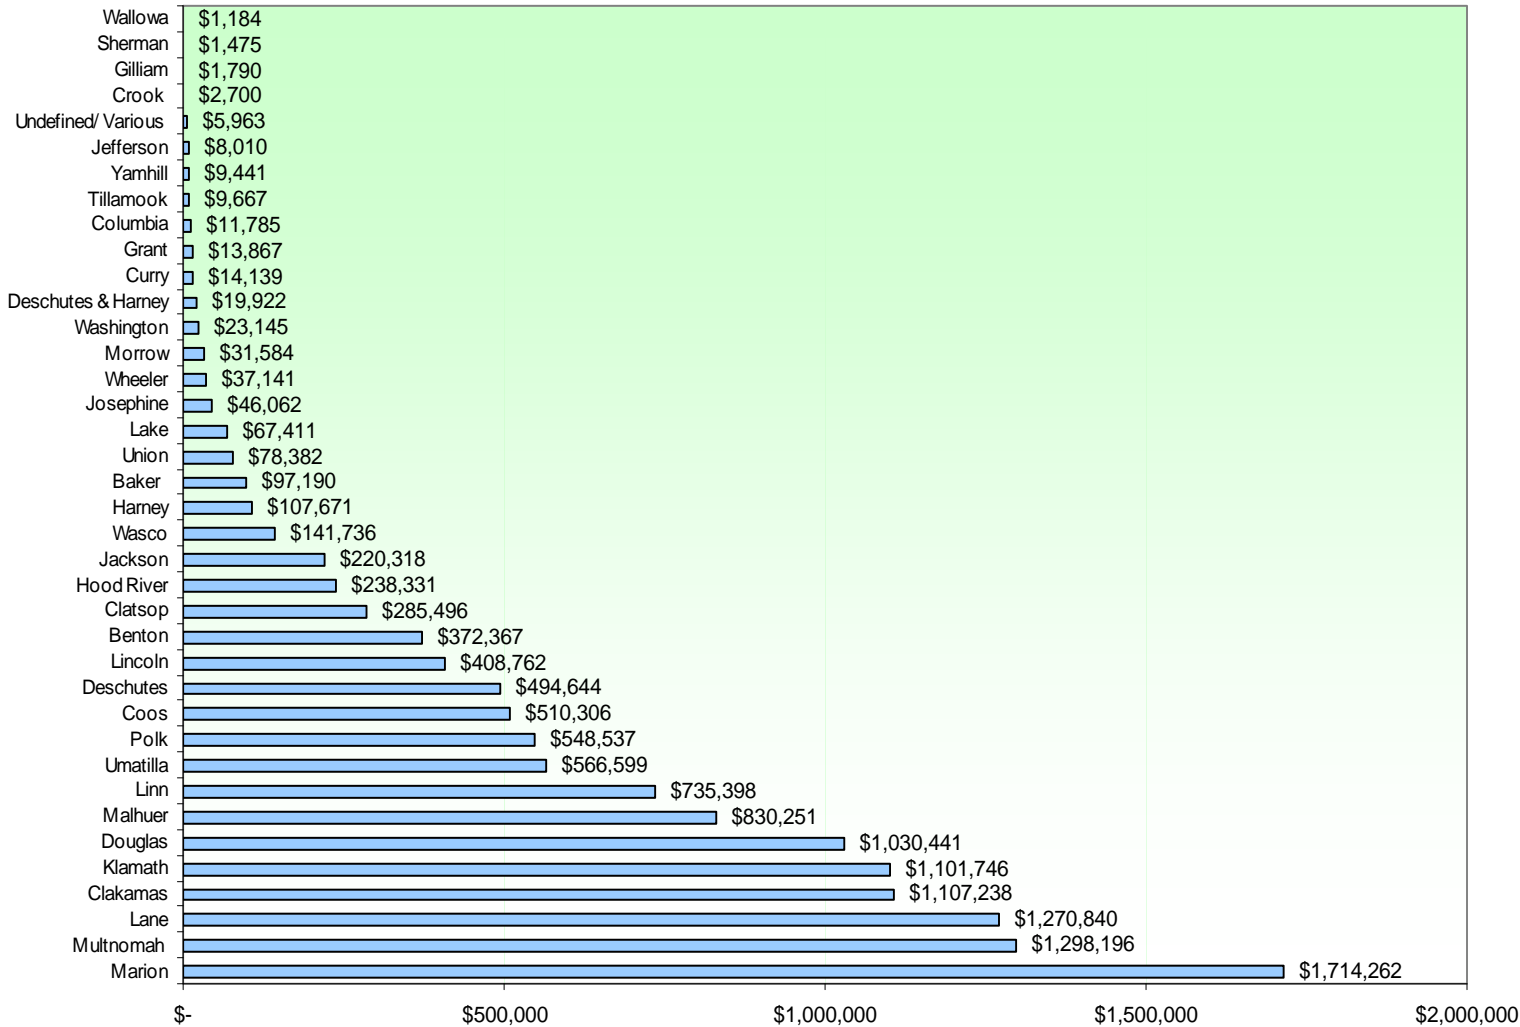

County	Dollars
Marion	\$ 1,714,262
Multnomah	\$ 1,298,196
Lane	\$ 1,270,840
Clakamas	\$ 1,107,238
Klamath	\$ 1,101,746
Douglas	\$ 1,030,441
Malhuer	\$ 830,251
Linn	\$ 735,398
Umatilla	\$ 566,599
Polk	\$ 548,537
Coos	\$ 510,306
Deschutes	\$ 494,644
Lincoln	\$ 408,762
Benton	\$ 372,367
Clatsop	\$ 285,496
Hood River	\$ 238,331
Jackson	\$ 220,318
Wasco	\$ 141,736
Harney	\$ 107,671
Baker	\$ 97,190
Union	\$ 78,382
Lake	\$ 67,411
Josephine	\$ 46,062
Wheeler	\$ 37,141
Morrow	\$ 31,584
Washington	\$ 23,145
Deschutes & Harney	\$ 19,922
Curry	\$ 14,139
Grant	\$ 13,867
Columbia	\$ 11,785
Tillamook	\$ 9,667
Yamhill	\$ 9,441
Jefferson	\$ 8,010
Undefined/ Various	\$ 5,963
Crook	\$ 2,700
Gilliam	\$ 1,790
Sherman	\$ 1,475
Wallowa	\$ 1,184
<b>Total</b>	<b>\$ 13,463,996</b>



## SB 338 Report June 17, 2009



### DAS

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures To Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors hired	MWESB working on a project	Estimated Energy Savings (\$)
1	Central Point Carpet Replacemnet	Jackson	02/20/09		5		04/24/09	74,876	0	6	340	5	4	2	0	N/A
2	UPS Battery Replacement SDC	Marion	02/01/09		5		04/08/09	94,618	0	9	160	9	4	1	0	N/A
3	Carpet Replacement	Umatilla	04/23/09	04/23/09	3	09/15/09		-	0	0	0	0	0	0	0	N/A
4	L&I Bldg. Water Pipe Replacement.	Marion	03/12/09	03/12/09	3	08/15/09		358,524	4	11	3,972	13	36	12	0	N/A
5	Exterior Canopy- Pendleton 202	Umatilla	03/17/09	03/17/09	3	09/01/09		11,631	0	5	0	5	4	0	0	N/A
6	Chiller Replacement - Pendleton 201	Umatilla	03/17/09	03/17/09	3	09/01/09		20,329	0	0	0	0	0	0	0	N/A
7	Unfunded		UF		0			-	0	0	0	0	0	0	0	
8	Unfunded		UF		0			-	0	0	0	0	0	0	0	
9	Painting/Ceiling Tile/Restroom Improv.	Umatilla	03/17/09	03/17/09	3	09/01/09		11,631	0	0	0	0	0	0	0	N/A
10	PSOB Fire System Upgrade - Ph. 2	Multnomah	04/10/09	04/27/09	3	09/30/09		26,840	0	8	0	6	9	3	0	N/A
								598,449	4	39	4,472	38	57	18	0	-

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion  
0) UF / UA  
UF =Unfunded Projects UA = Unassigned Project



## SB 338 Report June 17, 2009



### DOC

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors hired	MWESB working on a project	Estimated Energy Savings (\$)
11	Replace Freezer Lighting at CDC	Marion	05/23/09	05/11/09	3	07/15/09		\$ -	0	0	0	0	0	0	0	N/A
12	Replace expired wireless batteries	Marion, Tillamook	05/23/09		3	11/23/09		\$ -	0	0	0	0	0	0	0	N/A
13	Replace backup electrical system	Umatilla	05/15/09	04/29/09	3	11/15/09		\$ -	0	0	0	0	0	0	0	N/A
14	Install solar system	Umatilla	05/15/09		3	11/15/09		\$ -	0	0	0	0	0	0	0	N/A
15	Replace out of date Security System	Umatilla	06/01/09		1	11/01/09		\$ 121,744	0	0	0	0	0	0	0	N/A
16	Replace failing unit door control sys	Umatilla	06/01/09		1	06/01/10		\$ 97,851	0	0	0	0	0	0	0	N/A
17	Replace warehouse Lighting at CDC	Marion	05/23/09	05/05/09	3	09/23/09		\$ 20,933	0	0	0	0	0	0	0	N/A
18	Electrical panel upgrades	Various	06/01/09		1	01/01/11		\$ -	0	0	0	0	0	0	0	N/A
19	Replace electronic security network	Malhuer	06/01/09	05/13/09	3	10/01/11		\$ 330,827	0	0	0	0	0	0	0	N/A
20	Replace Lighting for energy efficiency	Various	05/15/09	05/14/09	3	10/15/11		\$ -	0	0	0	0	0	0	0	N/A
								\$ 571,355	0	0	0	0	0	0	0	\$ -

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion  
0) UF / UA  
UF =Unfunded Projects UA = Unassigned Project



**SB 338 Report  
June 17, 2009**



**ODFW**

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors hired	MWESB working on a project	Estimated Energy Savings (\$)
21	Sandy Hatchery Parking Lot Const	Clackamas	05/13/09	05/07/09	3	11/13/09		\$ 609	5	0	220	5	11	5	2	N/A
22	Denman Storage Bldg	Jackson	05/05/09	05/08/09	3	11/05/09		\$ 6,510	0	1	0	1	2	0	0	N/A
23	PW Schneider Storage Bldg	Grant	05/12/09		1	11/12/09		\$ -	0	0	0	0	0	0	0	N/A
24	Sauvie Island Storage Bldg	Columbia	04/29/09	05/07/09	3	10/23/09		\$ 11,785	0	1	0	0	0	0	0	N/A
25	Enterprise District Office Elevator	Wallowa	05/12/09		1	01/12/10		\$ -	0	0	0	0	0	0	0	N/A
26	New Bldg at Hatfield Marine Science Ctr	Lincoln	05/28/09		1	02/28/10		\$ -	0	0	0	0	0	0	0	N/A
27	Hatchery Repair Storage Bldg	Linn	05/09/09	04/09/09	3	07/09/09		\$ 3,238	0	1	0	1	3	0	0	N/A
28	McKenzie Hatchery ADA Sidewalk	Lane	04/30/09	04/13/09	5	05/30/09	04/30/09	\$ 8,536	0	5	248	5	15	4	2	N/A
29	Alea Hatchery Domestic Well Building	Benton	04/23/09	04/02/09	3	05/30/09		\$ -	2	4	126	6	2	1	0	N/A
30	EE Wilson Wildlife Area Heat Pump	Benton	04/16/09	04/01/09	5	04/16/09	04/16/09	\$ 6,933	0	2	44	2	5	2	0	\$ 38,550
31	Summer Lake Wildlife Area New Well	Lake	05/14/09	04/20/09	5	08/14/09	04/16/09	\$ 26,849	0	6	173	6	13	0	0	N/A
32	Salmon River Hatchery Heat Pumps	Lincoln	05/14/09	05/01/09	3	07/14/09		\$ -	1	1	23	1	4	0	0	N/A
33	District Office Replace Electric	Benton	05/12/09	05/07/09	3	08/12/09		\$ 19	0	0	0	0	0	0	0	N/A
34	HVAC System Upgrade	Douglas	05/11/09		1	07/11/09		\$ 29	0	0	0	0	0	0	0	N/A
35	Hatchery Electrical Panel Upgrade	Hood River	05/12/09	05/11/09	3	06/19/09		\$ -	0	0	0	0	0	0	1	N/A
36	Electrical Service and Panel Upgrade	Hood River	05/12/09	05/04/09	3	07/12/09		\$ 116	0	2	0	2	1	0	0	N/A
37	Pump Station Electrical Upgrades	Douglas	05/12/09		1	12/12/09		\$ -	0	0	0	0	0	0	0	N/A
38	Hatchery Pond Bottom Resurfacing	Lane	05/12/09	05/07/09	3	06/30/09		\$ -	0	0	0	0	0	0	1	N/A
39	Hatchery Supply Pipeline Replacement	Douglas	04/30/09	05/11/09	3	10/30/09		\$ -	0	0	0	0	0	0	0	N/A
40	Salmon River Hatchery New Residence	Lincoln	05/13/09	05/08/09	3	11/13/09		\$ 137	0	0	0	0	0	0	0	N/A
41	Wildlife Area Residence Replacement	Benton	05/01/09	04/14/09	3	11/05/09		\$ 15,601	29	7	283	32	40	19	0	N/A
42	Foundation Settlement Repair	Clackamas	05/08/09	05/12/09	3	08/12/09		\$ -	0	4	0	4	0	0	0	N/A
43	Hatchery Supply Pipeline Replacement	Clatsop	05/12/09	05/14/09	3	06/19/09		\$ 68	0	3	0	3	1	0	0	N/A
44	Dam Removal Project	Grant	05/22/09		1	05/22/10		\$ 33	0	0	0	0	0	0	0	N/A
								\$ 80,464	37	37	1,117	68	97	31	6	\$ 38,550

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion  
0) UF / UA  
UF =Unfunded Projects UA = Unassigned Project



## SB 338 Report June 17, 2009



### ODF

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
45	Warehouse Columns	Grants Pass	Cancelled		6			\$ -	0	0	0	0	0	0	0	N/A
46	Unfunded		UF		0			\$ -	0	0	0	0	0	0	0	N/A
47	Repair int lighting & service panel Oil Hs	Prineville	04/15/09	05/13/09	3	06/15/09		\$ -	0	0	0	0	0	0	0	N/A
48	Repair interior lighting Whs & Mach Stor	Prineville	04/15/09	05/13/09	3	06/15/09		\$ -	0	0	0	0	0	0	0	N/A
49	Replace vinyl flooring, refinish casewk	Springfield	05/01/09	05/08/09	3	06/15/09		\$ 15,349	0	5	120	5	1	0	0	N/A
50	Replace siding, repaint Storage Shed	Veneta	05/15/09	05/11/09	5	08/15/09	05/29/09	\$ 4,300	0	5	26	5	3	0	0	N/A
51	Unfunded		UF		0			\$ -	0	0	0	0	0	0	0	N/A
52	Replace siding, repaint Woodwork Shop	Veneta	Cancelled		6			\$ -	0	0	0	0	0	0	0	N/A
53	Replace worn carpeting HQ Office	Philomath	04/01/09	04/01/09	3	06/15/09		\$ -	0	0	0	0	0	0	0	N/A
54	Replace worn carpeting Unit Office	Dallas	04/01/09	04/01/09	5	06/01/09	05/15/09	\$ 9,729	0	5	56	5	1	0	0	N/A
55	Replace worn carpeting HQ Office	Toledo	04/01/09	04/01/09	5	06/01/09	05/29/09	\$ 6,300	0	5	60	5	1	0	0	N/A
56	Replace Siding, Repaint Equip. Shed	Veneta	05/11/09		6			\$ -	0	0	0	0	0	0	0	N/A
57	Replace electrical distribution & service	Klamath Falls	05/15/09	05/14/09	3	07/15/09		\$ -	0	0	0	0	0	0	0	N/A
58	Repair soffits at loading dock	Elkton	06/01/09	04/30/09	3	10/01/09		\$ 689	0	2	9	2	1	0	1	N/A
59	Replace siding, repaint ODFW office	Tillamook	06/01/09	05/12/09	3	10/01/09		\$ 765	0	1	17	1	1	0	2	N/A
60	Repaint, replace ceilings	Elkton	06/01/09	04/30/09	3	10/01/09		\$ 2,324	0	2	32	2	1	0	1	N/A
61	Replace siding, repaint Warehouse	Veneta	05/15/09	05/11/09	3	08/15/09		\$ 5,017	0	5	40	5	3	0	0	N/A
62	Replace roof and structural repairs	Elkton	06/01/09	04/30/09	3	12/01/09		\$ 5,596	0	2	76	2	1	0	1	N/A
63	John Day/Sisters Relocation Project	John Day	03/24/09	03/24/09	3	06/01/11		\$ 32,152	0	12	54	12	9	0	1	N/A
								\$ 82,221	0	44	490	44	22	0	6	\$ -

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion  
0) UF / UA  
UF =Unfunded Projects UA = Unassigned Project



**SB 338 Report**  
**June 17, 2009**  
**OUS**



Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
64	Owens Hall Comprhensive Renovation	Klamath	04/23/09	04/15/09	3	09/15/09		\$ 137,765	6	3	0	6	14	13	1	N/A
65	Campus Loop Phase II	Multnomah	02/11/09	02/11/09	3	10/01/10		\$ 148,406	0	15	0	14	17	15	0	\$ 214,113
66	Unassigned				0			\$ -	0	0	0	0	0	0	0	N/A
67	Phys. Ed Building	Polk		04/15/09	3	01/04/11	04/15/09	\$ 3,167	16	1	0	8	0	0	0	N/A
68	Office/Lab Bldg-Rpl Front Entry Door	Jefferson	04/29/09	04/29/09	3	06/29/09		\$ 2,570	0	1	16	0	1	0	1	N/A
69	Lab - Insulate Building	Harney	04/28/09	04/28/09	3	06/28/09		\$ -	0	0	0	0	0	0	0	N/A
70	Office/Lab Building - Replace Gutters	Jefferson	04/30/09	04/30/09	3	06/30/09		\$ 450	0	3	0	3	3	0	1	N/A
71	Baccus Garden Fence				0			\$ -	0	0	0	0	0	0	0	N/A
72	Replace Double Doors - Basement	Hood River	04/24/09	04/24/09	3	06/24/09		\$ -	0	0	0	0	0	0	0	N/A
73	Cold Storage - Replace Gutters	Hood River	04/30/09	04/30/09	3	06/30/09		\$ -	0	0	0	0	0	0	0	N/A
74	Gen Lighting -Lighting/Energy Upgrade	Sherman	05/04/09	05/04/09	3			\$ 1,475	0	1	7	0	1	0	0	N/A
75	Storage Garage				0			\$ -	0	0	0	0	0	0	0	N/A
76	Seafood Reasearch Center - Unfunded				0			\$ -	0	0	0	0	0	0	0	N/A
77	Office Lab Building--Repaint Exterior				0			\$ -	0	0	0	0	0	0	0	N/A
78	Gravel Access Drives--Regravel Drives				0			\$ -	0	0	0	0	0	0	0	N/A
79	Office/Lab Bldg-Repr Work Room Cabinets	Jefferson	04/30/09	04/30/09	3	06/30/09		\$ 4,990	0	3	31	0	4	1	0	N/A
80	Gravel Access Drives--Regravel Drives				0			\$ -	0	0	0	0	0	0	0	N/A
81	Potato Storage Refurb Heating System				0			\$ -	0	0	0	0	0	0	0	N/A
82	Office/Shop Refurbish Heating System				0			\$ -	0	0	0	0	0	0	0	N/A
83	Seafood Research Center Repair Windows				0			\$ -	0	0	0	0	0	0	0	N/A
84	Waste - Refurbish Waste Collection Area	Harney	04/28/09	04/28/09	3	07/12/09		\$ -	0	0	0	0	0	0	0	N/A
85	Gravel Access Drives--Regravel				0			\$ -	0	0	0	0	0	0	0	N/A
86	Truck Scale - Replace Overhead Door	Harney	04/28/09	04/28/09	3	06/28/09		\$ -	0	0	0	0	0	0	0	N/A
87	Truck Scale-Replace Sliding Door	Harney	04/28/09	04/28/09	3	06/28/09		\$ 800	0	2	0	2	0	0	0	N/A
88	HVAC upgrade-CPS	Jackson	04/13/09	04/13/09	3	04/30/09		\$ 10	2	2	59	2	4	2	0	N/A
89	Campus-Add ADA Path to Softball	Polk			5		03/13/09	\$ 6,817	0	8	62	8	2	0	0	N/A
90	SRC - Repair Perchloric Duct/Hood				6			\$ -	0	0	0	0	0	0	0	N/A
91	Door Access Control-classrooms	Jackson	05/18/09	04/27/09	3	06/17/09	05/18/09	\$ 10	0	7	0	6	2	0	0	N/A
92	Fire Alarm System-Art East	Jackson	04/27/09	04/27/09	3	05/27/09		\$ 2,161	0	3	0	3	6	2	0	N/A
93	Fire Alarm System-ECP	Jackson	04/28/09	04/27/09	3	05/28/09		\$ 2,870	0	3	0	3	6	2	0	N/A
94	Access Drives--Add Gravel				0			\$ -	0	0	0	0	0	0	0	N/A
95	Access Drives-Refurbish 8 Cattle Guards	Harney	04/23/09	04/23/09	3	07/12/09		\$ 12,186	2	3	207	0	10	1	3	N/A
96	Hay Barn-Repair Poles				0			\$ -	0	0	0	0	0	0	0	N/A
97	Irrigation Mainline - Refurbish	Harney	04/23/09	04/23/09	3	07/12/09		\$ -	0	0	0	0	0	0	0	N/A

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MMWESB working on a project	Estimated Energy Savings (\$)
98	Lab - Re-Side/Paint Building Exterior	Harney	04/28/09	04/28/09	3	06/28/09		\$ -	0	0	0	0	0	0	0	N/A
99	Door Access Control-Theatre	Jackson	05/18/09	04/27/09	3	06/17/09	05/18/09	\$ 17	0	7	0	6	2	0	0	N/A
100	Variable Frequency Drive	Jackson	04/20/09	04/22/09	3	05/04/09		\$ 17	0	1	0	1	4	2	2	N/A
101	Dipping Vat Building - Refurbish	Harney	04/28/09	04/28/09	3	06/28/09		\$ -	0	0	0	0	0	0	0	N/A
102	Metabolism Barn-Repl Overhead Doors	Harney	04/28/09	04/28/09	3	06/28/09		\$ 1,000	0	2	0	2	0	0	0	N/A
103	Line Fence - Re-Place Line Fence	Hood River	04/30/09	04/30/09	3	06/30/09		\$ 257	0	0	0	0	0	0	0	N/A
104	Rain Gutters	Lincoln	04/01/09	04/01/09	5	04/20/09	04/20/09	\$ 10,846	0	2	92	0	1	0	1	N/A
105	Seafood Research Ctr-Replace Boiler	Clatsop		12/26/08	5	01/05/09	01/05/09	\$ 34,370	0	3	115	3	7	0	0	N/A
106	Seafood Research Ctr-Refinish Ext Siding	Clatsop	04/29/09	04/29/09	3	06/30/09		\$ 8,920	0	2	132	0	3	0	0	N/A
107	Dock - Replace Floats	Lincoln		02/01/09	5	02/28/09	02/15/09	\$ 25,000	0	4	60	4	2	0	0	N/A
108	Corral - Re-Place Corral & Waterers	Harney	04/27/09	04/27/09	3	06/30/09		\$ 7,077	0	0	0	0	0	0	0	N/A
109	Equipment Shed - Re-Roof	Hood River	04/29/09	04/29/09	3	06/30/09		\$ 13,500	1	3	0	0	3	2	0	N/A
110	Door Access Control-Britt	Jackson	05/18/09	04/27/09	3	06/17/09	05/18/09	\$ 27	0	7	0	6	2	0	0	N/A
111	Door Access Library	Jackson	05/18/09	04/27/09	3	06/17/09	05/18/09	\$ 27	0	7	0	6	2	0	0	N/A
112	Fire Alarm System Replacement	Jackson	05/04/09	04/27/09	3	06/03/09		\$ 35	0	5	4	5	8	4	2	N/A
113	Equipment Shed - Reroof	Hood River	04/24/09	04/24/09	3	06/30/09		\$ -	0	0	0	0	0	0	0	N/A
114	Elevator Upgrade-CH	Jackson	04/20/09	04/17/09	3	05/20/09		\$ 24,421	0	7	309	1	6	4	1	N/A
115	Elevator Upgrade-EP	Jackson	05/04/09	04/17/09	3	06/03/09		\$ 30,959	0	7	42	6	10	6	2	N/A
116	Lab - Refurbish HVAC System	Harney	05/13/09	05/13/09	3	07/01/09		\$ 586	0	0	0	0	0	0	0	N/A
117	Refurb Chem Storage/Mixing Area	Hood River	04/29/09	04/29/09	3	06/29/09		\$ -	0	0	0	0	0	0	0	N/A
118	HVAC Upgrade MN	Jackson	06/15/09	04/30/09	3	08/14/09		\$ 50	0	2	0	2	4	2	2	\$ 100
119	Rice-Replace Motors w/ High Eff., VFD	Polk	04/02/09	04/22/09	3	08/31/09		\$ 131	0	5	146	0	1	0	0	N/A
120	Expanded Digital Control	Klamath	03/13/09	04/15/09	3	08/15/09		\$ 39,983	0	4	0	4	2	0	0	N/A
121	Exterior Lighting	Jackson	06/15/09	04/20/09	3	07/30/09		\$ 4,466	0	3	294	0	4	1	0	N/A
122	Exterior Door and Hardware Replacement	Lincoln	02/16/09	02/16/09	3	06/23/09		\$ 6,036	0	5	0	0	1	1	0	N/A
123	Drying Bldg - Refurbish Chem Storage	Harney	05/01/09	05/01/09	3	07/01/09		\$ 1,728	0	0	0	0	0	0	0	N/A
124	Roof replacement-CE	Jackson	06/15/09	04/16/09	3	07/15/09		\$ 4,173	0	6	0	6	2	0	1	N/A
125	Storm Water drainage Improvements	Jackson	06/15/09	04/22/09	3	07/15/09		\$ 100	0	0	0	0	0	0	0	N/A
126	Office - ADA Access & Refurbish Siding	Hood River	04/28/09	04/28/09	3	07/01/09		\$ 6,141	0	2	0	2	0	0	0	N/A
127	Roof Replacement-Music	Jackson	06/15/09	04/30/09	3	07/30/09		\$ 5,323	0	4	0	4	4	1	3	N/A
128	Theatre Roof Replacement	Jackson	06/15/09	04/15/09	3	08/15/09		\$ 7,390	1	8	0	8	3	0	2	N/A
129	Campbell-convert from steam to hydronics	Polk	04/22/09	04/22/09	3	08/31/09		\$ 449	0	0	0	0	1	0	1	N/A
130	Parking lot paving	Lincoln	04/14/09	04/14/09	3	06/15/09		\$ 10,736	0	2	0	0	1	1	0	N/A
131	Extension Office - Refurbish	Hood River	04/24/09	04/24/09	3	06/24/09		\$ 250	0	0	0	0	0	0	0	N/A
132	Learning Resources Ctr: Interior Finishes	Klamath	03/16/09	04/02/09	3	07/01/09		\$ 16,348	0	4	125	4	4	2	2	N/A
133	Fire Alarm System replacement	Jackson	05/04/09	04/27/09	3	06/03/09		\$ 200	0	5	4	5	8	4	2	N/A
134	Classroom Modernization CH	Jackson	06/08/09	04/27/09	3	08/30/09		\$ 2,570	1	6	0	2	3	0	2	N/A
135	Toilet Upgrades-Science Bldg	Jackson	06/15/09	04/30/09	3	08/14/09		\$ 6,150	0	5	0	1	12	6	3	N/A

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MMWESB working on a project	Estimated Energy Savings (\$)
136	Code & Safety Compliance Improvements	Lane	03/25/09	03/25/09	3	11/27/09		\$ 21,160	0	4	153	4	1	0	0	N/A
137	Roof replacement McNeal	Jackson	06/15/09	04/30/09	3	08/14/09		\$ 19,255	0	4	2	4	3	1	1	N/A
138	Replacement Direct Burial 12,000V Elec.	Klamath	04/15/09	04/15/09	3	07/15/09		\$ 133,782	0	12	835	5	15	3	2	N/A
139	Boiler replacement phase 2	Jackson	06/01/09	04/30/09	3	08/30/09		\$ 5,072	0	1	6	1	3	1	0	N/A
140	Seismic Upgrades	Lincoln	04/16/09	04/19/09	3	09/30/09		\$ 7,701	0	5	0	0	1	1	0	N/A
141	Exterior Building Repairs	Lane	06/16/09	04/06/09	3	09/10/09		\$ 95,101	0	12	471	0	11	4	0	N/A
142	Replace plumbing building 900	Lincoln	04/28/09	04/28/09	3	07/01/09		\$ 22,236	0	4	0	0	1	0	0	N/A
143	0143-Renov Labs in Ed Wing-HMSC	Lincoln	04/13/09	04/13/09	3	07/31/09		\$ 10,534	0	1	47	1	3	0	1	N/A
144	Strand Ag 1st Floor SE Bathrooms/Lab	Benton	05/07/09	05/07/09	3	01/01/10		\$ -	0	0	0	0	0	0	0	N/A
145	Gill Coliseum - exterior paint	Benton	12/15/08	12/15/08	3	07/01/09		\$ 84,175	0	89	119	3	10	1	0	N/A
146	AB Acad. Modern. & Access.	Multnomah	02/11/09	02/11/09	3	11/01/09		\$ 105,782	0	13	398	8	25	10	2	N/A
147	Electrical Upgrades and Replacements	Lane	04/06/09	04/13/09	3	11/20/09		\$ 5,634	0	5	13	5	3	0	0	N/A
148	Programmatic Modifications	Lane	04/13/09	04/13/09	3			\$ 1,098	0	2	0	2	0	0	0	N/A
149	Seawater system effluent treatment	Lincoln	04/27/09	04/27/09	3	07/01/09		\$ 54,004	0	11	2	0	3	1	0	N/A
150	Mechanical Upgrades and Replacements	Lane	06/16/09	04/13/09	3	01/31/10		\$ 2,790	0	2	11	2	2	1	0	N/A
151	Pierce Library Roof Repair / Replacement	Union	04/14/09	04/17/09	5	09/15/09		\$ 14,400	0	4	0	0	2	0	0	N/A
152	Roof Replacement, Owens, Semon, Boivin	Klamath	04/03/09	04/03/09	3	07/01/09		\$ 221,623	2	7	132	8	3	0	0	N/A
153	Deferred Interior Finish Replacements	Lane	04/06/09	04/06/09	3	01/31/10		\$ 186,794	1	18	752	19	11	5	0	N/A
154	Dorion Hall Demolition & Site Improvements	Union	04/14/09	04/17/09	3	09/15/09		\$ 1,118	17	7	8	1	2	0	0	N/A
155	Academic Modernization	Klamath	04/15/09		3			\$ 69,705	0	12	0	0	12	12	0	N/A
156	NH Acad Modernization and Accessibility	Multnomah	03/31/09	03/31/09	3	10/31/09		\$ 37,168	0	18	0	17	17	5	3	N/A
157	CH Classroom Upgrades	Multnomah	04/01/09	04/01/09	3	10/31/09		\$ 177,420	1	19	0	18	14	4	2	N/A
158	Campus-Steamline Phase II	Polk	04/20/09	04/20/09	3	09/15/09		\$ 35,119	0	7	191	7	11	0	2	N/A
159	LH Academic & Program Improvements	Multnomah	03/30/09	03/23/09	3	10/31/10		\$ 2,716	2	14	34	14	24	12	3	N/A
160	Strand Ag-Bldg repipe/upgrade plumbing	Benton	05/07/09	05/07/09	3	01/01/10		\$ 32,072	0	3	0	0	4	4	1	N/A
161	Waldo Hall - 4th floor renovation	Benton	03/25/09	03/25/09	3	01/01/10		\$ 1,572	0	0	0	0	0	0	0	N/A
162	Campus Roof Repair and Replacement	Multnomah	04/01/09	03/30/09	3	11/30/09		\$ 244,545	0	50	978	17	31	12	3	N/A
163	E&G Bldg. Code, Life Safety Improvements	Multnomah	04/01/09	04/01/09	3	10/31/09		\$ 81,395	0	31	290	16	53	28	28	N/A
164	Reed Hall-Sys Upgrades & Renov	Benton	02/26/09	02/26/09	3	10/01/09		\$ 26,109	1	24	254	25	1	0	2	N/A
165	Heckart Hall-Sys Upgrades & Renov	Benton	12/31/08	12/31/08	3	04/01/10		\$ 205,887	1	75	1,118	72	1	0	1	N/A
166	Science Building 2 Modernization	Multnomah	03/01/08	03/26/08	3	04/01/10		\$ 17,691	2	8	28	8	12	2	2	N/A
167	Health & Wellness Center	Polk	02/24/09	04/15/09	3	01/04/11	04/15/09	\$ 87,696	38	13	407	29	9	2	1	N/A
168	Classroom, Office Bldg	Polk	02/24/09	04/15/09	3	01/04/11	04/15/09	\$ 68,644	13	10	288	5	7	2	1	N/A
								\$ 2,672,956	107	658	8,242	424	465	182	86	\$ 214,213

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion  
0) UF / UA  
UF =Unfunded Projects UA = Unassigned Project



**SB 338 Report**  
**June 17, 2009**



**OJD**

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
169	Supreme Court Re-Roofing Project	Marion	04/24/09	04/27/09	3	08/01/09		\$ 1,936	0	18	958	18	17	4	0	N/A

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion  
 0) UF / UA  
 UF =Unfunded Projects UA = Unassigned Project



## SB 338 Report June 17, 2009



### OMD

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
170	Hillsboro Armory Storage Building	Washington	05/01/09	04/29/09	3	06/26/09		\$ -	0	7	140	7	19	10	1	N/A
171	Roseburg Armory Floor Replacement	Douglas	04/21/09	04/23/09	4	06/14/09		\$ 10,257	3	6	123	6	1	1	2	N/A
172	Hermiston HVAC For Drill Floor	Umatilla	05/04/09	04/27/09	3	06/22/09		\$ 29,308	0	6	18	6	4	2	0	N/A
173	COUTES - Restroom Remodel	Deschutes	05/01/09	04/30/09	3	08/02/09		\$ 19,269	4	4	1,008	7	14	10	7	N/A
174	LaGrande Armory Back Up Generator	Union	05/01/09	04/30/09	3	07/10/09		\$ 40,114	2	20	120	20	12	6	0	N/A
175	Bend Armory Back Up Generator	Deschutes	05/01/09	04/20/09	2	07/17/09		\$ -	0	43	7	43	15	6	0	N/A
176	Camp Withycombe Bld.6101 Reroof	Clackamas	04/27/09	04/27/09	3	08/01/09		\$ 258,112	0	14	0	12	10	3	0	N/A
177	Salem Armory Floor Tile Replacement	Marion	04/28/09	04/27/09	3	06/22/09		\$ 5,979	7	12	0	12	4	2	0	N/A
178	Jackson Armory Door Replacement	Multnomah	04/13/09	04/13/09	3	06/05/09		\$ 32,546	0	20	117	9	20	6	4	\$ 30,000
179	Camp Rilea Replace Roofing & Siding	Clatsop	05/04/09	04/21/09	3	08/14/09		\$ 3,120	0	1	120	1	9	4	0	\$ 25,000
180	Hood River Armory Storage Building	Hood River	05/01/09	04/20/09	3	08/29/09		\$ 192,811	0	15	336	6	20	12	0	\$ 45,000
181	Armory Parking Lot Upgrade	Josephine	05/01/09	04/30/09	3	06/22/09		\$ 5,043	0	20	31	15	10	4	0	N/A
182	Kleiver Armory Parking Lot Upgrade	Multnomah	05/01/09	04/29/09	3	07/29/09		\$ 5,033	0	14	191	12	4	2	2	N/A
183	Armory Compound Improvem'ts	Hood River	05/01/09	04/30/09	3	06/29/09		\$ 2,419	0	17	0	16	9	3	1	N/A
184	Hood River Armory Interior Remodel	Hood River	05/01/09	04/30/09	3	10/29/09		\$ 17,068	14	46	355	36	76	28	4	N/A
185	Blak Restroom & Shower Facility	Crook	05/01/09	05/01/09	3	10/28/09		\$ 2,700	7	3	250	6	25	14	0	N/A
186	Coos Bay Armory - Interior Remodel	Coos	05/01/09	05/01/09	3	07/29/09		\$ 24,144	0	11	151	11	29	20	0	\$ 50,000
187	Prineville CORC - Interior Remodel	Crook	06/01/09		1			\$ -	0	0	0	0	0	0	0	\$ 144,000
								\$ 647,923	37	259	2,967	225	281	133	21	\$ 294,000

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion 0) UF / UA  
UF =Unfunded Projects UA = Unassigned Project



**SB 338 Report  
June 17, 2009**



**OPRD**

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
188	Beverly Beach S.P. Playground	Lincoln	01/30/09	01/01/09	5	05/20/09	05/29/09	\$ 29,932	0	6	156	6	6	0	0	N/A
189	Tumalo State Park Playground	Deschutes	04/30/09		5		04/17/09	\$ 21,760	0	15	16	9	6	4	0	N/A
190	Arizona Beach SP Restroom	Curry	04/30/09	02/05/09	3	05/31/09		\$ -	0	18	163	2	2	0	0	N/A
191	Carl Washburn SP Paving	Lane	04/06/09		5		04/28/09	\$ 145,172	0	10	750	10	3	3	0	N/A
192	Bullards Beach SP Paving	Coos	04/30/09	02/05/09	5	05/15/09	05/28/09	\$ 159,140	0	10	815	10	2	2	0	N/A
193	Wallowa Lake SP Docks	Wallowa	04/30/09	02/05/09	3	06/30/09		\$ 1,184	0	2	600	2	0	0	0	N/A
194	Sarah Helmick SP Paving	Polk	04/30/09	02/05/09	5	05/15/09	05/22/09	\$ 140,794	0	8	700	8	2	2	0	N/A
195	Champoeg SP Restroom	Marion	04/06/09	01/02/09	5	05/31/09	05/21/09	\$ 356,041	0	76	900	25	5	0	0	N/A
								\$ 854,023	0	145	4,100	72	26	11	0	\$ -

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion  
0) UF / UA  
UF =Unfunded Projects UA = Unassigned Project



**SB 338 Report  
June 17, 2009**



**DSL**

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
196	fence removal	Deschutes	4/10/09		5		4/11/09	\$ 9,600	0	3	0	3	0	0	0	N/A
197	juniper removal	Deschutes/Harney	4/8/09	4/2/09	3	10/31/09		\$ 19,922	2	4	0	5	4	0	0	N/A
198	Portland Harbor Boundary Survey	Multnomah	6/1/09		1	6/1/10		\$ -	0	10	0	10	0	0	0	N/A
199	Chiller Replacement	Marion	3/19/09	4/24/09	3	6/30/09		\$ 160,123	0	5	0	5	9	4	4	\$ 3,709
								\$ 189,645	2	22	0	23	13	4	4	\$ 3,709

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion  
0) UF / UA  
UF =Unfunded Projects UA = Unassigned Project



## SB 338 Report June 17, 2009



### ODOT

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
200	93rd SE Yamhill Air Monitor Station Door	Multnomah			0			\$ -	0	0	0	0	0	0	0	N/A
201	Salem Building U Replace OH Door	Marion			0			\$ -	0	0	0	0	0	0	0	N/A
202	Santiam River SB Replace Locks	Marion			5	03/30/09		\$ 359	0	1	8	1	0	0	1	N/A
203	Sweet Home MS Roof Moss Treatment	Linn			0			\$ -	0	0	0	0	0	0	0	N/A
204	Soda Mt. MW Bldg Seal Roof Vents/Elec	Jackson			0			\$ -	0	0	0	0	0	0	0	N/A
205	Reedsport MS Replace Shingles, Door	Douglas			6			\$ -	0	0	0	0	0	0	0	N/A
206	Baker City OSP Office Exterior Repairs	Baker			0			\$ -	0	0	0	0	0	0	0	N/A
207	Humburg MS Install Elect Outlets	Clatsop			5	03/06/09		\$ 1,207	0	1	10	1	1	0	0	N/A
208	SRA Replace Door and Gutter	Baker	03/31/09	03/31/09	5	05/22/09	05/22/09	\$ 3,465	0	0	0	0	0	0	0	N/A
209	Moro MS Deferred Maintenance	Sherman			0			\$ -	0	0	0	0	0	0	0	N/A
210	Corvallis MS Replace Window Panes	Benton			0			\$ -	0	0	0	0	0	0	0	N/A
211	Rocky Point Scale Misc Repairs	Multnomah			0			\$ -	0	0	0	0	0	0	0	N/A
212	Seaside MS Replace O/H Dorr Panels	Clatsop	04/27/09	05/01/09	3	06/15/09		\$ -	0	0	0	0	0	0	0	N/A
213	District 13 Office Secure Crawl Space	Union			0			\$ -	0	0	0	0	0	0	0	N/A
214	Elgin MS Bldg Replace Flooring	Union	05/01/09	05/01/09	3	06/05/09		\$ -	0	0	0	0	0	0	0	N/A
215	Manning MS Stor C Doors	Washington			0			\$ -	0	0	0	0	0	0	0	N/A
216	Baker City MS Repair Roof	Baker			0			\$ -	0	0	0	0	0	0	0	N/A
217	Condon MS Replace Garage Door	Gilliam	04/15/09		5	04/17/09		\$ 1,790	0	2	6	2	3	1	0	N/A
218	Salem MS Replace Window Flooring	Marion	05/01/09	05/01/09	3	07/20/09		\$ -	0	0	0	0	0	0	0	N/A
219	Astoria DMV Repair Roof Damage	Clatsop			0			\$ -	0	0	0	0	0	0	0	N/A
220	C. Reynolds Repair Water Line/Boring	Union			0			\$ -	0	0	0	0	0	0	0	N/A
221	Fall River Scoop Shed Metal Siding	Deschutes			0			\$ -	0	0	0	0	0	0	0	N/A
222	Farewell Bend POE Repair Siding	Malheur			0			\$ -	0	0	0	0	0	0	0	N/A
223	I5-228 Sand Shed Siding Repairs	Linn	04/01/09		5	04/10/09		\$ 1,506	0	1	32	1	2	0	0	N/A
224	Salem Signal Bldg Replace Carpet	Marion	05/01/09	05/01/09	3	06/15/09		\$ -	0	0	0	0	0	0	0	N/A
225	Walterville Scale Gutters Paneling ADA	Lane	04/06/09		5	04/24/09		\$ 2,311	1	1	40	0	0	0	0	N/A
226	Sisters Scale Hs Window/Roof	Deschutes			5	03/18/09		\$ 1,108	0	1	9	1	4	0	1	N/A
227	Baker City Scale House Replace Roof	Baker	03/20/09		5	04/14/09		\$ 4,813	1	5	48	4	3	1	0	N/A
228	McMinnville MS Replace N Window	Yamhill	04/13/09	04/13/09	5	06/01/09	05/29/09	\$ 8,786	0	1	47	1	2	0	1	N/A
229	Woodburn POE Deferred Maintenance	Marion	04/20/09		5	04/18/09		\$ 6,270	0	5	64	5	6	5	0	N/A
230	Brothers Oasis SRA Replace Shelters	Deschutes	04/07/09		5	05/01/09		\$ 10,221	0	3	114	2	6	1	0	N/A
231	Chas Reynolds SRA Deferred Maint	Union	04/18/09		5	04/28/09		\$ 3,792	3	1	86	4	1	0	0	N/A

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
232	Noti Scale House ADA Ele Gutters	Lane	03/30/09		5		04/02/09	\$ 2,141	0	4	41	4	6	2	0	N/A
233	Cave Jct MS Replace Windows	Josephine	03/23/09		5		04/16/09	\$ 5,054	0	2	30	2	3	0	0	N/A
234	District 10 Office Replace Windows	Deschutes	04/20/09	04/20/09	5	05/22/09	06/01/09	\$ 49,600	1	2	288	3	3	0	0	N/A
235	Lagrande DMV Deferred Maint	Union	05/01/09	05/01/09	4	05/29/09		\$ 275	0	1	0	1	1	0	1	N/A
236	Wolf Creek Storage Replace Floor	Douglas			0			\$ -	0	0	0	0	0	0	0	N/A
237	Sand Shed Replace Broken Joists	Klamath			0			\$ -	0	0	0	0	0	0	0	N/A
238	Salem Bldg Q Replace OH Doors	Marion	04/13/09	05/01/09	5	05/13/09	05/01/09	\$ 5,920	0	3	16	3	1	0	0	N/A
239	Weatherby SRA Replace Roof	Baker			5		03/27/09	\$ 10,688	3	2	63	5	4	1	5	N/A
240	Sandy MS Deferred Maintenance	Clackamas			0			\$ -	0	0	0	0	0	0	1	N/A
241	Pendleton MS Deferred Maintenance	Umatilla	04/20/09	04/30/09	5	04/30/09	05/24/09	\$ 9,200	0	4	130	4	3	0	1	N/A
242	Woodburn MS Deferred Maintenance	Marion	04/06/09	04/06/09	5	04/20/09	05/08/09	\$ 1,480	1	1	16	2	2	0	2	N/A
243	Richland Shed Replace OH Doors	Baker			6			\$ -	0	0	0	0	0	0	0	N/A
244	Rose Lodge MS RR Vinyl Walls	Lincoln			5		03/18/09	\$ 2,297	0	2	12	2	2	1	2	N/A
245	Spray Sand Shed Interior Repairs	Wheeler			0			\$ -	0	0	0	0	0	0	0	N/A
246	Coaledo Scale House Roof & Siding	Coos	04/01/09		5		04/14/09	\$ 1,870	0	2	13	2	2	0	1	N/A
247	Tillamook DMV Deferred Maintenance	Tillamook			5		03/19/09	\$ 3,420	0	3	16	3	5	2	4	N/A
248	Myrtle Point Scale Roof Siding Floor	Coos			5		03/13/09	\$ 6,978	0	4	90	4	5	2	4	N/A
249	Ashland Scale House Siding	Jackson			5		04/01/09	\$ 7,581	0	2	60	2	3	0	2	N/A
250	Suncrest SRA Replace Elec Boxes	Jackson			0			\$ -	0	0	0	0	0	0	3	N/A
251	Troutdale MS Deferred Maintenance	Multnomah	03/31/09		5		04/30/09	\$ 3,423	1	1	19	2	1	0	1	N/A
252	Gateway OSP Bldg Misc Repairs	Lane			0			\$ -	0	0	0	0	0	0	0	N/A
253	e. Portland Illuminate Gateway	Multnomah			0			\$ -	0	0	0	0	0	0	0	N/A
254	Memaloose SRA Deferred Maintenance	Wasco	04/16/09		5		04/16/09	\$ 7,616	0	2	16	2	1	0	0	N/A
255	Canyonville MS Stormwater System	Douglas	04/01/09		5		04/21/09	\$ 5,610	0	2	15	2	4	2	1	N/A
256	Ona Beach MS Deferred Maintenance	Lincoln	04/06/09		5		05/01/09	\$ 5,984	0	6	24	6	2	0	1	N/A
257	Reg 1 Bldg Replace Carpet	Multnomah	04/16/09	04/30/09	5	05/22/09	05/15/09	\$ 18,055	0	8	48	8	3	1	0	N/A
258	Stanfield SRA Deferred Maintenance	Umatilla			5		03/30/09	\$ 9,297	0	1	0	1	2	0	1	N/A
259	Glenwood MS Electrical Changes	Lane			0			\$ -	0	0	0	0	0	0	0	N/A
260	Hermiston MS Replace Fencing	Umatilla	04/07/09		5		04/30/09	\$ 10,780	1	2	72	3	0	0	0	N/A
261	LaGrande Sand Shed Misc Repairs	Union	04/17/09	04/17/09	5	04/30/09	05/08/09	\$ 11,484	1	3	145	4	3	1	1	N/A
262	Stanton Blvd Sand Shed Deferred Maint	Baker			0			\$ -	0	0	0	0	0	0	2	N/A
263	LaGrande MS Storage - replace roof	Union	05/01/09	05/04/09	5	05/08/09	05/11/09	\$ 2,750	0	5	20	5	2	0	0	N/A
264	Mitchell MS Covered Timber Storage	Wheeler	04/28/09	04/28/09	5	05/04/09	05/14/09	\$ 22,857	2	8	388	3	1	1	0	N/A
265	Estacada MS Deferred Maintenance	Clackamas	03/23/09		5		04/21/09	\$ 9,900	2	1	134	3	3	1	0	N/A
266	Coos Bay DMV Deferred Maintenance	Coos	04/01/09		5		04/23/09	\$ 28,977	0	12	139	12	7	2	0	N/A
267	Barlow School Deferred Maintenance	Multnomah	04/03/09	04/03/09	5	05/15/09	05/15/09	\$ 13,080	0	7	181	7	3	0	1	N/A
268	Ashland MS Replace Carpet	Jackson	03/16/09		5		03/20/09	\$ 5,293	0	7	32	7	2	0	0	N/A
269	East Portland MS Decant Cover	Multnomah			0			\$ -	0	0	0	0	0	0	0	N/A

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
270	Hunter Cr MS Replace Water Line	Curry			5		03/20/09	\$ 14,139	0	3	40	3	4	2	2	N/A
271	North Portland MS Decant Cover	Multnomah	04/15/09	04/15/09	5	04/30/09	05/15/09	\$ 19,946	2	3	240	5	5	0	2	N/A
272	Salem Building E Repair Roof	Marion			5		03/16/09	\$ 15,000	0	8	152	8	4	2	0	N/A
273	Shaniko MS Shop Repair/Replace OH	Wasco			0			\$ -	0	0	0	0	0	0	0	N/A
274	Distict 12 Office Deferred Maintenance	Umatilla	04/06/09	04/02/09	4	05/15/09		\$ 12,125	0	0	0	0	0	0	0	N/A
275	Spray MS Deferred Maintenance	Wheeler	04/23/09	04/19/09	5	05/04/09	05/08/09	\$ 14,284	1	3	64	4	2	0	1	N/A
276	Glide Scale Deferred Maintenance	Douglas	03/26/09		5		03/23/09	\$ 13,780	0	2	200	2	8	4	1	N/A
277	C locks Sand Shed Replace Metal	Hood River	03/16/09		5		03/16/09	\$ 5,769	0	2	41	2	1	0	0	N/A
278	Coos Bay Br. Bldg Replace Roof	Coos	04/30/09	04/13/09	5	05/08/09	05/05/09	\$ 10,019	0	4	70	4	3	0	0	N/A
279	Coos Bay Sign Stor Replace Roof	Coos	04/13/09	04/13/09	5	05/08/09	05/05/09	\$ 10,019	0	4	70	4	3	0	0	N/A
280	Richland MS Shop Replace Roof	Baker	03/17/09	03/20/09	5	05/17/09	05/11/09	\$ 32,994	3	6	282	3	5	0	1	N/A
281	Gettings Cr Deferred Maintenance	Lane	04/27/09	04/29/09	3	06/18/09		\$ -	0	0	0	0	0	0	1	N/A
282	Baldock SRA Replace Roof	Clackamas			5		03/19/09	\$ 13,212	0	5	150	5	3	1	0	N/A
283	Silver Lake MS Deferred Maintenance	Lake			5		03/17/09	\$ 8,079	0	3	22	3	3	1	1	N/A
284	Grand Rhond Stor OH Door Window	Polk			5		04/06/09	\$ 3,697	0	3	16	3	2	1	3	N/A
285	Reith Stockpile - install security fence	Umatilla	04/22/09		5		04/30/09	\$ 12,000	0	1	50	1	5	0	1	N/A
286	Ashland POE Deferred Maintenance	Jackson			5		03/25/09	\$ 8,971	0	10	60	10	6	4	10	N/A
287	Bend MS Sand Shed Replace Roof	Deschutes	04/20/09	04/20/09	4	05/20/09		\$ -	0	0	0	0	1	1	1	N/A
288	C. Point MS Upgrade Water Line	Jackson			5		03/20/09	\$ 9,365	0	5	143	4	11	5	3	N/A
289	Austin MS Deferred Maintenance	Grant	04/29/09	05/01/09	5	05/08/09	05/10/09	\$ 13,834	1	6	162	3	6	4	1	N/A
290	Juntura MS Deferred Maintenance	Harney	03/20/09		5		04/13/09	\$ 14,772	2	0	277	1	6	2	2	N/A
291	Jantzen Shop Bldg Deferred Maint	Multnomah			0			\$ -	0	0	0	0	0	0	1	N/A
292	Klamath Falls MS Deferred Maintenance	Klamath			0			\$ -	0	0	0	0	0	0	0	N/A
293	Lapine MS Replace Doors/Floor	Deschutes	03/18/09		5		05/01/09	\$ 49,983	1	11	384	12	4	2	1	N/A
294	Burns MS Deferred Maintenance	Harney	04/22/09	04/30/09	5	05/01/09	05/06/09	\$ 3,745	0	2	32	2	2	1	1	N/A
295	Salem Dock Bldg F Roof	Marion	03/23/09		5		04/22/09	\$ 40,376	0	5	557	5	0	0	6	N/A
296	Seneca MS Shop Replace Doors	Grant			6			\$ -	0	0	0	0	0	0	1	N/A
297	Dist 14 Office Deffered Maintenance	Malheur			0			\$ -	0	0	0	0	0	0	1	N/A
298	Basque MS Deferred Maintenance	Malheur	03/31/09		5		04/13/09	\$ 12,117	0	4	185	2	4	2	1	N/A
299	Lawnfield Bldg Seal Roof/Gutters	Clackamas			0			\$ -	0	0	0	0	0	0	1	N/A
300	Coquille Deferred Maintenance	Coos	04/01/09		5		04/21/09	\$ 19,721	0	10	200	10	9	4	2	N/A
301	Maples SRA ADA Upgrades	Marion	04/13/09	04/13/09	4	05/22/09		\$ -	0	0	0	0	0	0	0	N/A
302	R5 Bldg Deferred Maintenance	Union	04/30/09	05/01/09	3	06/30/09		\$ -	0	0	0	0	0	0	0	N/A
303	Stinking Water Sand Roof and Repairs	Harney	04/15/09	04/06/09	5	05/01/09	05/03/09	\$ 27,856	1	6	372	3	4	2	2	N/A
304	Bend Bldg J Deferred Maintenance	Deschutes	04/24/09	04/24/09	4	05/15/09		\$ 12,870	0	5	94	5	3	1	1	N/A
305	Baldock MS Deferred Maintenance	Washington	03/30/09	03/30/09	5	04/30/09	05/06/09	\$ 23,145	0	3	172	3	2	1	1	N/A
306	Sisters MS Shop OH Doors	Deschutes			0			\$ -	0	0	0	0	1	1	1	N/A
307	Bachelor Butte Sand Shed Repl Roof	Deschutes	05/01/09	05/01/09	4	05/26/09		\$ -	0	0	0	0	5	5	0	N/A

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
308	Florance MS Deferred Maintenance	Lane	03/18/09		5		04/07/09	\$ 8,472	1	1	131	2	1	0	1	N/A
309	Alkali Lake Deferred Maintenance	Harney	4/31/09	04/17/09	5	05/22/09	05/19/09	\$ 36,132	3	7	534	10	11	1	1	N/A
310	Lakeview MS Deferred Maintenance	Lake	04/16/09	04/16/09	4	05/30/09		\$ 32,483	0	0	0	0	3	3	0	N/A
311	Boardman Deferred Maintenance	Morrow	04/06/09	04/24/09	4	05/29/09		\$ 31,584	0	0	0	0	0	0	2	N/A
312	Bend Shop Roof/OH Doors	Deschutes	04/15/09		5		04/29/09	\$ 28,694	6	3	144	9	5	3	2	N/A
313	Ontario MS Repair Water Filter System	Malheur	03/31/09	04/24/09	5	05/13/09	05/13/09	\$ 35,835	2	2	416	4	0	0	1	N/A
314	Ukiah Sand Shed Replace Roof	Umatilla			0			\$ -	0	0	0	0	2	2	0	N/A
315	Milwaukie Stone Bldg Replace Roof	Clackamas	04/06/09		5		04/29/09	\$ 46,554	7	4	1,093	7	5	2	0	N/A
316	The Dalles MS Deferred Maintenance	Wasco	04/03/09	04/03/09	5	05/05/09	05/05/09	\$ 51,145	0	4	261	4	4	0	0	N/A
317	Oak Grove SRA Deferred Maintenance	Linn	04/27/09	04/27/09	5	06/11/09		\$ 53,967	0	11	284	11	8	0	0	N/A
318	Port Orford MS Deferred Maintenance	Curry	04/27/09	04/27/09	4	05/31/09		\$ -	0	0	0	0	0	0	1	N/A
319	Boswell Spgs Deferred Maintenance	Douglas	03/31/09		5		04/25/09	\$ 60,965	2	0	291	2	7	0	0	N/A
320	Davis Slough Deferred Maintenance	Coos	05/01/09	05/01/09	3	07/30/09		\$ -	0	0	0	0	0	0	1	N/A
321	Baker City Sand Shed Roof & Siding	Baker	04/15/09	04/17/09	5	04/30/09	05/15/09	\$ 45,231	0	4	319	4	1	0	1	N/A
322	S. Umpqua SRA Deferred Maintenance	Douglas	10/01/09		1			\$ -	0	0	0	0	0	0	0	N/A
323	Cow Creek SRA Deferred Maintenance	Douglas	10/01/09		1			\$ -	0	0	0	0	0	0	0	N/A
324	Brothers MS Deferred Maintenance	Deschutes	05/01/09	05/01/09	3	06/01/09		\$ -	0	0	0	0	0	0	0	N/A
325	Central Point MS Deferred Maintenance	Jackson	04/30/09	04/30/09	3	05/22/09		\$ -	0	0	0	0	0	0	0	N/A
326	Warrenton MS Deferred Maintenance	Clatsop	04/06/09	04/06/09	5	06/01/09	05/15/09	\$ 39,841	0	5	510	0	3	0	0	N/A
327	Chemult MS Deferred Maintenance	Klamath	05/01/09	04/29/09	3	06/12/09		\$ -	0	0	0	0	0	0	0	N/A
328	Region 3 Bldg Deferred Maintenance	Douglas	04/06/09	04/16/09	4	05/29/09		\$ 62,828	0	3	134	3	1	0	1	N/A
329	Cabin Cr SRA Deferred Maintenance	Douglas	04/27/09	04/29/09	3	08/18/09		\$ -	0	0	0	0	0	0	0	N/A
330	Shady MS Deferred Maintenance	Douglas	04/27/09	04/27/09	4	05/26/09		\$ -	0	0	0	0	0	0	0	N/A
331	LaGrande Shop Deferred Maintenance	Union	05/01/09	05/01/09	3	06/30/09		\$ -	0	0	0	0	0	0	1	N/A
332	Manzanita SRA Deferred Maintenance	Josephine	04/13/09	04/13/09	3	06/26/09		\$ 34,269	0	10	300	10	4	1	1	N/A
333	Rail Station	Marion	04/15/09		5		04/29/09	\$ 24,496	0	1	25	1	2	0	0	\$ 10,920
								\$ 1,321,550	49	288	10,948	298	271	82	100	\$ 10,920

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion  
0) UF / UA  
UF =Unfunded Projects UA = Unassigned Project



## SB 338 Report June 17, 2009



### OYA

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
334	Agency Wide Central Control	Clatsop	05/01/09	02/09/09	3	11/30/09		\$ 1,307	2	1	0	3	0	0	0	N/A
335	Agency-wide Central Control Renovation	Linn	05/01/09	02/09/09	3	11/30/09		\$ 1,258	2	9	0	9	1	1	0	N/A
336	Agency-wide Central Control Renovation	Union	05/01/09	02/09/09	3	11/30/09		\$ 1,316	2	1	0	3	0	0	0	N/A
337	Agency-wide Central Control Renovation	Josephine	05/01/09	02/09/09	3	11/30/09		\$ 1,337	2	1	0	3	0	0	0	N/A
338	Agency-wide Central Control	Tillamook	05/01/09	02/09/09	3	11/30/09		\$ 1,407	2	1	0	3	0	0	0	N/A
339	Agencywide Central Control	Harney	05/01/09	02/09/09	3	11/30/09		\$ 1,572	2	1	0	3	0	0	0	N/A
340	Agencywide HVAC Renovation and Repair	Clatsop	05/01/09	02/09/09	3	08/31/09		\$ 172	2	0	0	2	0	0	0	\$ 48,000
341	Agencywide HVAC Renovation and Repair	Josephine	05/01/09	02/09/09	3	08/31/09		\$ 172	2	0	0	2	0	0	0	\$ 48,000
342	Agencywide HVAC Renovation and Repair	Linn	05/01/09	02/09/09	3	08/31/09		\$ 207	2	1	0	2	1	0	0	\$ 48,000
343	Agencywide HVAC Renovation and Repair	Harney	05/01/09	02/09/09	3	08/31/09		\$ 217	2	0	0	2	0	0	0	\$ 48,000
344	Agencywide HVAC Renovation and Repair	Union	05/01/09	02/09/09	3	08/31/09		\$ 225	2	0	0	2	0	0	0	\$ 48,000
345	Camp Tillamook Appliance Replacement	Tillamook	05/01/09	02/09/09	3	08/31/09		\$ 185	2	0	0	2	2	0	0	N/A
346	Rogue Valley YCF Fire Barrier...	Josephine	05/01/09	02/09/09	3	06/30/09		\$ 187	2	0	0	2	0	0	0	N/A
347	Agency-wide End of Life Appliance Rep.	Various	05/01/09	02/09/09	3	11/30/09		\$ 551	2	0	0	2	0	0	0	N/A
348	Hillcrest Walk-in Complex Replacement	Marion	05/01/09	02/09/09	3	08/31/09		\$ 683	2	0	0	2	0	0	0	N/A
349	RiverBend Facility Sewage Lagoon	Union	05/01/09	02/09/09	3	11/30/09		\$ 2,908	2	1	0	3	2	0	0	N/A
350	MacLaren Campus Gas HVAC Conv	Marion	05/01/09	02/09/09	3	01/31/10		\$ 3,967	2	2	0	2	2	0	0	\$ 1,500,000
351	Hillcrest - Zeta Living Unit Renovation	Marion	05/01/09	02/09/09	3	05/31/10		\$ 4,936	2	15	0	12	3	1	0	N/A
352	Tillamook YCF School House Const	Tillamook	05/01/09	02/09/09	3	11/30/09		\$ 7,310	2	0	0	2	1	0	0	N/A
353	Corvallis House Replacement	Linn	05/01/09	02/09/09	3	05/31/10		\$ 88,816	16	10	68	19	29	16	2	N/A
354	MacLaren Deferred Maintenance	Marion	05/01/09	02/09/09	3	05/31/10		\$ 74,110	12	5	0	11	14	4	0	N/A
355	Hillcrest Deferred Maintenance	Marion	05/01/09	02/09/09	3	02/28/09		\$ 3,948	2	0	0	2	0	0	0	N/A
356	Unassigned				0			\$ -	0	0	0	0	0	0	0	
357	Fire Barrier/Perimeter Fence Rd	Linn	05/01/09	02/09/09	3	06/30/09		\$ 187	2	0	0	2	0	0	0	N/A
358	Hillcrest Gymnasium Renovation	Marion	05/01/09	02/09/09	3	11/30/09		\$ 305	2	0	0	2	0	0	0	N/A
359	Hillcrest High School (see below)	Marion	05/01/09	02/09/09	3	11/30/09		\$ 1,797	2	0	0	2	0	0	0	N/A
360	MacLaren High School (see below)	Marion	05/01/09	02/09/09	3	11/30/09		\$ 1,797	2	0	0	2	0	0	0	N/A
								\$ 200,876	76	48	68	101	55	22	2	\$ 1,740,000

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion  
0) UF / UA  
UF =Unfunded Projects UA = Unassigned Project



## SB 338 Report June 17, 2009



### CCWD

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
361	BM: Safety and Security	Umatilla	04/30/09	04/22/09	3	07/01/10		\$ 115,000	0	14	406	10	4	4	0	N/A
362	BM: Aging Infrastructure	Umatilla	04/30/09	04/27/09	3	07/01/10		\$ -	0	8	178	6	1	0	0	\$ 1,160,000
363	BM: Aging Infrastructure	Umatilla	04/30/09	04/27/09	3	07/01/09		\$ 115,000	0	7	257	6	1	1	0	\$ 4,600,000
364	CE: New parking spaces	Deschutes	02/05/09	02/05/09	3	08/31/09		\$ 35,050	0	17	117	17	5	0	1	N/A
365	CE: Replace Electrical Distribution System	Deschutes	02/05/09	02/05/09	3	09/30/09		\$ 12,897	0	7	0	6	4	0	2	N/A
366	CE: Disability Access	Deschutes	02/05/09	02/05/09	3	10/31/10		\$ 35,431	1	15	44	16	7	2	1	N/A
367	CE: Roadway Repair	Deschutes	02/05/09	02/05/09	3	07/30/09		\$ 2,213	0	4	0	4	0	0	0	N/A
368	CE: Sidewalk/Hand Rail Replacement	Deschutes	02/05/09	02/05/09	3	04/30/09		\$ 36,605	4	5	0	8	10	0	2	N/A
369	CE: Fire Reduction	Deschutes	04/30/09	04/20/09	3	05/31/09		\$ 9,535	3	2	153	5	11	0	0	N/A
370	CE: Painting, Flooring, Roof Maintenance	Deschutes	02/26/09	03/23/09	3	08/31/10		\$ 21,700	0	4	140	4	2	1	0	N/A
371	CE: Building Weatherization	Deschutes	04/22/09	04/28/09	3	07/31/09		\$ 16,902	0	7	219	7	0	0	0	N/A
372	CE: Air conditioning suppression systems	Deschutes	02/05/09	02/05/09	3	09/30/09		\$ 4,075	0	3	0	3	0	0	0	N/A
373	CE: retrofit buildings	Deschutes	02/05/09	02/05/09	3	11/30/09		\$ 86,086	2	15	0	17	13	4	0	N/A
374	CH: Replace failing roof.	Marion	04/20/09	04/28/09	3	08/27/09		\$ 1,882	0	0	0	0	0	0	0	N/A
375	CH: Renovate building	Marion	03/20/09	03/20/09	3	11/16/09		\$ 12,027	0	11	66	11	18	2	0	N/A
376	CH: Replace failing storage barn	Marion	04/20/09	04/09/09	3	10/01/09		\$ 39,740	0	12	304	12	5	3	0	N/A
377	CH: HVAC and mechanical system	Marion	04/13/09	04/29/09	3	12/01/09		\$ 5,084	0	0	0	0	0	0	0	N/A
378	CH: Upgrade utility infrastructure	Marion	04/20/09	04/29/09	3	08/31/09		\$ 250	0	0	0	0	0	0	0	N/A
379	CH: Front entry roadway re-build.	Marion	04/20/09	04/22/09	3	09/15/09		\$ 71,852	3	4	293	7	6	3	2	N/A
380	CH: Upgrade primary electrical distribution	Marion	04/20/09	04/27/09	3	08/30/10		\$ 60,709	0	0	0	0	1	0	0	N/A
381	CH: Replace aged rooftop air handlers	Marion	04/20/09	04/09/09	3	08/31/09		\$ 32,622	0	5	152	5	5	2	0	N/A
382	CH: Upgrade elevators	Marion	04/20/09	04/27/09	3	08/31/09		\$ -	0	0	0	0	0	0	0	N/A
383	CH: Replace handicapped doors.	Marion	03/31/09	04/24/09	5	05/29/09	04/24/09	\$ 7,820	0	4	28	4	0	0	0	N/A
384	CH: Upgrade exterior lighting systems.	Marion	03/16/09	02/20/09	5	05/29/09	03/10/09	\$ 9,373	0	2	88	2	2	0	0	N/A
385	CH: Upgrade air doors	Marion	03/31/09	04/28/09	3	06/30/09		\$ 6,179	0	4	41	4	1	0	0	N/A
386	CH: Replacement Space	Marion	03/16/09	03/16/09	3	09/01/09		\$ 237,039	1	9	1,722	10	21	12	0	N/A
387	CH: Replace deteriorated fire station.	Marion	04/27/09	04/20/09	3	08/17/09		\$ 9,497	0	4	51	4	0	0	0	N/A
388	CH: Replace shift quarters.	Marion	03/02/09	03/02/09	3	10/15/09		\$ 51,910	0	13	371	13	7	0	0	N/A
389	CH: Create classroom	Polk	02/20/09	02/20/09	3	11/20/09		\$ 192,294	3	22	662	22	34	5	0	N/A
390	CH: Replace failing metal roof	Yamhill	04/20/09	04/29/09	3	07/10/09		\$ 655	0	0	0	0	0	0	0	N/A
391	CH: Re-roof Santiam Center	Marion	04/20/09	04/28/09	3	07/15/09		\$ 40	0	0	0	0	0	0	0	N/A
392	CL: Replace communications infrastructure	Clackamas	05/01/09	04/22/09	3	08/31/09		\$ 553,903	0	13	376	13	16	3	2	N/A
393	CL: Complete duct cleaning.	Clackamas	04/27/09	04/06/09	5	04/30/09	04/08/09	\$ 2,828	0	2	68	2	4	0	2	N/A
394	CL: Install roll up security doors	Clackamas	05/01/09	04/24/09	3	06/01/09		\$ -	0	2	12	2	0	0	0	N/A
395	CL: Replace Industrial wing roll up doors.	Clackamas	05/01/09	04/24/09	3	06/30/09		\$ -	0	3	0	3	0	0	0	N/A

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
396	CL: Repair/renovate	Clackamas	05/01/09	04/09/09	3	08/14/09		\$ 4,395	0	2	25	1	4	0	0	\$ 2,936
397	CL: Energy efficiency to HVAC system.	Clackamas	04/27/09	04/09/09	3	05/29/09		\$ -	0	2	0	1	4	0	0	\$ 1,670
398	CL: Repaint blue Rails, exterior doors.	Clackamas	05/01/09	04/17/09	5	07/01/09	04/27/09	\$ 13,950	2	0	47	1	4	0	0	N/A
399	CL: Ceiling tiles replacement.	Clackamas	05/01/09	04/20/09	5	06/19/09	06/01/09	\$ 2,730	1	3	110	4	5	1	2	N/A
400	CL: Patch, paint interior walls throughout.	Clackamas	05/01/09	04/23/09	3	07/24/09		\$ 1,210	0	2	43	2	2	0	0	N/A
401	CL: Carpet and linoleum replacement	Clackamas	05/01/09	04/27/09	3	07/31/09		\$ -	0	8	16	8	8	5	0	N/A
402	CL: Energy efficiency to HVAC system.	Clackamas	05/01/09	04/22/09	5	05/08/09	05/08/09	\$ -	0	2	89	1	4	0	0	\$ 396
403	CL: Patch,paint interior walls throughout.	Clackamas	05/01/09	04/27/09	3	07/24/09		\$ 17,335	5	2	0	4	4	0	2	N/A
404	CL: Replace floor	Clackamas	05/01/09	04/28/09	3	07/31/09		\$ -	0	7	48	7	7	4	0	N/A
405	CL: Energy efficiency HVAC system.	Clackamas	03/27/09	03/27/09	5	04/03/09	03/27/09	\$ 9,943	0	2	70	1	8	2	0	\$ 298
406	CL: Energy efficiency controls HVAC system	Clackamas	04/13/09	04/17/09	5	04/30/09	04/24/09	\$ 6,959	0	2	50	1	4	0	0	\$ 1,972
407	CL: Energy efficiency HVAC system.	Clackamas	04/13/09	04/14/09	5	04/30/09	04/21/09	\$ 7,338	0	2	48	1	4	0	0	\$ 1,972
408	CL: Install new fire alarm system.	Clackamas	05/01/09	04/13/09	5	05/29/09	05/21/09	\$ 22,582	1	6	56	6	6	0	0	N/A
409	CL: Repair/renovate	Clackamas	05/01/09	04/22/09	3	09/04/09		\$ 4,353	6	3	10	6	14	6	3	N/A
410	CL: Building wide air test and balance	Clackamas	05/01/09	04/22/09	3	09/11/09		\$ -	0	1	0	1	2	0	0	N/A
411	CL: Energy efficiency HVAC system.	Clackamas	05/01/09	04/17/09	3	09/04/09		\$ -	0	2	0	1	4	0	0	\$ 2,400
412	CL: Repair/renovate	Clackamas	05/01/09	04/22/09	3	09/04/09		\$ 12,838	5	8	0	9	21	6	5	TBD
413	CL: Ceiling tile replacement	Clackamas	05/01/09	04/20/09	3	06/19/09		\$ 2,730	1	7	63	8	7	2	3	N/A
414	CL: Patch paint interior walls throughout.	Clackamas	05/01/09	04/27/09	3	07/24/09		\$ 18,679	16	5	72	12	6	2	4	N/A
415	CL: Floor tile replacement	Clackamas	05/01/09	04/27/09	3	07/31/09		\$ -	0	7	0	7	7	4	0	N/A
416	CL: Repair/renovate a	Clackamas	05/01/09	04/22/09	3	09/04/09		\$ 25,324	6	8	30	10	21	6	5	TBD
417	CL: Energy efficiency HVAC system.	Clackamas	05/01/09	04/17/09	3	09/04/09		\$ -	0	2	0	1	4	0	0	\$ 1,100
418	CL: Energy efficiency HVAC system.	Clackamas	05/01/09	04/06/09	5	05/08/09	04/15/09	\$ 6,541	0	2	32	1	4	0	0	\$ 196
419	CL: Energy efficiency HVAC system.	Clackamas	05/01/09	04/20/09	3	06/26/09		\$ -	0	2	0	1	4	0	0	\$ 1,690
420	CL: Various electrical improvements.	Clackamas	04/15/09	04/06/09	3	06/30/09		\$ 65,214	0	35	477	32	12	2	1	N/A
421	CT: Visual Arts Building	Clatsop	04/27/09	04/27/09	3	09/01/09		\$ 16,001	0	0	0	0	10	10	2	\$ 2,150
422	CT: Library Building	Clatsop	04/27/09	04/27/09	3	09/01/09		\$ 23,117	0	0	16	0	10	10	2	\$ 3,100
423	CT: MERTS I	Clatsop	04/15/09	04/30/09	3	07/30/09		\$ 19,105	0	0	0	0	4	4	2	\$ 950
424	CT: Alder Hall	Clatsop	04/27/09	04/27/09	3	09/01/09		\$ 7,845	0	0	0	0	2	2	0	\$ 830
425	CT: Patriot Hall	Clatsop	04/20/09	04/20/09	3	08/14/09		\$ 23,840	0	3	80	3	4	2	0	\$ 7,650
426	CT: Campus-Wide	Clatsop	04/16/09	04/16/09	3	07/10/09		\$ 91,428	0	14	847	14	14	4	2	\$ 14,045
427	CT: Performing Arts Center	Clatsop	04/27/09	04/30/09	3	08/15/09		\$ 8,033	0	0	0	0	2	2	2	N/A
428	CT: Forerunner Teaching Vessel	Clatsop	04/22/09	04/22/09	3	02/26/10		\$ 4,195	0	0	8	0	2	0	0	N/A
429	CT: Forerunner Teaching Vessel	Clatsop	04/28/09	05/07/09	3	05/29/09		\$ 164	0	0	0	0	0	0	0	N/A
430	CT: Josie Peper Building	Clatsop	04/27/09	04/30/09	3	07/30/09		\$ 2,764	0	0	0	0	2	2	2	\$ 75
431	CG: heating/ventilation system components	Wasco	04/30/09	04/14/09	3	09/11/09		\$ 10,091	0	5	80	5	0	0	0	N/A
432	CG: Upgrade HVAC system	Wasco	04/30/09	04/14/09	3	09/11/09		\$ 1,776	0	2	70	2	0	0	0	N/A
433	CG: windows	Wasco	04/30/09	04/22/09	3			\$ 12,000	0	3	0	3	1	0	0	N/A
434	CG: windows	Wasco	04/30/09	04/22/09	3			\$ 55,600	0	3	0	3	1	0	0	N/A
435	CG: fire sprinkler system	Wasco	04/30/09	04/24/09	3			\$ 834	0	1	0	1	1	0	0	N/A
436	CG: Replace AC condenser units.	Wasco	04/30/09	04/14/09	3			\$ 2,674	0	3	90	3	0	0	0	N/A

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
437	KL: Concrete repair	Klamath	04/27/09	04/28/09	3	07/01/09		\$ 1,397	4	12	244	16	4	2	0	N/A
438	KL: Replace locks	Klamath	04/30/09	04/29/09	3	07/31/09		\$ 2,282	0	0	0	0	0	0	0	N/A
439	KL: Pipe irrigation canal	Klamath	04/01/09	03/17/09	3	04/17/09		\$ 438,683	2	7	410	9	13	4	3	N/A
440	KL: Paint	Klamath	04/27/09	04/30/09	3	07/01/09		\$ 250	0	3	136	3	3	1	0	N/A
441	KL: Parking lot	Klamath	04/29/09	04/28/09	3	07/01/09		\$ 36,659	2	11	451	13	12	3	1	N/A
442	KL: Carpeting	Klamath	04/27/09	04/29/09	3	07/15/09		\$ 686	0	11	33	11	6	1	1	N/A
443	KL: Windows, doors	Klamath	04/30/09	04/29/09	3	09/11/09		\$ -	0	0	0	0	0	0	0	\$ 6,000
444	KL: Re-side	Klamath	04/30/09	04/29/09	3	09/11/09		\$ 2,582	0	6	21	6	6	2	0	N/A
445	LA: ADA Compliance	Lane	04/28/09	04/04/09	3	03/01/10		\$ 40,603	3	6	15	6	11	1	0	N/A
446	LA: security lighting	Lane	04/28/09	04/30/09	3	03/01/10		\$ 24,778	1	2	264	3	6	0	0	N/A
447	LA: carpeting	Lane	04/27/09	04/10/09	3	03/01/10		\$ 9,263	0	1	0	1	2	0	0	N/A
448	LA: preparation to install card access	Lane	04/28/09	04/16/09	3	03/01/10		\$ 77,634	1	8	16	8	14	1	0	N/A
449	LA: Remove asbestos insulation	Lane	04/28/09	04/30/09	3	03/01/10		\$ 3,394	0	4	0	4	2	0	0	N/A
450	LA: I Installation emergency communication	Lane	04/28/09	04/30/09	3	03/01/10		\$ 26,787	1	9	432	10	2	0	0	N/A
451	LA: electrical system, water, sub-metering	Lane	04/28/09	04/30/09	3	03/01/10		\$ 20,959	0	4	48	4	5	0	0	N/A
452	LA: Electrical upgrades -	Lane	04/03/09	04/03/09	3	03/01/10		\$ 390,296	69	52	5,257	58	56	5	0	N/A
453	LA: sewer piping	Lane	04/29/09	04/30/09	3	03/01/10		\$ -	0	3	0	3	1	0	0	N/A
454	LA: roofs	Lane	04/29/09	04/30/09	3	03/01/10		\$ 25,162	0	12	583	12	5	2	4	N/A
455	LA: restrooms	Lane	04/29/09	04/30/09	3	03/01/10		\$ 20,487	1	3	0	4	2	0	0	N/A
456	LA: utility and infrastructure improvements	Lane	04/29/09	04/30/09	3	03/01/10		\$ 28,847	0	16	0	16	18	0	1	N/A
457	LA: audio and technical infrastructure	Lane	04/29/09	04/29/09	3	03/01/10		\$ 3,122	0	7	0	7	3	1	0	N/A
458	LA: paint spray booth	Lane	04/29/09	04/30/09	3	03/01/10		\$ 51,261	0	11	0	11	10	2	0	N/A
459	LA: Replace tile	Lane	04/29/09	04/30/09	3	03/01/10		\$ 44,372	0	2	0	2	0	0	0	N/A
460	LB: HVAC	Linn	03/24/09	03/25/09	3	06/30/09		\$ 109,057	0	8	740	8	16	2	0	\$ 59,100
461	LB: insulation, glazing	Linn	03/17/09	03/18/09	3	06/30/09		\$ 113,043	4	12	1,117	13	19	12	0	\$ 443,280
462	LB: electrical transformers	Linn	03/27/09	03/31/09	3	06/30/09		\$ 1,572	0	2	16	2	4	0	2	N/A
463	LB: Upgrade exterior corridor lighting.	Linn	03/27/09	03/31/09	3	06/30/09		\$ 62,169	0	3	252	3	4	0	0	N/A
464	LB: Upgrade sidewalk lighting.	Linn	03/27/09	03/30/09	3	06/30/09		\$ 1,560	0	3	6	3	3	0	0	\$ 10,000
465	LB: Tile and carpet replacement	Linn	03/09/09	03/11/09	3	06/30/09		\$ 63,443	0	11	736	11	16	7	0	N/A
466	LB: energy management/HVAC control system	Linn	03/27/09	03/30/09	3	06/30/09		\$ 268	2	5	212	6	2	0	0	\$ 1,063,920
467	LB: Upgrade hot water circulating pumps	Linn	03/27/09	03/30/09	3	06/30/09		\$ 20,617	1	3	34	3	6	0	2	\$ 15,000
468	LB: Improve lighting fixtures on existing pole	Linn	03/27/09	03/30/09	3	06/30/09		\$ 1,650	0	3	20	3	3	1	1	N/A
469	LB: rigging system	Linn	03/19/09	03/20/09	3	06/30/09		\$ 250	0	17	194	13	2	1	0	N/A
470	LB: Ceiling, lighting, wall surface and flooring	Linn	03/17/09	03/18/09	3	06/30/09		\$ 83,846	1	15	1,367	9	12	7	2	N/A
471	LB: Asphalt road and parking lot	Linn	03/27/09	03/30/09	3	06/30/09		\$ 11,955	0	7	40	7	4	2	0	N/A
472	LB: Connect to city water system	Linn	03/27/09	03/30/09	3	06/30/09		\$ 66,918	0	10	374	10	13	4	1	N/A
473	LB: kitchen	Linn	03/26/09	03/31/09	3	06/30/09		\$ 49,870	0	4	9	4	10	1	0	N/A
474	MH: Stage Rehabilitation	Multnomah	04/30/09	04/29/09	3	09/30/09		\$ 21,029	2	1	27	2	24	12	0	N/A
475	MH: Classroom Painting, Flooring Upgrades	Multnomah	04/01/09	04/15/09	3	08/31/09		\$ 69,432	0	11	5	11	6	0	0	N/A
476	MH: Restroom ADA Upgrades	Multnomah	04/06/09	04/29/09	3	09/30/09		\$ 6,796	2	3	20	4	40	20	0	N/A
477	MH: Roof Replacement	Multnomah	04/06/09	04/15/09	3	09/30/09		\$ 133,353	2	37	1,355	35	16	6	4	N/A

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
478	MH: Reconfigurations	Multnomah	04/01/09	04/29/09	3	09/30/09		\$ 28,762	2	4	244	5	36	18	0	N/A
479	MH: Science Labs ADA Upgrades	Multnomah	04/06/09	04/29/09	3	09/30/09		\$ 1,748	2	1	2	2	32	16	0	N/A
480	MH: Dental Labs ADA Upgrades	Multnomah	04/06/09	04/29/09	3	09/30/09		\$ 3,548	2	1	2	2	36	18	0	N/A
481	OC: security cameras	Lincoln	04/01/09	03/19/09	3	06/17/09		\$ 50,576	0	4	547	4	8	2	0	N/A
482	OC: Notification system and PA system	Lincoln	04/01/09	03/19/09	3	07/31/09		\$ 6,257	0	4	1	4	5	2	0	N/A
483	OC: Generator	Lincoln	04/01/09	03/19/09	3	08/19/09		\$ 119,026	0	4	104	4	5	2	0	N/A
484	OC: Add access hardware for Audubon door	Lincoln	04/01/09	03/19/09	3	06/10/09		\$ 980	0	2	1	2	5	2	0	N/A
485	OC: Add access hardware at patio door.	Lincoln	04/01/09	03/19/09	5	05/15/09	05/22/09	\$ 1,850	0	2	13	2	5	2	0	N/A
486	PO: Mass Notification System	Multnomah	02/18/09	03/23/08	3	03/31/10		\$ -	4	6	0	6	9	3	3	N/A
487	PO: ADA Upgrades	Multnomah	03/31/09	05/08/09	3	09/01/10		\$ 4,356	1	3	45	4	3	0	2	N/A
488	PO: Voice over IP	Multnomah	03/19/09	03/31/09	3	06/30/11		\$ -	0	7	116	6	8	0	2	N/A
489	PO: centralized clock system	Multnomah	03/18/09	04/09/09	3	09/15/09		\$ 35,333	0	2	0	0	4	2	2	N/A
490	PO: Fire/Life Safety Upgrades	Multnomah	03/30/09	03/31/09	3	03/30/10		\$ 14,524	3	2	0	3	4	1	3	N/A
491	PO: Electrical Upgrades	Multnomah	03/05/09	03/05/09	3	02/01/10		\$ 8,165	6	13	10	15	0	0	3	N/A
492	PO: Environmental Maintenance/Upgrades	Multnomah	04/01/09	04/01/09	3	09/30/09		\$ -	0	11	261	11	36	18	12	N/A
493	PO: Energy Management System	Multnomah	03/31/09	03/31/09	3	09/30/10		\$ -	0	1	0	1	0	0	0	N/A
494	PO: water supply lines	Multnomah	04/15/09	04/30/09	3	12/31/09		\$ -	5	12	0	13	7	5	0	N/A
495	PO: repairs/Seismic Upgrades	Multnomah	06/01/09	05/05/09	4	06/01/10		\$ -	0	0	0	0	0	0	1	N/A
496	PO: Roadways/Parking lots	Multnomah	03/23/09	03/23/09	3			\$ 18,937	0	10	190	10	15	6	3	N/A
497	PO: T-12 lighting	Multnomah	03/23/09	04/30/09	3	09/05/09		\$ 12,373	2	3	173	3	2	0	2	\$ 10,338
498	PO: boilers	Multnomah	04/08/09	04/30/09	3	10/31/09		\$ 2,744	1	4	0	4	0	0	0	\$ 15,500
499	PO: Gym flooring	Multnomah	06/20/09	04/23/09	3	09/01/09		\$ -	0	3	0	3	2	0	0	N/A
500	PO: swimming pool decking	Multnomah	05/09/09	04/29/09	3	09/09/09		\$ -	2	0	0	2	2	0	0	N/A
501	PO: Grounds Greenhouse & Shade house	Multnomah	04/08/09	04/13/09	3	09/30/09		\$ 1,455	0	2	0	2	4	0	2	N/A
502	PO: Skylight Replacements	Multnomah	04/01/09	04/03/09	3	09/01/09		\$ -	0	1	0	1	0	0	0	N/A
503	PO: boilers	Multnomah	04/08/09	04/30/09	3	10/31/09		\$ 1,150	1	4	0	4	0	0	0	\$ 10,000
504	PO: Parking Lot Lighting	Multnomah	03/16/09	04/30/09	3	04/02/10		\$ 446	0	4	8	4	2	0	2	N/A
505	RO: Replacement of electrical panels.	Josephine	04/01/09	04/02/09	3	07/31/09		\$ -	0	1	3	1	0	0	0	N/A
506	RO: Replacement of Aging HVAC Units -	Josephine	04/01/09	03/03/09	3	01/31/10		\$ -	2	3	207	3	7	0	0	\$ 161,463
507	RO:replacements for ADA and safety reason	Josephine	05/01/09	04/16/09	3	01/31/10		\$ -	2	3	364	4	3	0	0	N/A
508	RO: maintenance and sidewalk replacement	Josephine	05/01/09	04/24/09	3	10/31/09		\$ -	0	3	240	3	12	4	0	N/A
509	RO: Instructional space.	Josephine	04/01/09	04/01/09	3	12/31/09		\$ -	1	5	160	6	8	3	2	N/A
510	RO: Flooring Replacement.	Josephine	04/01/09	04/06/09	3	09/30/09		\$ -	0	0	0	0	0	0	0	N/A
511	RO: Window Replacement	Josephine	05/01/09	04/29/09	3	12/31/09		\$ -	2	2	310	3	8	1	0	\$ 282,139
512	RO: Illinois Valley	Josephine	04/01/09	04/29/09	3	09/30/09		\$ -	1	0	8	1	2	1	0	N/A
513	RO: Asphalt overlay	Josephine	04/01/09	03/18/09	3	07/31/10		\$ -	0	5	0	5	2	0	1	N/A
514	RO: Replace network	Josephine	04/01/09	04/24/09	3	12/31/10		\$ -	1	2	15	3	3	0	0	N/A
515	RO: Roof replacement	Josephine	04/01/09	04/21/09	3	10/31/09		\$ -	2	6	189	8	10	4	1	N/A
516	SW: Roofing repairs.	Coos	05/01/09	04/24/09	3			\$ 59,795	0	18	128	7	7	0	0	N/A
517	SW: Replace roadway lighting.	Coos	05/01/09	04/27/09	3			\$ 15,427	0	7	58	7	10	0	0	N/A
518	SW: Repair dryrot	Coos	05/01/09	04/22/09	3			\$ 17,284	0	6	67	6	0	0	0	N/A

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
519	SW: Repair screen vents	Coos	05/01/09	04/20/09	3			\$ 8,819	0	4	16	4	2	0	0	N/A
520	SW: HVAC repairs.	Coos	05/01/09	04/27/09	3			\$ 30,234	0	6	5	6	2	0	0	\$ 128,620
521	SW: Structural repairs	Coos	05/01/09	04/21/09	3			\$ 9,047	0	5	39	5	1	0	0	N/A
522	SW: HVAC upgrade	Coos	05/01/09	04/27/09	3			\$ 36,240	0	7	4	7	0	0	0	\$ 150,740
523	SW: Sidewalks, asphalt repairs.	Coos	05/01/09	04/24/09	3			\$ 8,271	0	11	49	11	3	0	0	N/A
524	SW: Flooring	Coos	05/01/09	04/25/09	3			\$ 17,250	0	5	0	5	3	0	0	N/A
525	SW: Paint buildings	Coos	05/01/09	04/24/09	3			\$ 29,447	0	6	0	6	0	0	0	N/A
526	SW: Clean and seal building	Coos	05/01/09	04/30/09	3			\$ 6,920	0	3	0	3	0	0	0	N/A
527	SW: Remodel 4 ADA compliance	Coos	05/01/09	04/21/09	3			\$ 17,681	0	5	58	5	0	0	0	N/A
528	TB: renovation of Building	Tillamook	05/11/09	05/18/09	3	08/14/09		\$ -	0	10	0	10	5	4	0	N/A
529	TV: Paving gravel lots	Malheur	04/30/09	04/28/09	3	09/18/09		\$ 21,022	0	10	236	3	5	3	0	N/A
530	TV: Repair asphalt parking lots	Malheur	04/21/09	04/10/09	3	08/31/09		\$ 20,598	0	7	588	0	1	0	0	N/A
531	TV: HVAC and energy efficiency	Malheur	04/23/09	04/16/09	3	09/18/09		\$ 145,446	4	8	188	6	3	1	0	N/A
532	TV: Restroom refurbish and upgrade	Malheur	04/21/09	04/10/09	3	09/03/09		\$ 136,632	1	23	803	18	20	8	2	N/A
533	TV: Roofing upgrade	Malheur	04/28/09	04/17/09	3	09/03/09		\$ 42,884	2	6	641	5	5	0	0	N/A
534	TV: install visual and audible alarms	Malheur	04/28/09	04/28/09	3	09/03/09		\$ 7,601	0	3	0	1	4	2	0	N/A
535	TV: ADA upgrades	Malheur	04/28/09	04/08/09	3	09/11/09		\$ 19,175	0	2	0	2	2	0	0	N/A
536	TV: Replace sidewalk	Malheur	04/21/09	04/16/09	5	05/08/09	05/08/09	\$ 19,914	0	5	112	5	10	4	0	N/A
537	TV: Replace sidewalk	Malheur	04/21/09	04/15/09	5	05/08/09	05/08/09	\$ 38,200	2	5	140	4	8	2	0	N/A
538	UM: Replace pool filtering system	Douglas	04/01/09	04/06/09	3	06/12/09		\$ 31,692	5	5	304	8	16	4	0	N/A
539	UM: ADA/Title 9 compliance issues	Douglas	04/01/09	02/16/09	3	09/30/09		\$ 26,957	5	5	258	7	6	4	4	\$ 62,743
540	UM: Remodel food service area	Douglas	04/01/09	02/16/09	3	09/30/09		\$ 9,015	0	9	24	9	2	0	0	N/A
541	UM: Replacement asbestos abatement	Douglas	04/01/09	03/23/09	3	06/30/09		\$ 39,336	5	10	446	11	16	3	3	N/A
542	UM: Remove hard water deposits	Douglas	04/20/09	04/30/09	3	09/30/09		\$ 30,015	2	7	451	5	8	0	0	N/A
543	UM: Restroom upgrades	Douglas	04/27/09	04/30/09	3	01/31/10		\$ 64,055	1	10	470	11	5	0	0	N/A
544	UM: Replace electrical panels	Douglas	04/27/09	04/30/09	3	11/30/09		\$ 345	0	6	51	6	2	0	0	N/A
545	UM: Replace sidewalks	Douglas	04/01/09	03/20/09	3	09/30/09		\$ 636,444	3	56	2,192	59	24	6	3	N/A
546	UM: Walkway security lighting	Douglas	04/27/09	04/29/09	3	06/30/09		\$ -	0	1	16	1	0	0	0	N/A
547	UM: New motors and pumps	Douglas	04/20/09	04/29/09	3	06/30/09		\$ 30,504	0	6	86	6	5	3	1	N/A
								\$ 6,242,599	230	1,136	33,289	1,141	1,242	372	125	\$ 8,222,273

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion  
0) UF / UA  
UF =Unfunded Projects UA = Unassigned Project



## SB 338 Report June 17, 2009



#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
1	DAS	Central Point Carpet Replacemnet			
2	DAS	UPS Battery Replacement SDC			
3	DAS	Carpet Replacement			
4	DAS	L&I Bldg. Domestic Water Pipe Replcmnt.			
5	DAS	Exterior Canopy- Pendleton 202		The numbers reported in line items 26 through 35 above reflect the design efforts for three projects that were combined into one design contract. The three projects that were combined are: -DAS_0005, 0006 & 0009.	
6	DAS	Chiller Replacement - Pendleton 201		The numbers to be reported in line items 26 through 35 are listed in DAS_0005 - Exterior Canopy - Pendleton 202 because the design efforts for three projects were combined into one design contract. The three projects that were combined are:-DAS_0005, 0009	
7	DAS	Unfunded			
8	DAS	Unfunded			
9	DAS	Painting/Ceiling Tile/Restroom Improv.		The numbers to be reported in line items 26 through 35 are listed in DAS_0005 - Exterior Canopy - Pendleton 202 because the design efforts for three projects were combined into one design contract. The three projects that were combined are: --DAS_0005, 0009	
10	DAS	PSOB Fire System Upgrade - Ph. 2		This is a design build contract. The contractor is currently designing (engineering) the project and is expected to start work on site next month. No payment invoices have been submitted yet.	
11	DOC	Replace Freezer Lighting at CDC		Received materials, mobilized contractor to begin install, material and labor encumbrances total \$82,765	
12	DOC	Replace expired wireless batteries		Waiting material receipt, \$99,255 encumbered for material. Awaiting material receipt to issue contract for install.	Project will be accomplished at four locations in Salem (OSP, OSCI, SCI, MCCF) and one in Tillamook (SFFC)

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
13	DOC	Replace backup electrical system		Energy savings and CO2 savings will be calculated after determination of solar panel output. Issued design contract for \$20,000. Design in progress, waiting for design documents.	
14	DOC	Install solar system		Energy savings and CO2 savings will be calculated after determination of solar panel output. Solicitation for Contractor complete, contract award in progress. Waiting for contractor insurance and bonding information.	Food bank buildings at TRCI
15	DOC	Replace out of date Security System		Solicitation for programmer complete. Negotiated fee to support contract award. Contract award in progress.	Out of date systems at TRCI.
16	DOC	Replace failing unit door control system		Solicitation for programmer complete. Negotiated fee to support contract award. Contract award in progress.	Systems with computer based system.
17	DOC	Replace warehouse Lighting at CDC		Energy Savings and CO2 savings will be calculated when total number of fixtures replaced is known after bidding. Contract in place, work in progress.	Efficient fluorescent lighting.
18	DOC	Electrical panel upgrades		Waiting receipt of insurance information from contractor. Contract award pending.	On electrical distribution panels for code compliance at all institutions. Project to be accomplished at SRCI in Ontario, PRCF in Baker City, EOCI in Pendleton, TRCI in Umatilla, CRCI in Portland, CCCF in Wilsonville, SFFC in Tillamook, DRCI in Madras...
19	DOC	Replace electronic security network		Contractor testing existing fiber cabling to determine suitability for re-use.	Network at SRCI.
20	DOC	Replace Lighting for energy efficiency		Waiting material delivery for first location, contractor selected, work to start pending arrival of material.	Efficient LED fixtures in non inmate handling areas at all institutions. Project to be accomplished at SRCI in Ontario, PRCF in Baker City, EOCI in Pendleton, TRCI in Umatilla, CRCI in Portland, CCCF in Wilsonville, SFFC in Tillamook, DRCI in Madras, SCC
21	ODFW	Sandy Hatchery Parking Lot Construction			
22	ODFW	Denman Storage Bldg	Mobilization, Insurance & Bonding, and Engineering project fees billed.		
23	ODFW	PW Schneider Storage Bldg		Pending signature by vendor.	
24	ODFW	Sauvie Island Storage Bldg			
25	ODFW	Enterprise District Office Elevator		Pending. Intent to Award 05/06/09.	

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
26	ODFW	New Bldg at Hatfield Marine Science Ctr			
27	ODFW	Roaring River Hatchery Repair Storage Bldg			
28	ODFW	McKenzie Hatchery ADA Sidewalk	Working for McKenzie Hatchery and ODFW was a pleasure. Everyone involved in the project was exceptionally helpful and professional.	Additional Work Done of \$ 815.00	
29	ODFW	Alsea Hatchery Domestic Well Building			
30	ODFW	EE Wilson Wildlife Area Heat Pump			
31	ODFW	Summer Lake Wildlife Area New Well	Job Completed		
32	ODFW	Salmon River Hatchery Heat Pumps			
33	ODFW	South Willamette District Office Replace Electric			
34	ODFW	Southwest Region Office HVAC System Upgrade		Rebidding.	
35	ODFW	Cascade Hatchery Electrical Panel Upgrade	No Work Performed for May.		
36	ODFW	Oxbow Hatchery Electrical Service and Panel Upgrade	During the last week of May the electrical permit was purchased and temporary service was provided, but no labor or material was paid for in that period.		
37	ODFW	Rock Creek Hatchery Umpqua Pump Station Electrical Upgrades		In Engineering (Coordinating with PacifiCorp)	
38	ODFW	McKenzie Hatchery Pond Bottom Resurfacing	No work in May. Project is scheduled to start June 5, 2009.		
39	ODFW	Rock Creek Hatchery Supply Pipeline Replacement			
40	ODFW	Salmon River Hatchery New Residence			
41	ODFW	EE Wilson Wildlife Area Residence Replacement	New foundation poured, framed walls and roof, installed all utilities installed and connected. Started siding. Completely repaired existing garage, ready to paint exterior, installed new garage doors and windows		
42	ODFW	Willamette Falls Fishway Entrance 1 Foundation Settlement Repair - Phase 1			
43	ODFW	North Nehalem Hatchery Supply Pipeline Replacement			

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
44	ODFW	Canyon Creek Meadows Dam Removal Project - Phase 1		Pending. Intent to Award 05/05/09	
45	ODF	Warehouse Columns		Agency has determined that the project is not economically viable.	
46	ODF	Unfunded			
47	ODF	Prineville Lighting Project		Project started and completed second week of June, 2009.	
48	ODF	Prineville Project Lighting		Project started and completed second week of June, 2009.	
49	ODF	Springfield-Office Flooring		Project is on schedule to be completed during the week of June 8, 2009.	
50	ODF	Veneta Siding		Project substantially complete under this project. Balance to be completed by other funds. Project encountered lead paint issues.	
51	ODF	Unfunded			
52	ODF	Veneta, Shop Siding		Agency has determined that the project is not economically viable.	
53	ODF	Philomath Carpet		Work to be completed week of 06/01/2009.	
54	ODF	Dallas Carpet Replacement		Project complete.	
55	ODF	Toledo Carpet Replacement		Project Complete.	
56	ODF	Veneta Replace Siding		Agency has determined that the project is not economically viable.	
57	ODF	K-Falls Fire Cache Electrical			
58	ODF	Elkton Loading Dock			
59	ODF	Tillamook Siding replacement		Contract for balance of project with MSES firm to be executed 06/15/2009.	
60	ODF	Processing Ceiling / Mold Remediation			
61	ODF	Veneta			
62	ODF	Processing Plant Roof Replacement			
63	ODF	John Day/ Sisters Relocation			
64	OUS	Owens Hall Comprehensive Renovation		Klamath County Community Development - \$715.70	
65	OUS	Campus Loop Phase II			
66	OUS	Unassigned			
67	OUS	Phys. Ed Building		Projects 0067, 0167 and 0168 combined into this project, report 0167 is all one project.	
68	OUS	Office/Lab Bldg-Rpl Front Entry Door	Inline builders		
69	OUS	Lab - Insulate Building		No expenditures for May	

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
70	OUS	Office/Lab Building - Replace Gutters		No expenditures for May	
71	OUS	Baccus Garden Fence			
72	OUS	Replace Double Doors - Basement		No expenditures for May	
73	OUS	Cold Storage - Replace Gutters		No expenditures for May	
74	OUS	Gen Lighting -Lighting/Energy Upgrade		Coburn Electric	
75	OUS	Storage Garage			
76	OUS	Seafood Reasearch Center - Unfunded			
77	OUS	Office Lab Building--Repaint Exterior			
78	OUS	Gravel Access Drives--Regravel Drives			
79	OUS	Office/Lab Bldg-Repr Work Room Cabinets	Cascade Garage		
80	OUS	Gravel Access Drives--Regravel Drives			
81	OUS	Potato Storage Prop Refurbish Heating System			
82	OUS	Office/Shop Refurbish Heating System			
83	OUS	Seafood Research Center Repair Windows			
84	OUS	Waste - Refurbish Waste Collection Area		No expenditures for May	
85	OUS	Gravel Access Drives--Regravel			
86	OUS	Truck Scale - Replace Overhead Door		No expenditures for May	
87	OUS	Truck Scale-Replace Sliding Door		No expenditures for May	
88	OUS	HVAC upgrade-CPS		Spring Air completed their portion in May, now someone needs to do clean up and repair ceiling. Invoice received May 28, will be paid in June.	
89	OUS	Campus-Add ADA Path to Softball			
90	OUS	Seafood Research Center - Repair Perchloric Duct/Hood			
91	OUS	Door Access Control-classrooms			
92	OUS	Fire Alarm System-Art East			
93	OUS	Fire Alarm System-ECP			
94	OUS	Access Drives--Add Gravel			

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
95	OUS	Access Drives-Refurbish 8 Cattle Guards		Obisidan Ridge, High Tower Prefab	
96	OUS	Hay Barn-Repair Poles			
97	OUS	Irrigation Mainline - Refurbish		No expenditures for May	
98	OUS	Lab - Re-Side/Paint Building Exterior		No expenditures for May	
99	OUS	Door Access Control-Theatre			
100	OUS	Variable Frequency Drive		May report received, no invoicing for May	
101	OUS	Dipping Vat Building - Refurbish		No expenditures for May	
102	OUS	Metabolism Barn-Repl Overhead Doors		No expenditures for May	
103	OUS	Line Fence - Re-Place Line Fence		BOLI fee MCAREC PO 079966 \$250.00 Marking Fee/Mtls \$6.99 Hood River Supply	
104	OUS	Rain Gutters		Aaire Care of Oregon Invoice	
105	OUS	Seafood Research Ctr-Replace Boiler			
106	OUS	Seafood Research Ctr-Refinish Ext Siding		Airrun developments	
107	OUS	Dock - Replace Floats			
108	OUS	Corral - Re-Place Corral & Waterers		Inspections Inc Building Permit \$320.81	
109	OUS	Equipment Shed - Re-Roof	James Maher Construction, Inc. - Mike Maher Onwer - (541) 490-3159 - Project #117		
110	OUS	Door Access Control-Britt			
111	OUS	Door Access Library			
112	OUS	Fire Alarm System Replacement			
113	OUS	Equipment Shed - Reroof		No expenditures for May	
114	OUS	Elevator Upgrade-CH			
115	OUS	Elevator Upgrade-EP			
116	OUS	Lab - Refurbish HVAC System		Printing Charge VP001307 \$171.91Survival Media/Burns Times Bid Ads \$164.25 BOLI FEE \$250.00 J0431148	
117	OUS	Refurb Chem Storage/Mixing Area		No expenditures for May	
118	OUS	HVAC Upgrade MN			
119	OUS	Rice-Replace Motors w/ High Eff., VFD			
120	OUS	Expanded Digital Control	Johnson Controls - May 2009 - Ordered/delivered required material for the project.		
121	OUS	Exterior Lighting		May \$ for the City of Ashland to install transformer. No data sheet was received from the City. Hours reported are for Rogue Electric.	
122	OUS	Exterior Door and Hardware Replacement		BOLI Fee \$125.00 J0431182 Devco Eng Invoice split between 0122 and 0140 Inv #21545 Total Invoice amount \$11,823 and this was split so \$5,911.50 was applied to this	

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
123	OUS	Drying Bldg - Refurbish Chem Storage		Improper Format. See original form.	
124	OUS	Roof replacement-CE	Henris roofing: Project is progressing well		
125	OUS	Storm Water drainage Improvements		P0008991, Robco Vendor did not send data form for April or May, PM will notify ROBCO	
126	OUS	Office - ADA Access & Refurbish Siding		Improper Format. See original form.	
127	OUS	Roof Replacement-Music		No report recived from Central Oregon Roofing for May	
128	OUS	Theatre Roof Replacement			
129	OUS	Campbell-convert from steam to hydronics	No billing for month of May		
130	OUS	Parking lot paving		Devco Eng Inv 21518	
131	OUS	Extension Office - Refurbish		BOLI fee MCARC Abate WRN350903 J0430174 \$250	
132	OUS	Learning Resources Ctr: Interior Finishes			
133	OUS	Fire Alarm System replacement			
134	OUS	Classroom Modernization CH		BOLI fees \$250	
135	OUS	Toilet Upgrades-Science Bldg			
136	OUS	Code & Safety Compliance Improvements		No work took place in the month of May due to reducing safety and aesthetic impacts during the Commencement season. All work to resume mid-June	
137	OUS	Roof replacement McNeal			
138	OUS	Replacement of Direct Burial 12,000V Elec			
139	OUS	Boiler replacement phase 2		BOLI fees \$250 City of Ashland, Plan check-Structural \$362.70	
140	OUS	Seismic Upgrades		Devco Eng Invoice split between 0122 and 0140 Inv #21545 Total Invoice amount \$11,823 and this was split so \$5,911.50 was applied to this BOLI fee HMSC WRN 348444 J0431182 \$125.00 JE112 Go Oregon Printing Chg 13188 \$264.67 J0432176...	
141	OUS	Exterior Building Repairs		West side roof removed and reassemble work started; doing brick a motor repair work	
142	OUS	Replace plumbing building 900		RW Eng invoices 16060 16273 JE112 Go Oregon Printing Chg 14575 218.46 Capital City/ABC Inc dba Newport Ne 111.44...	

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
143	OUS	0143-Renov Labs in Ed Wing-HMSC		Improper Format. See original form.	
144	OUS	Strand Ag 1st Floor SE Bathrooms/Lab		No expenditures for May	
145	OUS	Gill Coliseum - exterior paint		No expenditures for May	
146	OUS	AB Acad. Modern. & Access.			Fire/life safety improvements, new teaching space
147	OUS	Electrical Upgrades and Replacements			
148	OUS	Programmatic Modifications			
149	OUS	Seawater system effluent treatment		Improper Format. See original form.	
150	OUS	Mechanical Upgrades and Replacements		No work done in May, waiting on material to arrive in mid to late June	
151	OUS	Pierce Library Roof Repair / Replacement	Bid Package for Roofing Replacement Issued.	Design Complete - Bid Package for Roofing Subcontractors to be issued early June. Anticipate start of construction with EWA or GMP in place mid June as forecasted. On Schedule.	
152	OUS	Roof Replacement, Owens, Semon, Boivin			
153	OUS	Deferred Interior Finish Replacements			
154	OUS	Dorion Hall Demolition & Site Improvements	Project estimating, value engineering and budgeting are in process. Final design documents were completed on 5/21/09. Early Work Amendment #2 was released on May 28, 2009 for Abatement Phase.	Currently in Abatement Phase of Work-Structural Demolition expected to begin late June-09	
155	OUS	Academic Modernization			
156	OUS	NH Acad Modernization and Accessibility	Project was in pre-construction during May	5 Contractors hired - 2 are Minority owned business	New and expanded instructional space
157	OUS	CH Classroom Upgrades		One ESB sub-contractor	Abate and upgrading old classrooms
158	OUS	Campus-Steamline Phase II			
159	OUS	LH Academic & Program Improvements		Energy efficiency calculations will be made after final selection of windows to be used 2 contractors used - 1 is using an Emerging Small Business as a sub-contractor	
160	OUS	Strand Ag-Bldg repipe/upgrade plumbing		Improper Format. See original form.	
161	OUS	Waldo Hall - 4th floor renovation		Improper Format. See original form.	
162	OUS	Campus Roof Repair and Replacement		2 subcontractors are ESB	
163	OUS	E&G Bldg. Code and Life Safety Improvements		1 minority, 1 ESB and 3 women owned subcontractors, 2 women owned contractor, 1 ESB contractor, 2 MWESB contractor & subcontractor	
164	OUS	Reed Hall-Sys Upgrades & Renov		Improper Format. See original form.	
165	OUS	Heckart Hall-Sys Upgrades & Renov		Improper Format. See original form.	Improper Format. See original form.

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
166	OUS	Science Building 2 Modernization		1 subcontractor is MWESB	
167	OUS	Health & Wellness Center		Projects 0067, 0167 and 0168 combined into this project, report 0167 is all one project.	
168	OUS	Classroom, Office Bldg		Projects 0067, 0167 and 0168 combined into this project, report 0167 is all one project.	
169	OJD	Supreme Court Bldg. Roof Replacement		With the help of our DAS project manager, the contractor, and a good stretch of dry weather, OJD continues to expedite this project and as a result the project remains ahead of schedule.	
170	OMD	Hillsboro Armory Storage Building		Project is substantially complete, with punchlist items to be completed by June 19, 2009.	
171	OMD	Roseburg Armory Floor Tile Replacement		Substantially complete. Punch-list items remain.	
172	OMD	Hermiston HVAC For Drill Floor		This project adds HVAC to the 5400 square foot drill hall where there is currently no A/C. This project will increase armory rentals, previous lack of A/C meant inside temperature of over 100 degrees during summer rental events.	
173	OMD	Redmond COUTES - Restroom Remodel			
174	OMD	LaGrande Armory Back Up Generator		Contractor is Kronsberg Electric, Redmond, OR The generator was scheduled to ship on June 15, 2009 but arrived, has been installed and tested. Fenced enclosure installation remains.	
175	OMD	Bend Armory Back Up Generator		Contractor is TOMCO Electric, Bend, OR Generator is a long lead item from order to delivery. Ship date for generator is 15 June 2009.	
176	OMD	Camp Withycombe Bld.6101 Reroof		Contractor is Arrow Roofing, Portland, OR. The roof is substantially complete with detail finish work remaining.	
177	OMD	Salem Armory Floor Tile Replacement		The contract will be extended approximately three weeks to allow additional asbestos abatement in the Armory Auditorium.	
178	OMD	Jackson Armory Door Replacement		Contractor is The Door Works, Portland, OR Excellent contractor, project proceeding ahead of schedule.	

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
179	OMD	Camp Rilea Replace Roofing & Siding	Masonry installation scheduled start May 27th. Specialty doors and roofing has been ordered. Material delivery expected 2nd week of June 2009. 95% of construction completion anticipated by end of June.	Richart Family, Inc. Resident contractor Sherwood, OR.	
180	OMD	Hood River Armory Storage Building		Contractor is Hale Construction NW, Hood River, OR. Contract is \$470,720, COP budget is \$200K. The \$270K not funded for this project will be funded from two other stimulus projects at this site and from existing budget.	
181	OMD	Grants Pass Armory Parking Lot Upgrade			
182	OMD	Kleiver Armory Parking Lot Upgrade	Hours and Labor Cost have been forecasted for the day of the 26 through the 29th.		
183	OMD	Hood River Armory Compound Improvem'ts			
184	OMD	Hood River Armory Interior Remodel			Interior remodel of kitchen, finishes throughout armory, complete data/telecom rewire, new doors/window, utilities and HVAC system.
185	OMD	BIAK Restroom & Shower Facility	Contractor is mobilized and project is under way with no unresolved issues.	Funding for this project is in both the federal and state stimulus funding packages.	This project adds a new 2165 square foot restroom and shower facility (male/female).
186	OMD	Coos Bay Armory - Interior Remodel	May labor hours and dollars are for demolition and general labor. Non-construction hours and doors are for supervision on the jobsite for work through payroll work ending 5/5/09. Payroll week ending 5/22/09 has not been processed at the time this report..		This project remodels the female restroom and adds shower and locker room area. The project replaces single pane windows and upgrades lighting throughout. The project improves the parking to include ADA signage and parking, and expands the vehicle compound.
187	OMD	Prineville CORC - Interior Remodel		The contract award is in progress. Work will probably not start until early July 2009.	
188	OPRD	Beverly Beach SP Playground			
189	OPRD	Tumalo State Park Playground			
190	OPRD	Arizona Beach SP Restroom			
191	OPRD	Carl Washburn SP Paving			
192	OPRD	Bullards Beach SP Paving			
193	OPRD	Wallowa Lake SP Docks			
194	OPRD	Sarah Helmick SP Paving			

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
195	OPRD	Champoeg SP Restroom			
196	DSL	Fence Removal			
197	DSL	Juniper removal		One remaining project pending snowmelt expected to be completed in June 09	
198	DSL	Portland Harbor Boundary Survey	Project to Begin 6/08/09.		
199	DSL	Chiller Replacement			
200	ODOT	93rd SE Yamhill Air Monitor Station Door			
201	ODOT	Salem Building U Replace OH Door			
202	ODOT	Santiam River SB Replace Locks			
203	ODOT	Sweet Home MS Roof Moss Treatment			
204	ODOT	Soda Mt. MW Bldg Seal Roof Vents/Elec			
205	ODOT	Reedsport MS Replace Shingles, Door			
206	ODOT	Baker City OSP Office Exterior Repairs			
207	ODOT	Humbug MS Install Elect Outlets			
208	ODOT	Baker Valley SRA Replace Door and Gutter		Project is complete, waiting on contractor paperwork submission- \$3,465 reported on last update paperwork	Contractor - Tom VanBell Construction
209	ODOT	Moro MS Deferred Maintenance			
210	ODOT	Corvallis MS Replace Window Panes			
211	ODOT	Rocky Point Scale Misc Repairs			
212	ODOT	Seaside MS Replace O/H Dorr Panels		Project 99% complete, requiring final ODOT inspection	Contractor - Coast Garage Doors
213	ODOT	District 13 Office Secure Crawl Space			
214	ODOT	Elgin MS Bldg Replace Flooring		Project 99% complete, waiting final ODOT inspection	Contractor - Oregon Contract Flooring LLC
215	ODOT	Manning MS Stor C Doors			
216	ODOT	Baker City MS Repair Roof			
217	ODOT	Condon MS Replace Garage Door			
218	ODOT	Salem MS Replace Window Flooring		Project 20% complete	Contractor - Bringham Construction Business Classification 3 & 4
219	ODOT	Astoria DMV Repair Roof Damage			
220	ODOT	C. Reynolds Repair Water Line/Boring			
221	ODOT	Fall River Scoop Shed Metal Siding			
222	ODOT	Farewell Bend POE Repair Siding			
223	ODOT	I5-228 Sand Shed Siding Repairs			

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
224	ODOT	Salem Signal Bldg Replace Carpet		Project 50% complete	Contractors - Oregon Contract Flooring, Phil-Am Enterprises, Willamete Express
225	ODOT	Walterville Scale Gutters Paneling ADA			
226	ODOT	Sisters Scale Hs Window/Roof			
227	ODOT	Baker City Scale House Replace Roof			
228	ODOT	McMinnville MS Replace N Window			Contractor - GJ Rylands Construction
229	ODOT	Woodburn POE Deferred Maintenance			
230	ODOT	Brothers Oasis SRA Replace Shelters			
231	ODOT	Chas Reynolds SRA Deferred Maint			
232	ODOT	Noti Scale House ADA Ele Gutters			
233	ODOT	Cave Jct MS Replace Windows			
234	ODOT	District 10 Office Replace Windows			Contractor - Great Northern Windows Inc
235	ODOT	Lagrande DMV Deferred Maint	Paulsen Environmental Consulting	Great Contractor, quick response asbestos testing	Asbestos testing only part completed in May
236	ODOT	Wolf Creek Storage Replace Floor			
237	ODOT	K Falls Sand Shed Replace Broken Joists			
238	ODOT	Salem Bldg Q Replace OH Doors			
239	ODOT	Weatherby SRA Replace Roof			
240	ODOT	Sandy MS Deferred Maintenance			
241	ODOT	Pendleton MS Deferred Maintenance		Quality OK	Contractor - Alabar Construction Inc.
242	ODOT	Woodburn MS Deferred Maintenance			
243	ODOT	Richland Scoop Shed Replace OH Doors			
244	ODOT	Rose Lodge MS RR Vinyl Walls			
245	ODOT	Spray Sand Shed Interior Repairs			
246	ODOT	Coaledo Scale House Roof & Siding			
247	ODOT	Tillamook DMV Deferred Maintenance			
248	ODOT	Myrtle Point Scale Roof Siding Floor			
249	ODOT	Ashland Scale House Siding			
250	ODOT	Suncrest SRA Replace Elec Boxes			
251	ODOT	Troutdale MS Deferred Maintenance			
252	ODOT	Gateway OSP Bldg Misc Repairs			
253	ODOT	e. Portland Illuminate Gateway			

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
254	ODOT	Memaloose SRA Deferred Maintenance			
255	ODOT	Canyonville MS Stormwater System			
256	ODOT	Ona Beach MS Deferred Maintenance			
257	ODOT	Reg 1 Bldg Replace Carpet			2 Contractors - Willamette Express and Oregon Flooring LLC
258	ODOT	Stanfield SRA Deferred Maintenance			
259	ODOT	Glenwood MS Electrical Changes			
260	ODOT	Hermiston MS Replace Fencing			
261	ODOT	LaGrande Sand Shed Misc Repairs		Good, quality work	Contractor - Precise Construction LLC ESB
262	ODOT	Stanton Blvd Sand Shed Deferred Maint			
263	ODOT	LaGrande MS Storage - replace roof	Thank you for the work	Compete, no problems, good work	Jeff Weaver Construction Inc - ESB
264	ODOT	Mitchell MS Covered Timber Storage			Contractor - Hanging Rock Construction
265	ODOT	Estacada MS Deferred Maintenance			
266	ODOT	Coos Bay DMV Deferred Maintenance			
267	ODOT	Barlow School Deferred Maintenance	Thank you for the opportunity to work	May labor for sealing work	
268	ODOT	Ashland MS Replace Carpet			
269	ODOT	East Portland MS Decant Cover			
270	ODOT	Hunter Cr MS Replace Water Line			
271	ODOT	North Portland MS Decant Cover			Minority and ESB
272	ODOT	Salem Building E Repair Roof			
273	ODOT	Shaniko MS Shop Repair/Replace OH			
274	ODOT	Distict 12 Office Deferred Maintenance		Project 80% complete, due to complexity and ordering of fixtures and parts, project completion has been delayed	
275	ODOT	Spray MS Deferred Maintenance		Good Project, quality work	Contractor - Precise Construction LLC _ESB
276	ODOT	Glide Scale Deferred Maintenance			
277	ODOT	C locks Sand Shed Replace Metal			
278	ODOT	Coos Bay Br. Bldg Replace Roof	Farrar inc would like to thank ODOT for the Go-Oregon Project, and the opportunity to work	Contractor completed project ahead of schedule	
279	ODOT	Coos Bay Sign Stor Replace Roof			Contractor - Farrar Inc
280	ODOT	Richland MS Shop Replace Roof		Good Job	ABCO Construction
281	ODOT	Gettings Cr Deferred Maintenance		Project is on schedule and 90% complete	Contractor J & R Maintenance and Painting
282	ODOT	Baldock SRA Replace Roof			
283	ODOT	Silver Lake MS Deferred Maintenance			
284	ODOT	Grand Rhond Stor OH Door Window			

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
285	ODOT	Reith Stockpile - install security fence			
286	ODOT	Ashland POE Deferred Maintenance			
287	ODOT	Bend MS Sand Shed Replace Roof		Project 93.2% complete, waiting on additional materials found required during roof replacement	Contractor The Roofing Company
288	ODOT	C. Point MS Upgrade Water Line			
289	ODOT	Austin MS Deferred Maintenance		Great Contractor. Excellent Quality, on-time	Contractor Four Seasons Roofing - ESB
290	ODOT	Juntura MS Deferred Maintenance			
291	ODOT	Jantzen Beach Shop Bldg Deferred Maint			
292	ODOT	Klamath Falls MS Deferred Maintenance			
293	ODOT	Lapine MS Replace Doors/Floor			
294	ODOT	Burns MS Deferred Maintenance	Great Job, Thank you	Excellent work, delay due to windows being shipped wrong size	Contractor - Phillip Sitz Construction
295	ODOT	Salem Dock Bldg F Roof			
296	ODOT	Seneca MS Shop Replace Doors			
297	ODOT	Dist 14 Office Deferred Maintenance			
298	ODOT	Basque MS Deferred Maintenance			
299	ODOT	Lawnfield Bldg Seal Roof/Gutters			
300	ODOT	Coquille Deferred Maintenance			
301	ODOT	Maples SRA ADA Upgrades		Project is 90% complete, finish work left	Contractor - MV Weyden Construction Co.
302	ODOT	R5 Bldg Deferred Maintenance		Materials Delays have impacted timeline, scheduled to resume 6/15 when materials arrive	Contractor - Precise Construction LLC - ESB
303	ODOT	Stinking Water Sand Roof and Repairs		Great Job, Excellent workmanship and on time	Contractor Four Seasons Roofing, ESB
304	ODOT	Bend Bldg J Deferred Maintenance		90% complete with Phase 2, asbestos abatement, requiring additional scheduling to perform work	
305	ODOT	Baldock MS Deferred Maintenance		Final inspection OK, no additional work required - all stats report in last update	
306	ODOT	Sisters MS Shop OH Doors			
307	ODOT	Bachelor Butte Sand Shed Repl Roof		Project 10% complete, materials problems	The Roofing Company
308	ODOT	Florance MS Deferred Maintenance			
309	ODOT	Alkali Lake Deferred Maintenance		Partial Payment made and reported in April of \$25,061 (no stats only payment #). Total project was \$36,132	Contractor - Central Oregon Pole Buildings
310	ODOT	Lakeview MS Deferred Maintenance		90 % complete, parital payment made in April for work perform	Rob Thornton Construction

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
311	ODOT	Boardman Deferred Maintenance		East bound project 75% done, West bound 40% done. Specific materials and fixtures are back ordered and taking 4-6 weeks for delivery. New projected completion date 6/30	Minority, women, and ESB contractors
312	ODOT	Bend Shop Roof/OH Doors			
313	ODOT	Ontario MS Repair Water Filter System	Great Job , Thanks	Payment made in April for \$28,111	Contractor Philp Sitz Conctruction
314	ODOT	Ukiah Sand Shed Replace Roof			
315	ODOT	Milwaukie Stone Bldg Replace Roof			
316	ODOT	The Dalles MS Deferred Maintenance			Information for Central Oregon Garage Door Work
317	ODOT	Oak Grove SRA Deferred Maintenance			Contractor McBeth Builders
318	ODOT	Port Orford MS Deferred Maintenance		Problems with Contractor, may need to re-bid product and remove contractor	Contractor Phil Aguilar Construction
319	ODOT	Boswell Spgs Deferred Maintenance			
320	ODOT	Davis Slough Deferred Maintenance		Project 10% complete, submittal reviews	Contractor John Carrol Construction LLC
321	ODOT	Baker City Sand Shed Roof & Siding		Problems with contractor (Specs), materials	Contractor Wellens Farwell Construction
322	ODOT	S. Umpqua SRA Deferred Maintenance			
323	ODOT	Cow Creek SRA Deferred Maintenance			
324	ODOT	Brothers MS Deferred Maintenance		Project 99% complete, waiting on paperwork and invoice submittal	Contractor High Desert Agg and Paving
325	ODOT	Central Point MS Deferred Maintenance		Project 99% complete	Contractor - Knife River
326	ODOT	Warrenton MS Deferred Maintenance			Contractor - Weatherguard
327	ODOT	Chemult MS Deferred Maintenance		Project 50% complete	Philip Sitz Construction
328	ODOT	Region 3 Bldg Deferred Maintenance		Lower of the floors is 99% complete, paving 99% complete and wiating on paperwork, new completion date 6/30	Zerback Construction for window portion of project
329	ODOT	Cabin Cr SRA Deferred Maintenance		Project 10% complete	Marv. E. Noah
330	ODOT	Shady MS Deferred Maintenance		Project 50% complete, materials on order taking longer then anticipated in original timeline	Contractor - Bineham Construction
331	ODOT	LaGrande Shop Deferred Maintenance		Phase 1 is 60% complete, phase 2 10% complete	Contractors West Coast Roofing, Extra Effort Consulting and Supply
332	ODOT	Manzanita SRA Deferred Maintenance		Contractor must resolve punchlist items before final payment made, initial \$34,269 for April work paid	Contractor H2 Construction Inc.
333	ODOT	Rail Station			

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
334	OYA	Agency Wide Central Control		Phase 1 electrical construction starts in June for the Agency-wide Central Controls Renovation Project. Contracts for Ch2M Hill and electrical include projects 0334-0339. Dollars and hours are reported however to avoid double reporting, jobs are reported..	Agencywide Central Control Room Renovation Project. Project replaces outdated, end of life access control with programmable logic control (PLC) system in each Central Control Room.
335	OYA	Agency Wide Central Control Renovation		Phase 1 electrical construction starts in June for the Agency-wide Central Controls Renovation Project. Contracts for Ch2M Hill and electrical include projects 0334-0339. Dollars and hours are reported however to avoid double reporting, jobs are reported..	Agencywide Central Control Room Renovation Project. Project replaces outdated, end of life access control with programmable logic control (PLC) system in each Central Control Room.
336	OYA	Agency Wide Central Control Renovation		Phase 1 electrical construction starts in June for the Agency-wide Central Controls Renovation Project. Contracts for Ch2M Hill and electrical include projects 0334-0339. Dollars and hours are reported however to avoid double reporting, jobs are reported.	Agency-wide Central Control Room Renovation Project at RiverBend Facility. Project replaces outdated, end of life access
337	OYA	Agency Wide Central Control Renovation		Phase 1 electrical construction starts in June for the Agency-wide Central Controls Renovation Project. Contracts for Ch2M Hill and electrical include projects 0334-0339. Dollars and hours are reported however to avoid double reporting, jobs are reported...	Agencywide Central Control Room Renovation Project Rouge Valley YCF. Project replaces outdated, end of life access control with programmable logic control (PLC) system in each Central Control room.
338	OYA	Agency Wide Central Control		Phase 1 electrical construction starts in June for the Agency-wide Central Controls Renovation Project. Contracts for Ch2M Hill and electrical include projects 0334-0339. Dollars and hours are reported however to avoid double reporting, jobs are reported ...	Agencywide Central Control Room Renovation Project Rouge Valley YCF. Project replaces outdated, end of life access control with programmable logic control (PLC) system in each Central Control room.
339	OYA	Agency Wide Central Control		Phase 1 electrical construction starts in June for the Agency-wide Central Controls Renovation Project. Contracts for Ch2M Hill and electrical include projects 0334-0339. Dollars and hours are reported however to avoid double reporting, jobs are reported...	Agencywide Central Control Room Renovation Project Rouge Valley YCF. Project replaces outdated, end of life access control with programmable logic control (PLC) system in each Central Control room.
340	OYA	Agency Wide HVAC Renovation and Repair		50% Materials have been purchased. Upgrades for desk top computers being processed. LD Construction Project Manager and Project Consultant work on projects 0334-0360 percentage of expenditures dollars and hours are reported on individual projects..	Direct Digital Controllers (DDC) are at the end of useful life and will be replaced. Where possible appropriate additional zone controls will be installed to increase energy efficiency.

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
341	OYA	Agencywide HVAC Renovation and Repair		50% Materials have been purchased. Upgrades for desk top computers being processed.LD Construction Project Manager and Project Consultant work on projects 0334-0360 percentage of expenditures dollars and hours are reported on individual projects however...	Direct Digital Controllers (DDC) are at the end of useful life and will be replaced. Where possible appropriate additional zone controls will be installed to increase energy efficiency.
342	OYA	Agencywide HVAC Renovation and Repair		50% Materials have been purchased. Upgrades for desk top computers being processed.LD Construction Project Manager and Project Consultant work on projects 0334-0360 percentage of expenditures dollars and hours are reported on individual projects...	Direct Digital Controllers (DDC) are at the end of useful life and will be replaced. Where possible appropriate additional zone controls will be installed to increase energy efficiency.
343	OYA	Agency wide HVAC Renovation and Repair		50% Materials have been purchased. Upgrades for desk top computers being processed.LD Construction Project Manager and Project Consultant work on projects 0334-0360 percentage of expenditures dollars and hours are reported on individual projects...	Direct Digital Controllers (DDC) are at the end of useful life and will be replaced. Where possible appropriate additional zone controls will be installed to increase energy efficiency.
344	OYA	Agencywide HVAC Renovation and Repair		50% Materials have been purchased. Upgrades for desk top computers being processed.LD Construction Project Manager and Project Consultant work on projects 0334-0360 percentage of expenditures dollars and hours are reported on individual projects...	Replace outdated end of life HVAC unit with energy efficient heat pump system.
345	OYA	Camp Tillamook Appliance Replacement		Appliance has been ordered, delivery expected first couple of weeks of June. LD Construction Project Manager and Consultant Project Manager are not recorded in the jobs portion of this report. These 2 jobs work on all of Go Oregon projects, to avoid...	Camp Tillamook provides centralized food service for both Tillamook YCF and Camp Tillamook. The project replaces end of life kitchen appliance and expands food service capacity. Includes new range and walk-in freezer.
346	OYA	Rogue Valley YCF Fire Barrier...		LD Construction Project Manager and Project Consultant work on projects 0334-0360 percentage of expenditures dollars and hours are reported on individual projects however to avoid double reporting on residents employed on project these 2 are reflected...	Rogue Valley YCF Fire Barrier/Perimeter Fence Road Fields around the facility have had grass fires over the past years. The project provides for a fire barrier and security perimeter road and enhances the functionality of the facility.
347	OYA	Agencywide End of Life Appliance Replac.		All appliances have been purchased expect delivery over the next couple of months (Purchase for \$92,000) LD Construction Project Manager and Project Consultant work on projects 0334-0360 percentage of expenditures dollars and hours are reported on...	Agency-wide End of Life Appliance Replacement.Replaces end of life washer/dryers and dishwashers in 7 facilities

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
348	OYA	Hillcrest Walk-in Complex Replacement		CM/GC and A&E Contractor's working on project. Construction on schedule.LD Construction Project Manager and Project Consultant work on projects 0334-0360 percentage of expenditures dollars and hours are reported on individual projects however to avoid...	Replaces walk-in Complex of 2 freezers and 2 refrigerators
349	OYA	RiverBend Facility Sewage Lagoon		Materials have been purchased. LD Construction Project Manager and Project Consultant work on projects 0334-0360 percentage of expenditures dollars and hours are reported on individual projects however to avoid double reporting on residents employed...	Provides for feasibility study, design services, and construction of expanded effluent irrigation. Expanded irrigation is needed because of short land application window.Project expands sewage lagoon system capacity and replaces end of life system compone
350	OYA	MacLaren Campus Gas HVAC Conv.		CM/GC and A&E Contractor's working on project. Construction on schedule.LD Construction Project Manager and Project Consultant work on projects 0334-0360 percentage of expenditures dollars and hours are reported on individual projects however to avoid...	Replaces antiquated boiler plant with energy efficient HVAC units at each building.
351	OYA	Hillcrest - Zeta Living Unit Renovation		CM/GC and A&E Contractor's working on project. Construction on schedule.LD Construction Project Manager and Project Consultant work on projects 0334-0360 percentage of expenditures dollars and hours are reported on individual projects however to avoid...	Renovation of 24 bend high security/mental health facility. The project extends the useful life of the building and adapts the facility to a different use; i.e. a secure intensive treatment living unit.Project will remove hazardous materials, replace room
352	OYA	Tillamook YCF School House Cons Comp		A&E contract has been executed. PO for CCTV (\$20,004) has been processed, waiting for delivery. Project is on schedule. LD Construction Project Manager and Project Consultant work on projects 0334-0360 percentage of expenditures dollars and hours...	Tillamook YCF School House Construction Completion - This construction project was started in 2006 and never completed. Currently the building is sealed up from the elements and not in use.Camp Tillamook and Tillamook YCF would like to consolidate...
353	OYA	Corvallis House Replacement		Excavation has been completed. Working with the City of Albany on final permits, public hearing completed. Project on schedule. LD Construction Project Manager and Project Consultant work on projects 0334-0360 percentage of expenditures dollars and hours...	The nearly 100 year old facility has approximately \$3.2 Million in deferred maintenance and \$1.8 Million for programmatic and code improvements. The cost to relocate the Young Women's Transition Program to existing OYA property in Albany (Oak Creek YCF)
354	OYA	MacLaren Deferred Maintenance		CM/GC and A&E Contractor's working on project. Tri Star Detention has delivered product, security fence has been installed construction underway. LD Construction Project Manager and Project Consultant work on projects 0334-0360 percentage of expenditures	MacLaren Deferred Maintenance - the project breaks down into various projects.- CIU/Geer Phase II - replace doors and exterior windows with maximum security doors, add access control programmable logic control (PLC) system and closed-circuit television..

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
355	OYA	Hillcrest Deferred Maintenance		CM/GC and A&E Contractor's working on project. Construction on schedule.LD Construction Project Manager and Project Consultant work on projects 0334-0360 percentage of expenditures dollars and hours are reported on individual projects however to avoid...	The project breaks down into various deferred maintenance projects. Hillside BCP Information Technology (IT) Recovery Site Security - CCTV Expansion - Food Service Building Security Enhancements - Site improvements (expand parking capacity and revamp...
356	OYA	Unassigned			
357	OYA	Oak Creek Fire Barrier/Perimeter Fence Rd		LD Construction Project Manager and Project Consultant work on projects 0334-0360 percentage of expenditures dollars and hours are reported on individual projects however to avoid double reporting on residents employed on project these 2 are reflected...	Oak Creek YCF Fire Barrier/Perimeter Fence Road Accomplishes work not included in the scope of the 07 09 renovation. Provides fire barrier and security for facility enhancing the functionality of the facility.
358	OYA	Hillcrest Gymnasium Renovation		CM/GC and A&E Contractor's working on project. Construction on schedule. LD Construction Project Manager and Project Consultant work on projects 0334-0360 percentage of expenditures dollars and hours are reported on individual projects however to avoid...	Replace bleachers, provide sound dampening and repaint the interior.
359	OYA	Hillcrest High School (see below)		CM/GC and A&E Contractor's working on project. Construction on schedule.LD Construction Project Manager and Project Consultant work on projects 0334-0360 percentage of expenditures dollars and hours are reported on individual projects however to avoid...	Hillcrest High School Interior Paint and Asbestos Floor Tile Replacement Replace asbestos floor tile and repaint surfaces as needed (the removal of the asbestos floor and the cove vase involves damage to the wall surface which will need to be repainted.
360	OYA	MacLaren High School (see below)		CM/GC and A&E Contractor's working on project. Construction on schedule.LD Construction Project Manager and Project Consultant work on projects 0334-0360 percentage of expenditures dollars and hours are reported on individual projects however to avoid...	MacLaren High School Interior Paint and Asbestos Floor Replacement. Replace asbestos floor tile and repaint surfaces as needed. The removal of the asbestos floor and the cove base involves damage to the wall surface which will need to be repainted.
361	CCWD	BM: Safety and Security	This month we have completed the site security and access for two buildings at the college. Next month we should have the Pendleton campus under construction. The ADA-accessible door scope has been finalized and work will be contracted in June. The RFP...		
362	CCWD	BM: Aging Infrastructure with Primary Safety Implications	Distribution system is under review and construction should start in June.		

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
363	CCWD	BM: Aging Infrastructure with Secondary Safety Implications or Principal Energy-Use Implications	HVAC systems retro commissioning work has continued, and potential measure are being developed with energy saving as a key factor in leveraging the project cost. The solar feasibility study is underway for the McCrae Activity Center and a new membrane...		
364	CCWD	CE: New parking spaces to deal with current enrollment growth			
365	CCWD	CE: Replace Aging Electrical Distribution System & Electrical Upgrades			
366	CCWD	CE: Disability Access improvements including four elevators for existing buildings			
367	CCWD	CE: Roadway Repair			
368	CCWD	CE: Sidewalk/Hand Rail Replacement			
369	CCWD	CE: Fire Reduction			
370	CCWD	CE: Painting, Flooring and Roof Maintenance			
371	CCWD	CE: Building Weatherization - Insulation and Windows			
372	CCWD	CE: Air conditioning and fire suppression systems	Engineer hired. One contractor hired. No payments made in May.		
373	CCWD	CE: retrofit buildings to respond to enrollment growth.			
374	CCWD	CH: Replace failing roof.	We have invoices from the contractors for this project which will be paid in June.		
375	CCWD	CH: Renovate building 50, expand facility.	We have an invoice from the contractor which will be paid in June.		
376	CCWD	CH: Replace failing storage barn			
377	CCWD	CH: HVAC and mechanical system capital maintenance.	We have an invoice from the contractor, it will be paid in June.		
378	CCWD	CH: Upgrade utility infrastructure	We have an invoice from the contractor, it will be paid in June.		
379	CCWD	CH: Front entry roadway re-build.			

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
380	CCWD	CH: Upgrade primary electrical distribution	We have an invoice from the contractor which will be paid in June.		
381	CCWD	CH: Replace aged rooftop air handlers	Work in progress, no invoices for this project were paid in May.		
382	CCWD	CH: Upgrade elevators	Work in progress for this project, waiting for invoice from contractor.		
383	CCWD	CH: Replace worn handicapped operator doors.			
384	CCWD	CH: Upgrade exterior lighting systems.			
385	CCWD	CH: Upgrade air doors	Project is in progress, waiting for invoices from contractor.		
386	CCWD	CH: Replacement Space, Training and Economic Center, TI costs only.			
387	CCWD	CH: Replace deteriorated training fire station.	Work is in progress, no contractor invoices for this project were paid in May.		
388	CCWD	CH: Replace shift quarters.	Work in progress, contractor's invoice will be paid in June.		
389	CCWD	CH: Create classroom	Work is in progress, contractor invoice will be paid in June.		
390	CCWD	CH: Replace failing metal roof	We have an invoice from the contractor, it will be paid in June.		
391	CCWD	CH: Re-roof Santiam Center	We have an invoice from the contractor, it will be paid in June.		
392	CCWD	CL: Replace aging college communications infrastructure			
393	CCWD	Complete duct cleaning.			Initial work completed 4/8/09. Identified 1 (one) additional duct in need of cleaning April 28th. This last duct was cleaned on May 1st.
394	CCWD	CL: Install roll up security doors on paint booth.			
395	CCWD	CL: Replace Industrial wing roll up doors.			
396	CCWD	CL: Repair/renovate			Estimated Energy Savings listed above is the annual savings.
397	CCWD	CL: Energy efficiency controls installed to HVAC system.			Estimated Energy Savings shown above is the annual savings.
398	CCWD	CL: Repaint courtyard blue handrails and Barlow exterior doors.			

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
399	CCWD	CL: Ceiling tiles replacement.			
400	CCWD	CL: Patch and paint interior walls throughout.			
401	CCWD	CL: Carpet and linoleum replacement throughout non-remodeled areas.			
402	CCWD	CL: Energy efficiency controls installed to HVAC system.			Figure listed on line #59 is the estimated annual savings.
403	CCWD	CL: Patch and paint interior walls throughout.			
404	CCWD	CL: Replace floor covering in selected areas.			
405	CCWD	CL: Energy efficiency controls installed into HVAC system.			
406	CCWD	CL: Energy efficiency controls installed into HVAC system.			The figure listed for #59 is the estimated annual savings.
407	CCWD	CL: Energy efficiency system installed into HVAC system.			The figure listed for #59 is the estimated annual savings.
408	CCWD	CL: Install new fire alarm system.			
409	CCWD	CL: Repair/renovate air handling units, exhaust fans, pumps, fans and controls.			The figure for #59 is an estimate of the annual savings. One of the sub-contractors is Progressive Mechanical and they are an ESB business (#3141).
410	CCWD	CL: Building wide air test and balance			
411	CCWD	CL: Energy efficiency system installed into HVAC system.			The figure for #59 is the estimated annual savings.
412	CCWD	CL: Repair/renovate air handling units, exhaust fans, pumps, fans and controls.			The figure listed for #59 is the estimated annual savings. Sub-contractor is an Emerging Small Business.
413	CCWD	CL: Ceiling tile replacement with recessed light fixtures			
414	CCWD	CL: Patch and paint interior walls throughout.			
415	CCWD	CL: Floor tile replacement in all three building.			
416	CCWD	CL: Repair/renovate air handling units, exhaust fans, pumps, fans and controls.			The figure for #59 is the estimated annual savings. Sub-contractor is an Emerging Small Business.
417	CCWD	CL: Energy efficiency system installed into HVAC system.			The figure listed for #59 is the estimated annual savings.

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
418	CCWD	CL: Energy efficiency system installed into HVAC system.			The figure for #59 is the estimated annual savings.
419	CCWD	CL: Energy efficiency system installed into HVAC system.			The figure for #59 is the estimated annual savings.
420	CCWD	CL: Various electrical improvements.			
421	CCWD	CT: Visual Arts Building			
422	CCWD	CT: Library Building			
423	CCWD	CT: MERTS I			
424	CCWD	CT: Alder Hall			
425	CCWD	CT: Patriot Hall			
426	CCWD	CT: Campus-Wide			
427	CCWD	CT: Performing Arts Center			
428	CCWD	CT: Forerunner Teaching Vessel			
429	CCWD	CT: Forerunner Teaching Vessel - Rebuild floating dock			
430	CCWD	CT: Josie Peper Building			
431	CCWD	CG: heating/ventilation system components			
432	CCWD	CG: Upgrade HVAC system			
433	CCWD	CG: windows			
434	CCWD	CG: windows			
435	CCWD	CG: fire sprinkler system			
436	CCWD	CG: Replace AC condenser units.			
437	CCWD	KL: Concrete repair			
438	CCWD	KL: Replace locks			
439	CCWD	KL: Pipe irrigation canal			
440	CCWD	KL: Paint			
441	CCWD	KL: Parking lot			
442	CCWD	KL: Carpeting			
443	CCWD	KL: Windows, doors			
444	CCWD	KL: Re-side			
445	CCWD	LA: ADA Compliance	Multiple contractors and vendors		
446	CCWD	LA: security lighting	Multiple contractors and vendors		
447	CCWD	LA: carpeting	flooring on order		
448	CCWD	LA: preparation to Install card access security	multiple vendors		
449	CCWD	LA: Remove asbestos Insulation			

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
450	CCWD	LA: Infrastructure to allow the Installation of a college-wide emergency communication system.			
451	CCWD	LA: electrical system, water, sub-metering			
452	CCWD	LA: Electrical upgrades -			
453	CCWD	LA: sewer piping			
454	CCWD	LA: roofs			
455	CCWD	LA: restrooms			
456	CCWD	LA: classroom utility and infrastructure improvements			
457	CCWD	LA: smart class room audio and technical infrastructure			
458	CCWD	LA: paint spray booth			
459	CCWD	LA: Replace tile			
460	CCWD	LB: HVAC mechanical, insulation, ductwork maintenance			
461	CCWD	LB: insulation, glazing			
462	CCWD	LB: electrical transformers			
463	CCWD	LB: Upgrade exterior corridor lighting.			
464	CCWD	LB: Upgrade sidewalk lighting.			
465	CCWD	LB: Tile and carpet replacement			
466	CCWD	LB: Upgrade energy management/HVAC control system network.			
467	CCWD	LB: Upgrade hot water circulating pumps			
468	CCWD	LB: Improve lighting fixtures on existing poles			
469	CCWD	LB: rigging system			
470	CCWD	LB: Ceiling, lighting, wall surface and flooring			
471	CCWD	LB: Asphalt road and parking lot area for student and staff egress.			
472	CCWD	LB: Connect to city water system for drinking water.			
473	CCWD	LB: kitchen			
474	CCWD	MH: Stage Rehabilitation			

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
475	CCWD	MH: Classroom Painting and Flooring Upgrades			
476	CCWD	MH: Restroom ADA Upgrades			
477	CCWD	MH: Roof Replacement			
478	CCWD	MH: Reconfigurations			
479	CCWD	MH: Science Labs ADA Upgrades			
480	CCWD	MH: Dental Labs ADA Upgrades			
481	CCWD	OC: security cameras			Cameras and wiring have been installed at apx. 90% of locations. DVR's are on order. Security mounting poles will be installed in June.
482	CCWD	OC: Notification system and PA system	Includes (40) hours ofr OCCC facilities Manager pursuant to Amendment #001 to our state stimulus grant agreement.		Russ Engle, OCCC Facilities, is developing strategies and obtaining quotes for various Public Address and Notification Systems and contracting.
483	CCWD	OC: Generator			Western States is currently under contract and proceeding with design build work for this project. Generator has been ordered and will be delievered to job site for installation in August.
484	CCWD	OC: Add access hardware for Audubon door.			
485	CCWD	OC: Add access hardware at patio door.			
486	CCWD	PO: Mass Notification System			NOTE: Items 36 - 57, no invoices received/paid to date; however two Purchase Orders are in process and will be issued the first week of June. One for \$308,000 and one for \$159,000.
487	CCWD	PO: ADA Upgrades			
488	CCWD	PO: Voice over IP			
489	CCWD	PO: centralized clock system			Material partial just arriving for installation beginning this month-end and into June.
490	CCWD	PO: Fire/Life Safety Upgrades			
491	CCWD	PO: Electrical Upgrades for Arc Fault protection			
492	CCWD	PO: Environmental Maintenance/Upgrades			
493	CCWD	PO: Energy Management System			
494	CCWD	PO: water supply lines			NOTE: No invoices received/paid to date.

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
495	CCWD	PO: Concrete settlement repairs/Seismic Upgrades			Selected ESB contractor has not been able to obtain performance bond as of date. If not produced by Monday 6/1/09 contract will be awarded to second lowest bidder. On 6/4/09 contract was awarded to the second lowest bidder.
496	CCWD	PO: Roadways/Parking lots repaving and seal coats			NOTE: We didn't do any stimulus work in May for this project.
497	CCWD	PO: T-12 lighting			
498	CCWD	PO: boilers			
499	CCWD	PO: Gym flooring			Wood on order from Lumber Products in Eugene Oregon. We begin to remove old floor on 6/15/09. Sub contracts are let to WBE for demo.
500	CCWD	PO: swimming pool decking			
501	CCWD	PO: Grounds Greenhouse & Shade house			
502	CCWD	PO: Skylight Replacements			Contractor has been selected and they will begin production in a week (6/1/09).
503	CCWD	PO: boilers			
504	CCWD	PO: Parking Lot Lighting			
505	CCWD	RO: Replacement of electrical panels.			
506	CCWD	RO: Replacement of Aging HVAC Units			
507	CCWD	RO: Deck and handrail replacements for ADA and safety reasons.			
508	CCWD	RO: Concrete maintenance and sidewalk replacement			
509	CCWD	RO: Instructional space.			
510	CCWD	RO: Flooring Replacement.			
511	CCWD	RO: Window Replacement in Classroom Buildings.			
512	CCWD	RO: Efficiency/Safety			
513	CCWD	RO: Asphalt overlay and lighting for parking lots and roads.			
514	CCWD	RO: Replace network and communication infrastructure			
515	CCWD	RO: Roof replacement			
516	CCWD	SW: Roofing repairs.			
517	CCWD	SW: Replace roadway and parking lot lighting.			

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
518	CCWD	SW: Repair dryrot			
519	CCWD	SW: Repair screen vents			
520	CCWD	SW: HVAC repairs.			
521	CCWD	SW: Structural repairs			
522	CCWD	SW: HVAC upgrade			
523	CCWD	SW: Sidewalks, asphalt and concrete repairs.			
524	CCWD	SW: Flooring			
525	CCWD	SW: Paint the classroom buildings and laboratories			
526	CCWD	SW: Clean and seal building			
527	CCWD	SW: Remodel 4 bathrooms for ADA compliance			
528	CCWD	TB: renovation of the Career and Technical Building			Asbestos abatement began on 5-18-09 Actual demolition work will begin on Thursday 6-11-09.
529	CCWD	TV: Paving gravel lots			
530	CCWD	TV: Repair asphalt parking lots			
531	CCWD	TV: HVAC and energy efficiency			
532	CCWD	TV: Restroom refurbish and upgrade			
533	CCWD	TV: Roofing upgrade			
534	CCWD	TV: install visual and audible alarms with strobes			
535	CCWD	TV: ADA upgrades			
536	CCWD	TV: Replace sidewalk			
537	CCWD	TV: Replace sidewalk			
538	CCWD	UM: Replace pool filtering system and supporting piping.	Report for H2O Technologies, FJM Enterprises, North Umpqua Plumbing and Specialty Ventures.		In process of being rebuilt
539	CCWD	UM: ADA/Title 9 compliance issues	Reports are for Paul Bentley and Caldwell Construction.		Architectural plans in process
540	CCWD	UM: Remodel food service area	Report for R. E. Noah and Specialty Ventures		Demolition complete
541	CCWD	UM: Replacement and asbestos abatement	Report is for Picknell Construction and Specialty Ventures.		Project is close to completion.
542	CCWD	UM: Remove hard water deposits	Report is for NuFlow		Library Building is finished.
543	CCWD	UM: Restroom upgrades	report is for Steve Songer construction, Ron Atkinson Construction and Dev, and Rex Price Architecture		Work in process
544	CCWD	UM: Replace electrical panels and main control cabinets	Reports are for Specialty Ventures and I.E.S.		One Building complete

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
545	CCWD	UM: Replace sidewalks	The report is for Knife River Guido Construction Inc, Flury Brothers, Rogue Valley Construction, Safari Signs, Picknell Construction and Brotherton Pipeline.		Sidewalks and paving in process
546	CCWD	UM: Walkway security lighting	Report for SIMS Electric, Inc.		removal of pre-existing lighting
547	CCWD	UM: New motors and pumps	The report is for Mid-State Industrial services		The project is close to completion.



## SB 338 STIMULUS PACKAGE



### Go Oregon Agency Contacts

Agency	Name	Phone	Email
DAS	Randy C. Gengler	503-378-2381	<a href="mailto:randy.gengler@das.state.or.us">randy.gengler@das.state.or.us</a>
DOC	Vern Rowan	503-934-1012	<a href="mailto:vernon.r.rowan@state.or.us">vernon.r.rowan@state.or.us</a>
DSL	Pamela Konstantopoulos	503-986-5283	<a href="mailto:Pamela.Konstantopoulos@state.or.us">Pamela.Konstantopoulos@state.or.us</a>
ODF	Bob McKee	503-945-7503	<a href="mailto:robert.p.mckee@state.or.us">robert.p.mckee@state.or.us</a>
ODFW	Enrique Rodriguez	503-947-6159	<a href="mailto:Enrique.G.Rodriguez@state.or.us">Enrique.G.Rodriguez@state.or.us</a>
ODOT	Virginia K. Carey	503-986-5800	<a href="mailto:virginia.k.carey@state.or.us">virginia.k.carey@state.or.us</a>
OJD	Bob Baxter	(503) 986-6410	<a href="mailto:Robert.A.Baxter@state.or.us">Robert.A.Baxter@state.or.us</a>
OMD	Roy Swafford	503-584-3596	<a href="mailto:roy.swafford@or.ngb.army.mil">roy.swafford@or.ngb.army.mil</a>
OPRD	Bob Reitmajer	503-986-0753	<a href="mailto:bob.reitmajer@state.or.us">bob.reitmajer@state.or.us</a>
OUS	Bob Simonton	541-346-5728	<a href="mailto:bob_simonton@ous.edu">bob_simonton@ous.edu</a>
OYA	Shawna Hill	503-981-2560	<a href="mailto:shawna.hill@state.or.us">shawna.hill@state.or.us</a>
CCWD	Use Link :		<a href="http://www.oregon.gov/CCWD/stimulus/CommunityCollegesProjectContactsList.pdf">http://www.oregon.gov/CCWD/stimulus/CommunityCollegesProjectContactsList.pdf</a>
