



SB 338 Progress Report on Oregon's Stimulus Package

Putting Oregonians to work on projects
across the state

August 17, 2009
Progress Report #4



<http://oregon.gov/recovery/GoOregon.shtml>

TABLE OF CONTENTS

Overview

Executive Summary	1
Project Detail.....	2
Planned Project Start Date.....	2
Actual Project Start Date.....	2
Project Status.....	3
Planned Project Completion Date.....	3
Expenditures to Date	4
Total Jobs.....	4
Total Construction Hours	5
Jobs Filled by Oregonians to Date	5
Total Goods and Services.....	6
MWESB.....	6
Projected Energy Savings.....	7
Jobs by County	8
Expenditures by County	9

Agency Summary

Department of Administrative Services (DAS)	10
Department of Corrections (DOC).....	11
Oregon Department of Fish and Wildlife (ODFW).....	12
Oregon Department of Forestry (ODF)	13
Oregon University System (OUS)	14
Oregon Judicial Department (OJD).....	17
Oregon Military Department (OMD)	18
Oregon Parks and Recreation Department (OPRD)	19
Department of State Lands (DSL).....	20
Oregon Department of Transportation (ODOT)	21
Oregon Youth Authority (OYA).....	25
Community College Workforce Development.(CCWD).....	26

Project Notes	31
----------------------------	-----------

Agency Point of Contacts	56
---------------------------------------	-----------

Executive Summary

The Oregon Legislature enacted Senate Bill 338 in February 2009, to stimulate Oregon's economy. The bill authorized 547 deferred-maintenance projects to create new jobs by infusing \$175 million into the market. Known as the "Go Oregon! Economic Stimulus Recovery Package," the bill placed the Department of Administrative Services (DAS) in the lead role to coordinate, oversee and report on the projects, managed by 12 state agencies.


This report represents a summary view of the status of Go Oregon! projects. A more in-depth report of agency-level data and source documents appears online: www.oregon.gov/recovery.

Statistics in Brief (Data as of July 31, 2009)

Planned and Actual Project Start Dates	Total started projects = 487 Thru July, 488 projects planned to start; 487 actually started.
Project Status	Of the 487 projects started, 284 are on schedule; 22 are behind schedule, and 181 are complete.
Project Completion Date (or scheduled completion date if ongoing)	<ul style="list-style-type: none"> • 416 projects are scheduled for completion by December, 2009. • The remaining projects are larger, more complicated projects; some will last until 2011.
Expenditures to Date	\$ 38,449,629
Number of Jobs Created or Retained	1,055 jobs created; 4,154 jobs retained (5,209 total)
Number of Construction Hours Worked	223,180
Percentage of Jobs Filled by Oregon Residents	79 percent. Oregon residents filled 4,123 of the 5,209 total jobs.
Extent to Which Oregon Products, Vendors, Contractors and Sub-Contractors Used	87 percent. 2,701 out of 3,094 companies that supplied materials and labor to complete Go Oregon! projects, are based in Oregon.
Extent to Which Minority, Women, and Emerging Small Businesses Used	8 percent. Of the 4,048 total firms contracted, 338 hold an MWESB certificate in Oregon.
Savings on Energy Costs for Energy Efficient Projects	\$12,063,890

Project Detail


Planned project start date

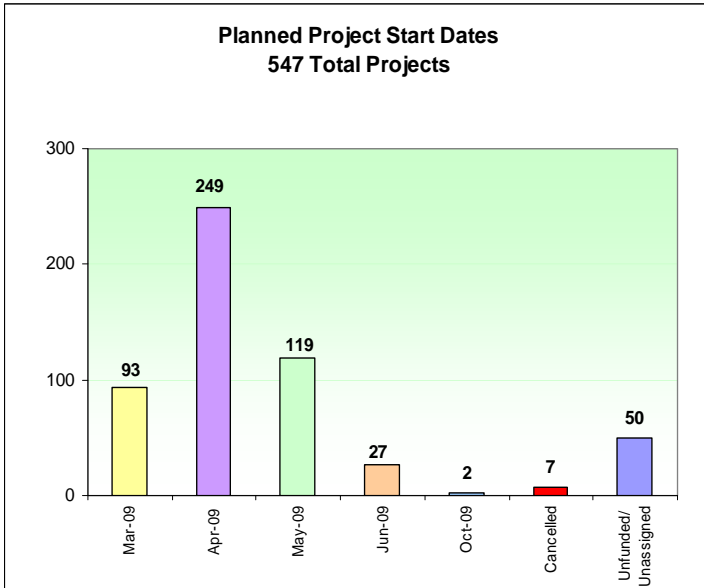

	Mar-09	Apr-09	May-09	Jun-09	Oct-09	Cancelled	Unfunded/Unassigned	Total
DAS	5	3	0	0	0	0	2	10
DOC	0	0	6	4	0	0	0	10
ODFW	5	19	0	0	0	0	0	24
ODF	1	3	6	4	0	3	2	19
OUS	16	49	13	13	0	1	13	105
OJD	0	1	0	0	0	0	0	1
OMD	0	3	14	1	0	0	0	18
OPRD	1	7	0	0	0	0	0	8
DSL	1	2	0	1	0	0	0	4
ODOT	24	59	14	0	2	3	32	134
OYA	0	0	26	0	0	0	1	27
CCWD	40	103	40	4	0	0	0	187
Total	93	249	119	27	2	7	50	547

The “planned project start date” represents the date when the responsible agency *anticipated* that people would begin to work on projects regardless of whether that meant architects or electricians. Every aspect of a project provides people with employment.



Actual project start date

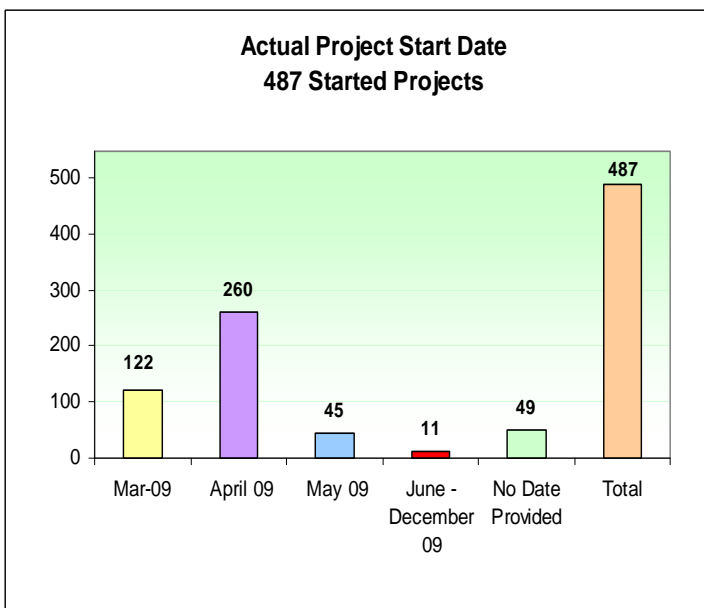

	Started 3/9/2009	Started April 09	Started May 09	Started June - December 09	No Date Provided	Total
DAS	5	3	0	0	0	8
DOC	0	1	4	5	0	10
ODFW	0	6	13	4	0	23
ODF	1	6	7	0	0	14
OUS	15	71	5	0	0	91
OJD	0	1	0	0	0	1
OMD	0	15	2	1	0	18
OPRD	8	0	0	0	0	8
DSL	0	2	0	1	1	4
ODOT	21	18	10	0	48	97
OYA	26	0	0	0	0	26
CCWD	46	137	4	0	0	187
Total	122	260	45	11	49	487

The “actual project start date” represents the date when the responsible agency first employed people to work on the project in any capacity.


Project status

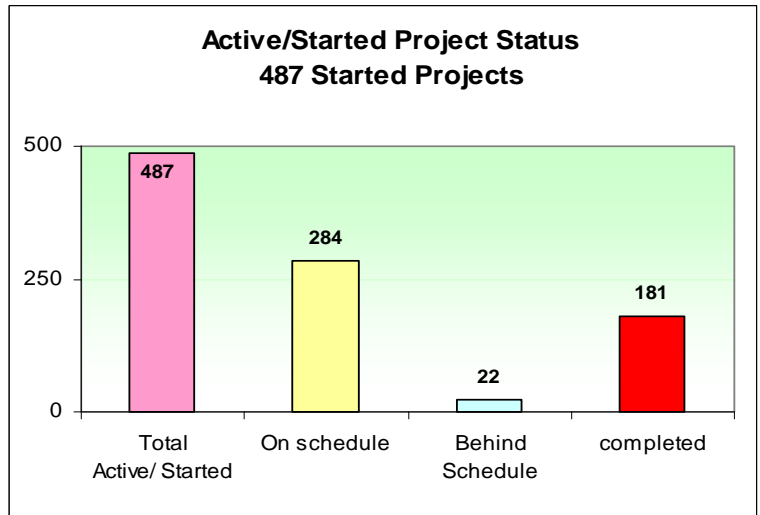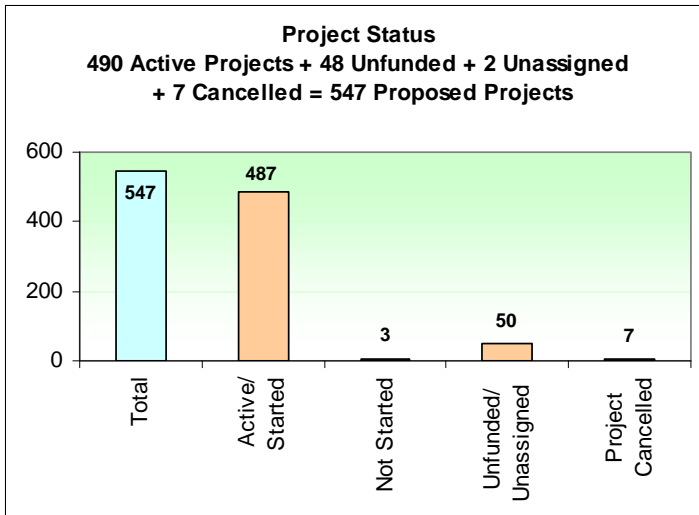

To simplify tracking, DAS established seven status levels:

1. Active/Started – people have been employed to support the project
2. Active/Not Started – no one has been employed in support of the project
3. On Schedule – the project is on track with the agency’s expected timing for the project
4. Behind Schedule – the project has fallen behind the agency’s expected schedule
5. Completed – the agency has successfully completed the project
6. Project Cancelled – the agency stopped the project before completion
7. Unfunded/Unassigned – Projects that did not receive funding under SB 338.


Project completion date (or scheduled completion date if still ongoing)

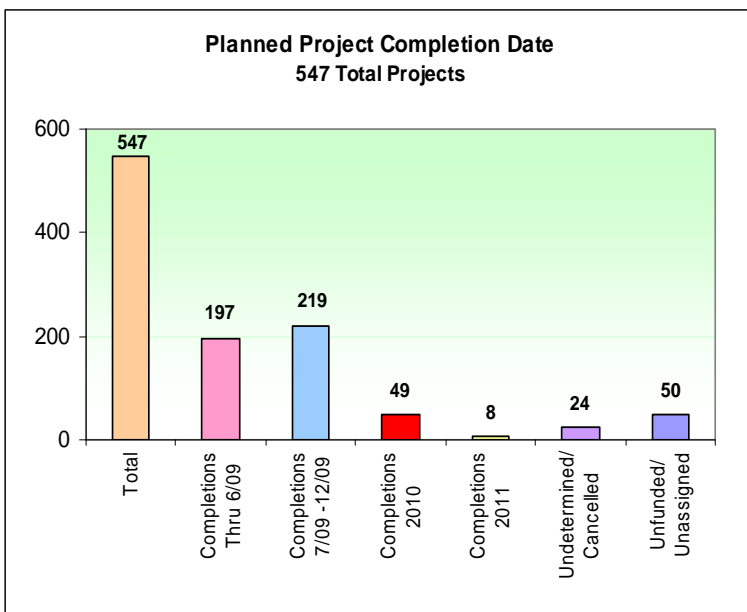

	Total	Complete Thru 6/09	Complete 7/09 Thru 12/09	Complete 2010	Complete 2011	Undetermined/Cancelled	Unfunded/Unassigned
DAS	10	2	6	0	0	0	2
DOC	10	0	6	1	3	0	0
ODFW	24	3	17	4	0	0	0
ODF	19	5	8	0	1	3	2
OUS	105	17	62	9	3	1	13
OJD	1	0	1	0	0	0	0
OMD	18	7	10	0	0	1	0
OPRD	8	6	2	0	0	0	0
DSL	4	1	2	1	0	0	0
ODOT	134	94	3	0	0	5	32
OYA	27	3	19	4	0	0	1
CCWD	187	59	83	30	1	14	0
Total	547	197	219	49	8	24	50

Estimated completion dates through June 2009, represent *completed* and *anticipated* project completion dates. Completion dates signify the date on which the responsible agency grants “final acceptance” of the project.


Expenditures to date

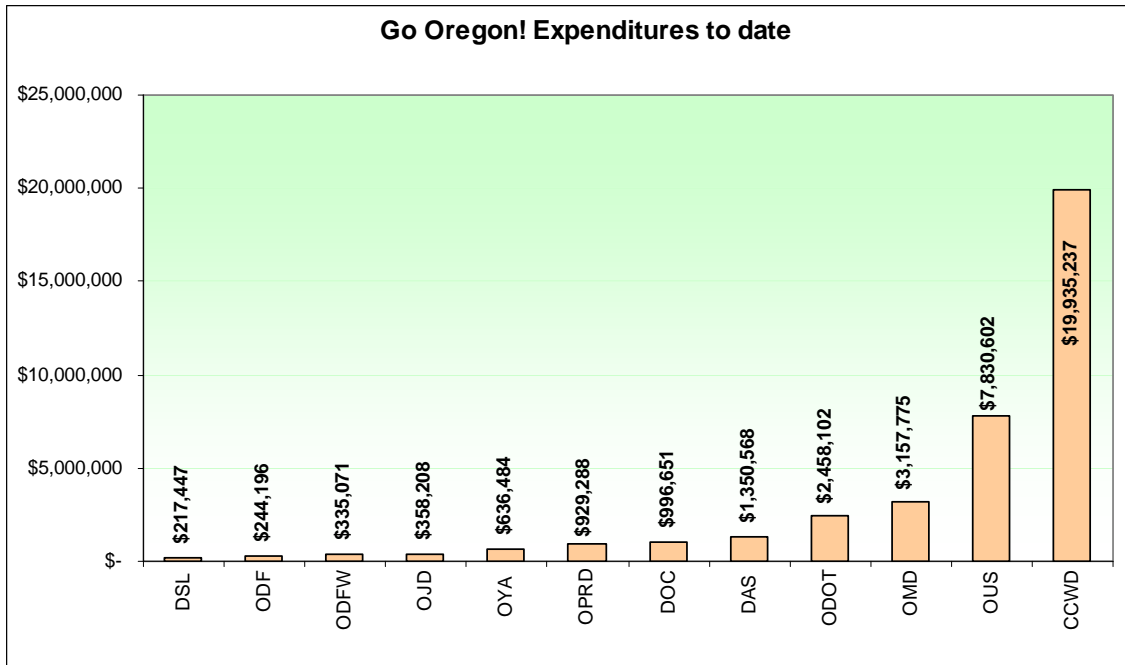

	Expenditures to date
DSL	\$ 217,447
ODF	\$ 244,196
ODFW	\$ 335,071
OJD	\$ 358,208
OYA	\$ 636,484
OPRD	\$ 929,288
DOC	\$ 996,651
DAS	\$ 1,350,568
ODOT	\$ 2,458,102
OMD	\$ 3,157,775
OUS	\$ 7,830,602
CCWD	\$ 19,935,237
Total	\$ 38,449,629

“Expenditures to date” reflects the amount of money paid by the State to individuals, contractors or materials-suppliers. Total = **\$38,449,629**


Number of jobs created or retained

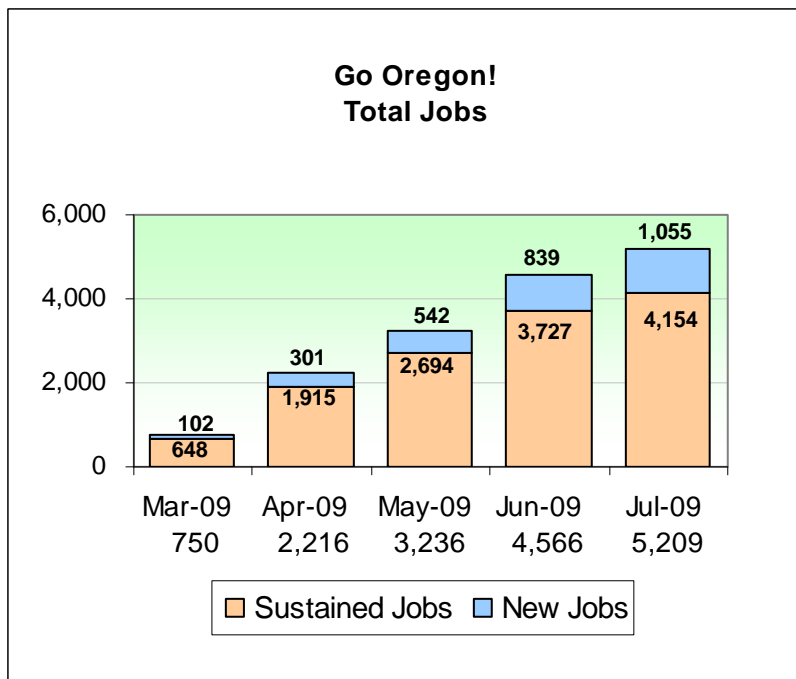

	Total New Jobs	Total Sustained Jobs	Total Jobs
DAS	14	90	104
DOC	0	3	3
ODFW	72	90	162
ODF	8	62	70
OUS	254	1,068	1,322
OJD	2	28	30
OMD	61	308	369
OPRD	0	145	145
DSL	4	29	33
ODOT	55	406	461
OYA	84	164	248
CCWD	501	1,761	2,262
Total	1,055	4,154	5,209

The “number of jobs created or retained” reflects individual people (one person = one job) working on Go Oregon! projects.


Number of construction hours worked

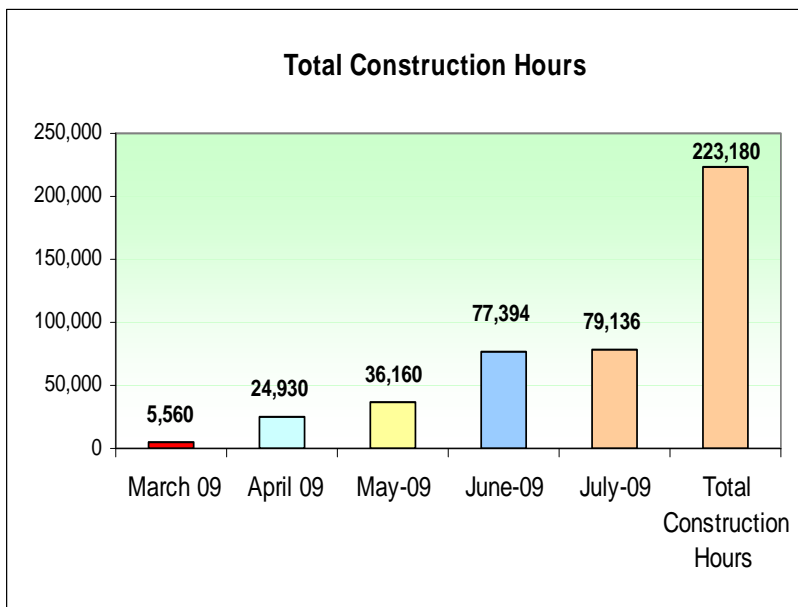

	March 09	April 09	May-09	June-09	July-09	Total Construction Hours
DAS	612	1,805	2,055	1,771	1,744	7,987
DOC	0	0	0	0	0	0
ODFW	22	146	949	1,524	1,242	3,883
ODF	54	0	436	665	424	1,579
OUS	1,597	2,292	4,354	20,899	28,557	57,698
OJD	0	4	954	741	158	1,857
OMD	0	858	2,109	6,398	3,159	12,524
OPRD	0	3,944	156	230	250	4,580
DSL	0	0	0	8	109	117
ODOT	970	5,321	4,657	3,488	811	15,247
OYA	0	68	0	190	802	1,060
CCWD	2,305	10,494	20,491	41,480	41,880	116,649
Total	5,560	24,930	36,160	77,394	79,136	223,180

Although Go Oregon! projects involve other types of work, “construction hours” best reflects the most significant labor pool affected.


Jobs filled by Oregon residents

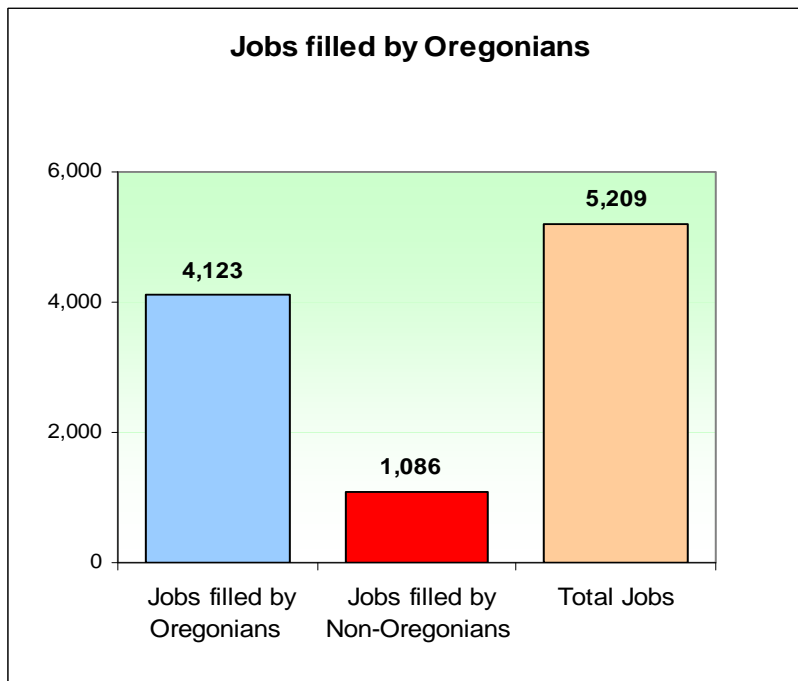

	Jobs filled by Oregonians	Jobs filled by Non-Oregonians	Total Jobs
DAS	85	19	104
DOC	3	0	3
ODFW	117	45	162
ODF	67	3	70
OUS	1077	245	1322
OJD	30	0	30
OMD	275	94	369
OPRD	72	73	145
DSL	29	4	33
ODOT	417	44	461
OYA	180	68	248
CCWD	1771	491	2262
Total	4,123	1,086	5,209

Rather than delay the economic benefits of Go Oregon! projects, contractors and businesses supplemented a predominantly Oregonian workforce with non-Oregonians.


Extent to which Oregon products, vendors, contractors, and sub-contractors used

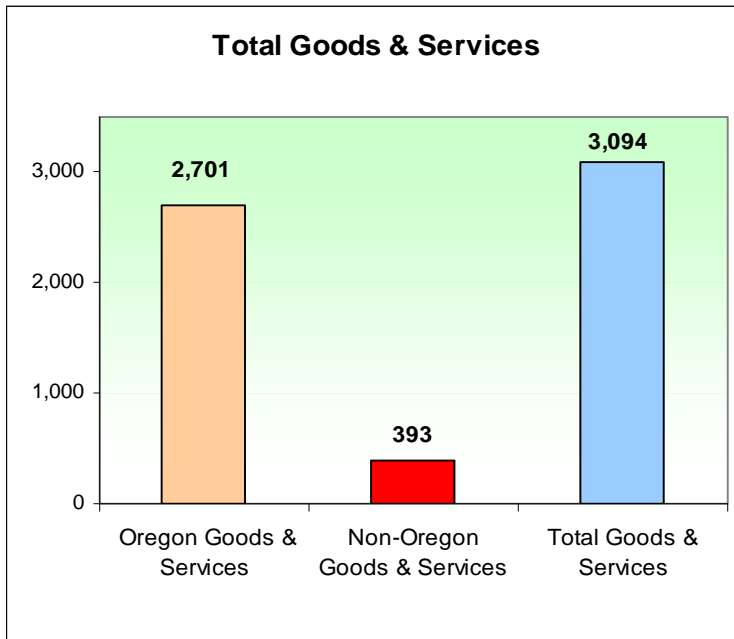

	Oregon Goods & Services	Non-Oregon Goods & Services	Total Goods & Services
DAS	48	11	59
DOC	3	0	3
ODFW	150	1	151
ODF	36	8	44
OUS	639	97	736
OJD	16	2	18
OMD	164	37	201
OPRD	21	6	27
DSL	7	0	7
ODOT	302	36	338
OYA	81	22	103
CCWD	1,234	173	1,407
Total	2,701	393	3,094

DAS made a strong effort to ensure that Oregon companies knew about Go Oregon! opportunities. By relying on a few non-Oregon companies (8 percent), agencies launched, and in some cases, completed projects in a timely manner.


Extent to which minority, women, and emerging small businesses used

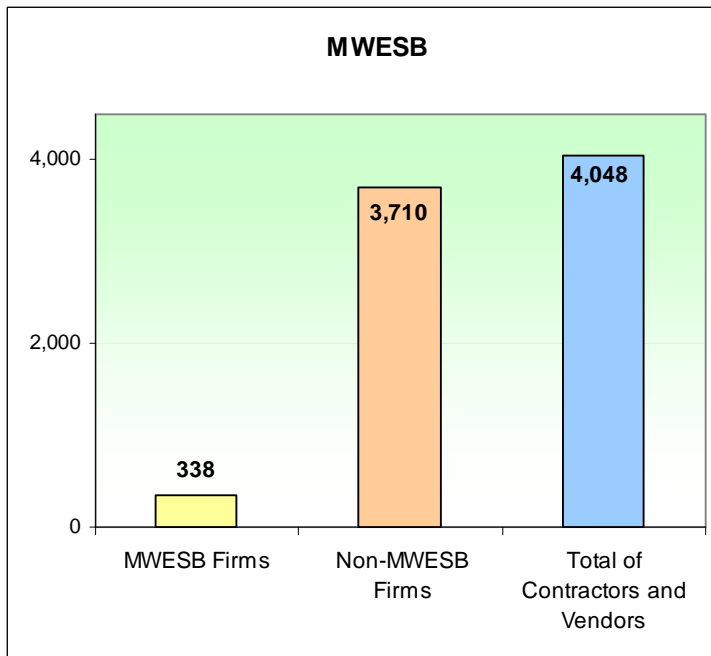

	MWESB Firms	Non-MWESB Firms	Total of Contractors and Vendors
DAS	1	74	75
DOC	0	10	10
ODFW	11	165	176
ODF	7	58	65
OUS	87	873	960
OJD	1	20	21
OMD	20	260	280
OPRD	0	37	37
DSL	2	11	13
ODOT	95	367	462
OYA	9	191	200
CCWD	105	1,644	1,749
Total	338	3,710	4,048

DAS worked closely with the Governor’s advocate for Minority, Women, and Emerging Small Business to promote Go Oregon! project opportunities among the firms registered in Oregon as MWESB.

Savings on energy costs for energy efficiency projects

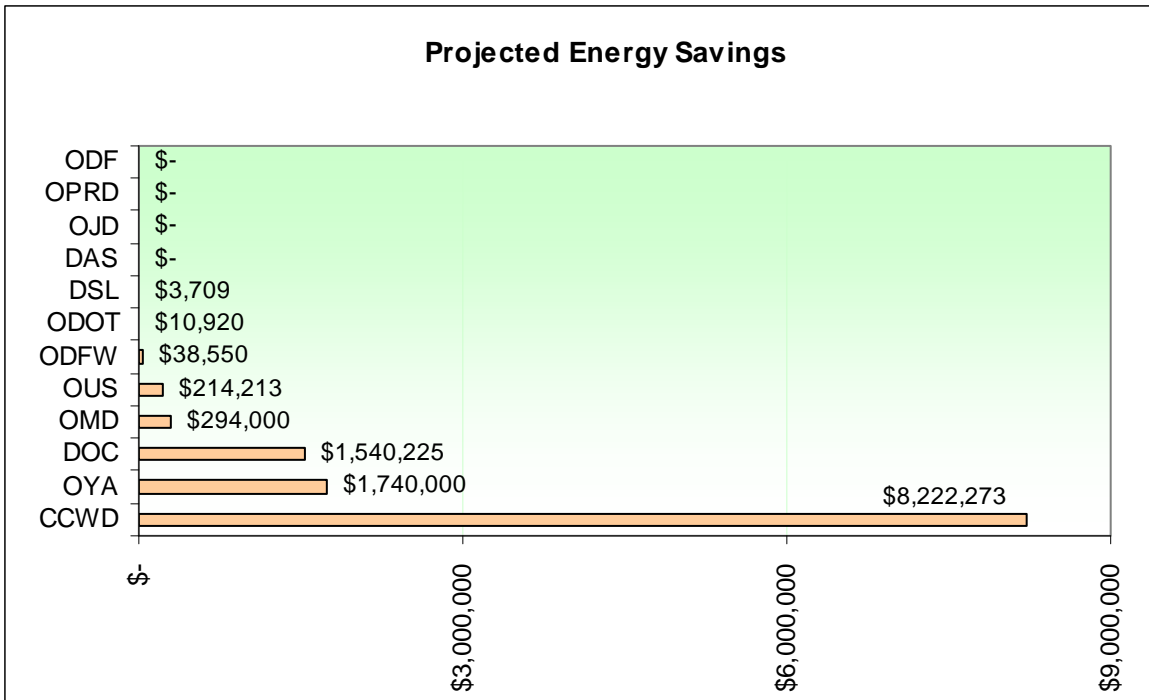


	Savings on Energy Costs for Energy Efficient Projects
CCWD	\$ 8,222,273
OYA	\$ 1,740,000
DOC	\$ 1,540,225
OMD	\$ 294,000
OUS	\$ 214,213
ODFW	\$ 38,550
ODOT	\$ 10,920
DSL	\$ 3,709
DAS	\$ -
OJD	\$ -
OPRD	\$ -
ODF	\$ -
Total	\$12,063,890

“Savings on energy costs for energy efficiency projects” represents reported savings for all agencies performing energy efficiency projects. “Savings” represents estimated energy savings over the life of the project.

Jobs by County


Jobs by County

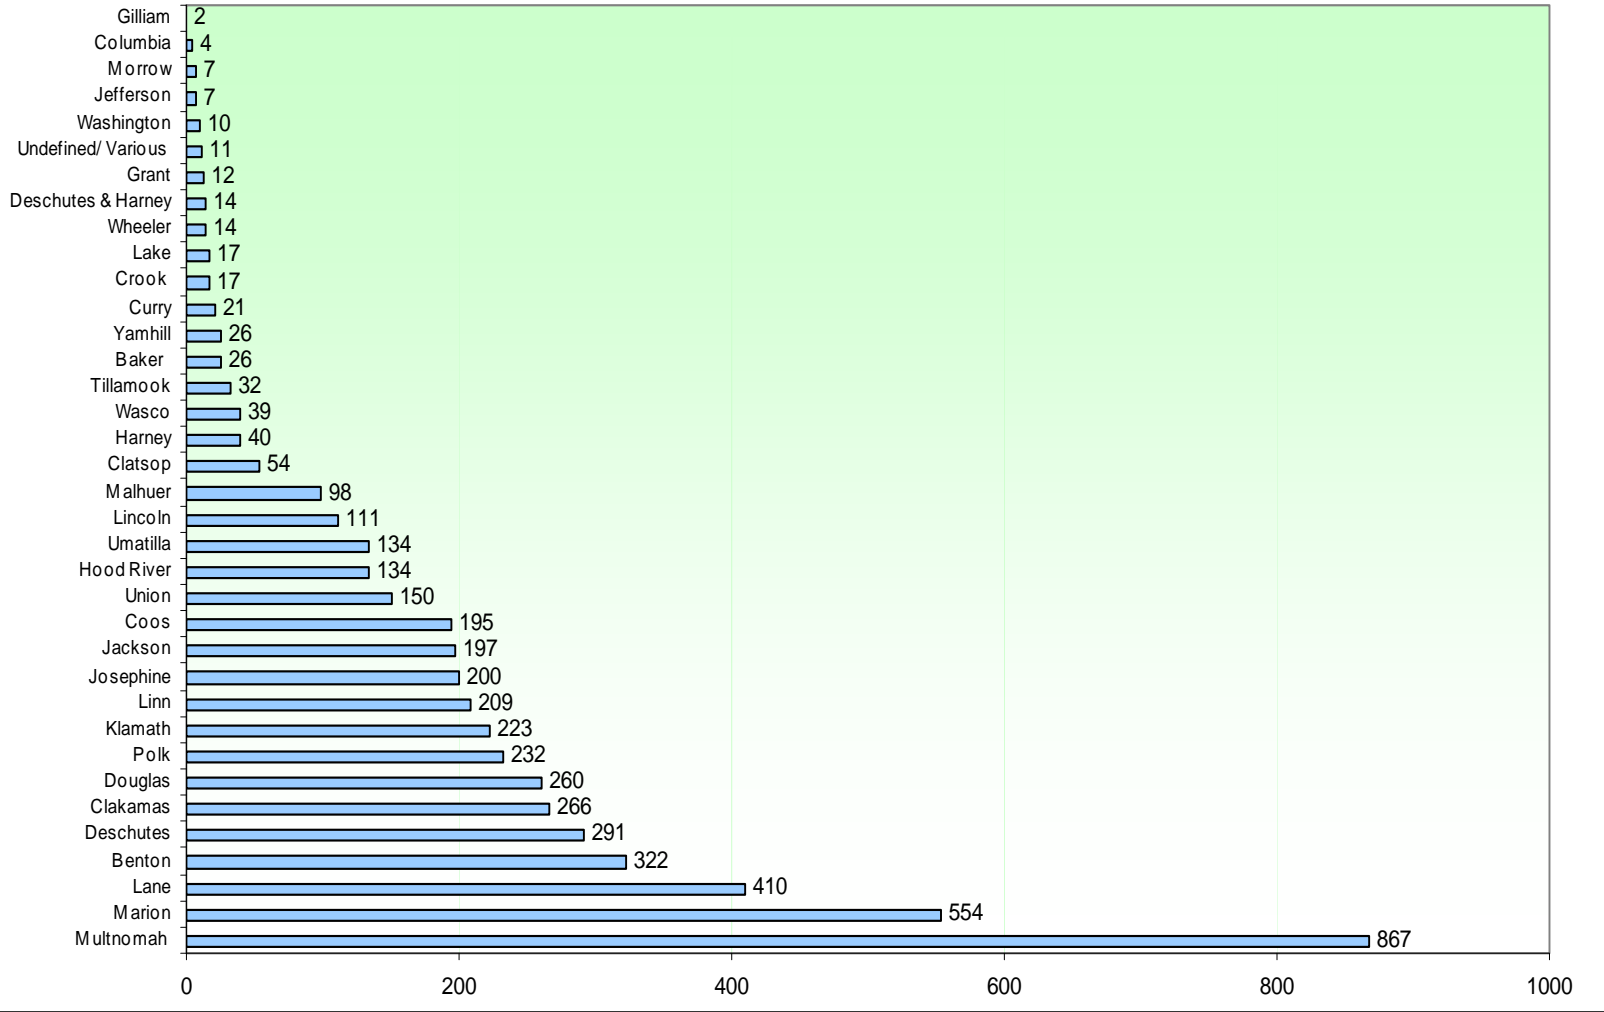

County	Jobs
Multnomah	867
Marion	554
Lane	410
Benton	322
Deschutes	291
Clakamas	266
Douglas	260
Polk	232
Klamath	223
Linn	209
Josephine	200
Jackson	197
Coos	195
Union	150
Hood River	134
Umatilla	134
Lincoln	111
Malhuer	98
Clatsop	54
Harney	40
Wasco	39
Tillamook	32
Baker	26
Yamhill	26
Curry	21
Crook	17
Lake	17
Wheeler	14
Deschutes & Harney	14
Grant	12
Undefined/ Various	11
Washington	10
Jefferson	7
Morrow	7
Columbia	4
Gilliam	2
Wallowa	2
Sherman	1

Expenditures by County

Expenditures by County

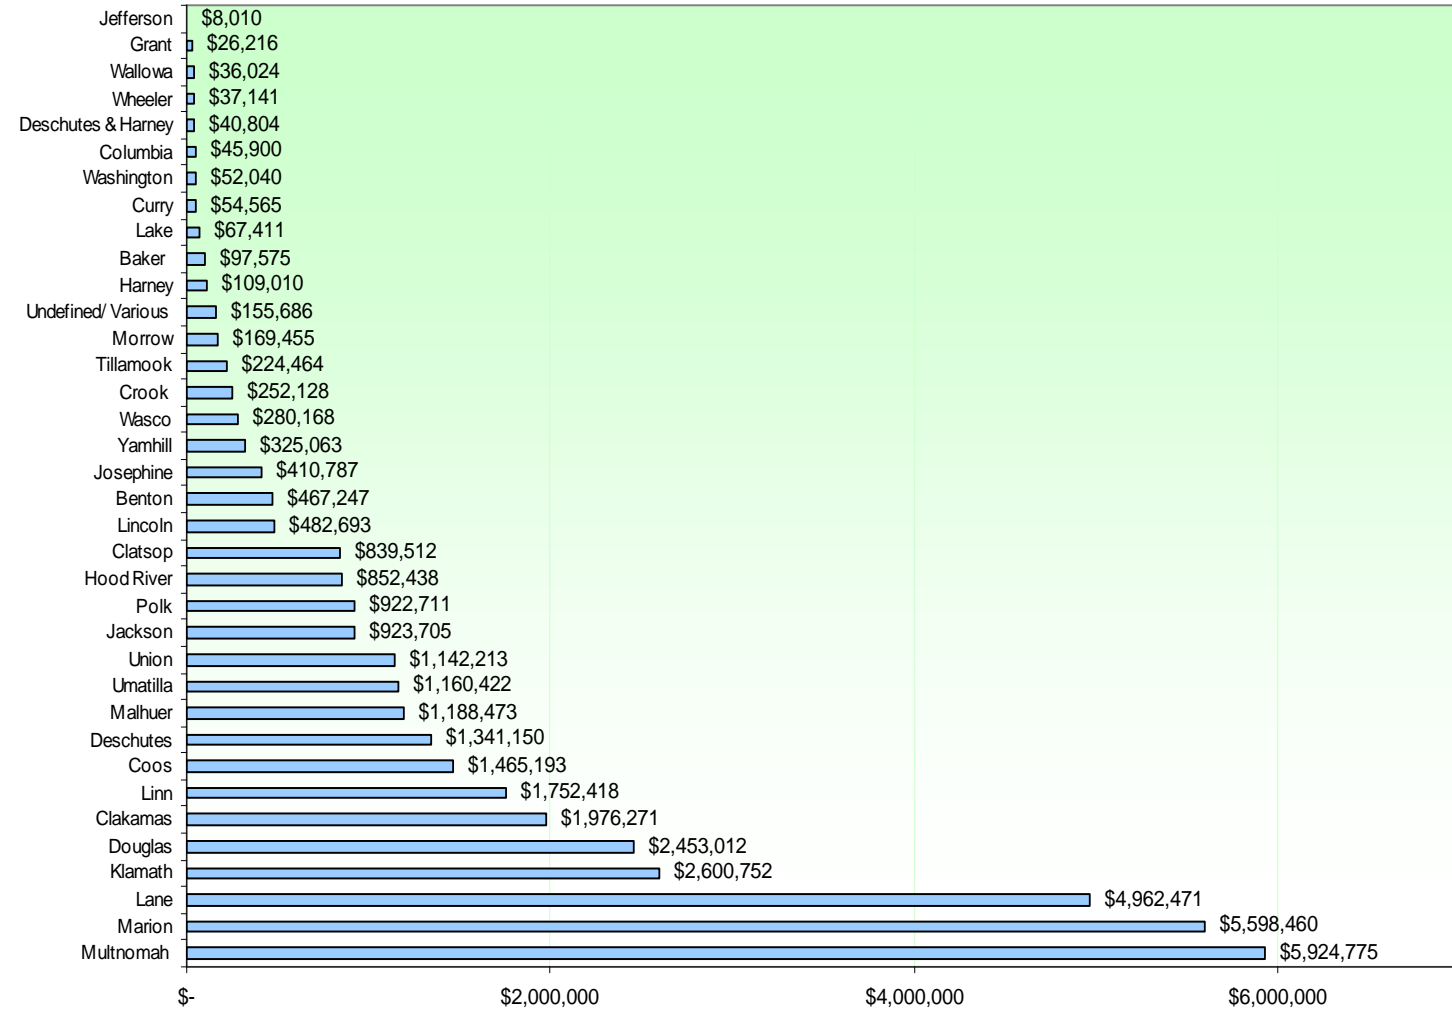

County	Dollars
Multnomah	\$ 5,924,775
Marion	\$ 5,598,460
Lane	\$ 4,962,471
Klamath	\$ 2,600,752
Douglas	\$ 2,453,012
Clakamas	\$ 1,976,271
Linn	\$ 1,752,418
Coos	\$ 1,465,193
Deschutes	\$ 1,341,150
Malhuer	\$ 1,188,473
Umatilla	\$ 1,160,422
Union	\$ 1,142,213
Jackson	\$ 923,705
Polk	\$ 922,711
Hood River	\$ 852,438
Clatsop	\$ 839,512
Lincoln	\$ 482,693
Benton	\$ 467,247
Josephine	\$ 410,787
Yamhill	\$ 325,063
Wasco	\$ 280,168
Crook	\$ 252,128
Tillamook	\$ 224,464
Morrow	\$ 169,455
Undefined/ Various	\$ 155,686
Harney	\$ 109,010
Baker	\$ 97,575
Lake	\$ 67,411
Curry	\$ 54,565
Washington	\$ 52,040
Columbia	\$ 45,900
Deschutes & Harney	\$ 40,804
Wheeler	\$ 37,141
Wallowa	\$ 36,024
Grant	\$ 26,216
Jefferson	\$ 8,010
Gilliam	\$ 1,790
Sherman	\$ 1,475



SB 338 Report August 17, 2009



DAS

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures To Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors hired	MWESB working on a project	Estimated Energy Savings (\$)
1	Central Point Carpet Replacemnet	Jackson	04/03/09	04/03/09	5	04/14/09	04/24/09	74,876	0	6	340	5	2	1	0	N/A
2	UPS Battery Replacement SDC	Marion	02/01/09	03/02/09	5	04/01/09	04/08/09	94,618	0	9	160	9	4	1	0	N/A
3	Carpet Replacement	Umatilla	04/23/09	04/23/09	3	09/15/09		-	0	0	0	0	0	0	0	N/A
4	L&I Bldg. Water Pipe Replacement.	Marion	03/12/09	03/12/09	3	08/15/09		697,930	8	11	5,441	13	12	4	0	N/A
5	Exterior Canopy- Pendleton 202	Umatilla	03/17/09	03/17/09	3	09/01/09		25,152	0	35	85	35	8	3	1	N/A
6	Chiller Replacement - Pendleton 201	Umatilla	03/17/09	03/17/09	3	09/01/09		139,981	4	10	657	8	13	4	0	N/A
7	Unfunded		UF/UA	UF/UA	0	UF/UA		-	0	0	0	0	0	0	0	
8	Unfunded		UF/UA	UF/UA	0	UF/UA		-	0	0	0	0	0	0	0	
9	Painting/Ceiling Tile/Restroom Improv.	Umatilla	03/17/09	03/17/09	3	09/01/09		187,331	2	11	929	9	12	3	0	N/A
10	PSOB Fire System Upgrade - Ph. 2	Multnomah	04/10/09	04/27/09	3	09/30/09		130,680	0	8	375	6	3	1	0	N/A
								1,350,568	14	90	7,987	85	54	17	1	-

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion
0) UF / UA
UF =Unfunded Projects UA = Unassigned Project



**SB 338 Report
August 17, 2009**



DOC

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors hired	MWESB working on a project	Estimated Energy Savings (\$)
11	Replace Freezer Lighting at CDC	Marion	05/23/09	05/11/09	3	07/15/09	7/10/09	\$ 75,243	0	2	0	2	3	0	0	N/A
12	Replace expired wireless batteries	Marion	05/23/09	07/30/09	3	11/23/09		\$ 63,640	0	0	0	0	0	0	0	N/A
13	Replace backup electrical system	Umatilla	05/15/09	04/29/09	3	11/15/09		\$ -	0	0	0	0	0	0	0	N/A
14	Install solar system	Umatilla	05/15/09	06/30/09	3	11/15/09		\$ -	0	0	0	0	0	0	0	N/A
15	Replace out of date Security System	Umatilla	06/01/09	06/25/09	3	11/01/09		\$ 124,348	0	0	0	0	0	0	0	N/A
16	Replace failing unit door control sys	Umatilla	06/01/09	06/25/09	3	06/01/10		\$ 133,971	0	0	0	0	0	0	0	N/A
17	Replace warehouse Lighting at CDC	Marion	05/23/09	05/05/09	3	09/23/09		\$ 113,620	0	0	0	0	0	0	0	N/A
18	Electrical panel upgrades	Various	06/01/09	06/08/09	3	01/01/11		\$ -	0	0	0	0	0	0	0	N/A
19	Replace electronic security network	Malhuer	06/01/09	05/13/09	3	10/01/11		\$ 330,827	0	1	0	1	0	0	0	N/A
20	Replace Lighting for energy efficiency	Various	05/15/09	05/14/09	3	10/15/11		\$ 155,002	0	0	0	0	0	0	0	N/A
								\$ 996,651	0	3	0	3	3	0	0	\$ -

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion
 0) UF / UA
 UF =Unfunded Projects UA = Unassigned Project



**SB 338 Report
August 17, 2009**



ODFW

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors hired	MWESB working on a project	Estimated Energy Savings (\$)
21	Sandy Hatchery Parking Lot Const	Clackamas	05/13/09	05/07/09	3	11/13/09		\$ 45,942	5	4	442	5	11	5	2	N/A
22	Denman Storage Bldg	Jackson	05/05/09	05/08/09	3	11/05/09		\$ 6,510	0	1	0	1	2	0	0	N/A
23	PW Schneider Storage Bldg	Grant	05/12/09	07/07/09	3	11/12/09		\$ 12,349	0	1	18	1	3	1	1	N/A
24	Sauvie Island Storage Bldg	Columbia	04/29/09	05/07/09	3	10/23/09		\$ 45,900	0	4	231	0	7	0	0	N/A
25	Enterprise District Office Elevator	Wallowa	05/12/09	05/28/09	3	01/12/10		\$ -	0	0	0	0	0	0	0	N/A
26	New Bldg at Hatfield Marine Science Ctr	Lincoln	05/28/09	06/04/09	3	02/28/10		\$ 28,968	0	3	0	3	4	4	2	N/A
27	Hatchery Repair Storage Bldg	Linn	05/09/09	04/09/09	5	07/09/09	05/30/09	\$ 8,368	0	1	0	1	3	0	0	N/A
28	McKenzie Hatchery ADA Sidewalk	Lane	04/30/09	04/13/09	5	05/30/09	04/30/09	\$ 8,536	0	5	248	5	9	2	1	N/A
29	Alesea Hatchery Domestic Well Building	Benton	04/23/09	04/02/09	5	05/30/09	06/26/09	\$ -	4	6	175	8	5	1	0	N/A
30	EE Wilson Wildlife Area Heat Pump	Benton	04/16/09	04/01/09	5	04/16/09	04/16/09	\$ 6,933	0	2	44	2	3	1	0	\$ 38,550
31	Summer Lake Wildlife Area New Well	Lake	05/14/09	04/20/09	5	08/14/09	06/04/09	\$ 26,849	0	6	173	6	13	0	0	N/A
32	Salmon River Hatchery Heat Pumps	Lincoln	05/14/09	05/01/09	5	07/14/09	06/11/09	\$ 8,628	2	9	39	10	4	0	0	N/A
33	District Office Replace Electric	Benton	05/12/09	05/07/09	3	08/12/09		\$ 19	0	4	96	4	1	0	0	N/A
34	HVAC System Upgrade	Douglas	05/11/09	06/16/09	3	07/11/09		\$ 18,624	0	9	90	5	4	1	0	N/A
35	Hatchery Electrical Panel Upgrade	Hood River	05/12/09	05/11/09	5	07/12/09	06/26/09	\$ -	0	4	131	2	2	0	1	N/A
36	Electrical Service and Panel Upgrade	Hood River	05/12/09	05/04/09	5	07/12/09	06/19/09	\$ 116	0	3	282	3	5	3	0	N/A
37	Pump Station Electrical Upgrades	Douglas	05/12/09	No Date	1	12/12/09		\$ -	0	0	0	0	0	0	0	N/A
38	Hatchery Pond Bottom Resurfacing	Lane	05/12/09	05/07/09	5	07/12/09	06/23/09	\$ -	4	2	359	6	8	0	1	N/A
39	Hatchery Supply Pipeline Replacement	Douglas	04/30/09	05/11/09	3	10/30/09		\$ -	0	5	406	5	4	0	0	N/A
40	Salmon River Hatchery New Residence	Lincoln	05/13/09	05/08/09	3	11/13/09		\$ 137	4	0	161	4	6	2	1	N/A
41	Wildlife Area Residence Replacement	Benton	05/01/09	04/14/09	5	11/05/09	07/01/09	\$ 51,740	51	9	526	32	33	17	1	N/A
42	Foundation Settlement Repair	Clackamas	05/08/09	05/12/09	3	05/08/10		\$ -	0	5	0	5	7	7	0	N/A
43	Hatchery Supply Pipeline Replacement	Clatsop	05/12/09	05/14/09	3	08/12/09		\$ 65,418	2	3	462	5	9	1	0	N/A
44	Dam Removal Project	Grant	05/22/09	06/12/09	3	05/22/10		\$ 33	0	4	0	4	7	3	1	N/A
								\$ 335,071	72	90	3,883	117	150	48	11	\$ 38,550

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion
0) UF / UA
UF =Unfunded Projects UA = Unassigned Project



SB 338 Report August 17, 2009



ODF

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
45	Warehouse Columns	Grants Pass	Cancelled	Cancelled	6	Cancelled	Cancelled	\$ -	0	0	0	0	0	0	0	N/A
46	Unfunded		UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
47	Repair int lighting & service panel Oil Hs	Prineville	05/15/09	05/13/09	5	06/15/09	06/26/09	\$ 1,500	0	2	13	2	3	0	1	N/A
48	Repair interior lighting Whs & Mach Stor	Prineville	05/15/09	05/13/09	5	06/15/09	06/26/09	\$ 3,120	0	2	27	2	3	0	1	N/A
49	Replace vinyl flooring, refinish casewk	Springfield	05/01/09	05/08/09	5	07/31/09	07/31/09	\$ 16,519	0	5	127	5	1	0	0	N/A
50	Replace siding, repaint Storage Shed	Veneta	05/15/09	05/11/09	5	08/15/09	05/29/09	\$ 4,300	0	5	26	5	3	0	0	N/A
51	Unfunded		UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
52	Replace siding, repaint Woodwork Shop	Veneta	Cancelled	Cancelled	6	Cancelled	Cancelled	\$ -	0	0	0	0	0	0	0	N/A
53	Replace worn carpeting HQ Office	Philomath	04/01/09	04/01/09	5	06/15/09	06/05/09	\$ 11,971	0	5	80	5	1	0	0	N/A
54	Replace worn carpeting Unit Office	Dallas	04/01/09	04/01/09	5	06/01/09	05/15/09	\$ 9,729	0	5	56	5	1	0	0	N/A
55	Replace worn carpeting HQ Office	Toledo	04/01/09	04/01/09	5	06/01/09	05/29/09	\$ 6,300	0	5	60	5	1	0	0	N/A
56	Replace Siding, Repaint Equip. Shed	Veneta	Cancelled	Cancelled	6	Cancelled	Cancelled	\$ -	0	0	0	0	0	0	0	N/A
57	Replace electrical distribution & service	Klamath Falls	05/15/09	05/14/09	3	10/30/09		\$ 4,705	2	0	45	2	2	0	0	N/A
58	Repair soffits at loading dock	Elkton	06/01/09	04/30/09	3	11/01/09		\$ 4,126	0	4	9	4	1	1	1	N/A
59	Replace siding, repaint ODFW office	Tillamook	06/01/09	05/12/09	3	10/01/09		\$ 20,464	5	3	435	6	3	0	1	N/A
60	Repaint, replace ceilings	Elkton	06/01/09	04/30/09	3	11/01/09		\$ 13,927	0	4	32	4	1	1	1	N/A
61	Replace siding, repaint Warehouse	Veneta	05/15/09	05/11/09	5	08/15/09	07/31/09	\$ 53,636	1	6	533	6	9	4	0	N/A
62	Replace roof and structural repairs	Elkton	06/01/09	04/30/09	3	12/01/09		\$ 33,529	0	4	76	4	1	1	1	N/A
63	John Day/Sisters Relocation Project	John Day	03/24/09	03/24/09	3	06/01/11		\$ 60,370	0	12	60	12	6	2	1	N/A
								\$ 244,196	8	62	1,579	67	36	9	7	\$ -

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion
0) UF / UA
UF =Unfunded Projects UA = Unassigned Project



**SB 338 Report
August 17, 2009
OUS**



Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
64	Owens Hall Comprehensive Renovation	Klamath	04/23/09	04/15/09	3	10/30/09		\$ 751,789	19	70	5,683	89	44	11	1	N/A
65	Campus Loop Phase II	Multnomah	02/11/09	02/11/09	3	10/01/10		\$ 378,256	0	16	0	15	7	5	0	\$ 214,113
66	Unassigned		UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
67	Phys. Ed Building	Polk	02/24/09	04/15/09	3	01/04/11		\$ 5,861	16	8	764	8	1	0	0	N/A
68	Office/Lab Bldg-Rpl Front Entry Door	Jefferson	04/30/09	04/29/09	3	07/12/09		\$ 2,570	0	1	16	1	1	0	1	N/A
69	Lab - Insulate Building	Harney	04/30/09	04/28/09	3	07/12/09		\$ -	0	0	0	0	0	0	0	N/A
70	Office/Lab Building - Replace Gutters	Jefferson	04/30/09	04/30/09	3	07/12/09		\$ 450	0	3	0	3	3	0	1	N/A
71	Baccus Garden Fence		UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
72	Replace Double Doors - Basement	Hood River	04/30/09	04/24/09	3	07/12/09		\$ -	0	2	13	2	1	0	0	N/A
73	Cold Storage - Replace Gutters	Hood River	04/30/09	04/30/09	3	07/12/09		\$ -	0	0	0	0	0	0	0	N/A
74	Gen Lighting -Lighting/Energy Upgrade	Sherman	05/04/09	05/04/09	3	07/12/09		\$ 1,475	0	1	7	1	1	0	0	N/A
75	Storage Garage		UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
76	Seafood Reasearch Center - Unfunded		Cancelled	Cancelled	6	Cancelled	Cancelled	\$ -	0	0	0	0	0	0	0	N/A
77	Office Lab Building--Repaint Exterior		UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
78	Gravel Access Drives--Regravel Drives		UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
79	Office/Lab Bldg-Repr Work Room Cabinets	Jefferson	04/30/09	04/30/09	3	07/12/09		\$ 4,990	0	3	31	3	4	1	0	N/A
80	Gravel Access Drives--Regravel Drives		UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
81	Potato Storage Refurb Heating System		UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
82	Office/Shop Refurbish Heating System		UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
83	Seafood Research Center Repair Windows		UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
84	Waste - Refurbish Waste Collection Area	Harney	04/30/09	04/28/09	3	07/12/09		\$ -	0	0	0	0	0	0	0	N/A
85	Gravel Access Drives--Regravel		UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
86	Truck Scale - Replace Overhead Door	Harney	04/30/09	04/28/09	3	07/12/09		\$ -	0	0	0	0	0	0	0	N/A
87	Truck Scale-Replace Sliding Door	Harney	04/30/09	04/28/09	3	07/12/09		\$ 800	0	2	0	2	0	0	0	N/A
88	HVAC upgrade-CPS	Jackson	04/13/09	04/13/09	5	04/30/09	04/30/09	\$ 10,907	2	2	117	3	2	1	0	N/A
89	Campus-Add ADA Path to Softball	Polk	03/02/09	03/10/09	5	03/31/09	03/13/09	\$ 6,817	0	8	62	8	1	0	0	N/A
90	SRC - Repair Perchloric Duct/Hood		UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
91	Door Access Control-classrooms	Jackson	05/18/09	04/27/09	5	06/17/09	05/18/09	\$ 22,774	0	7	112	6	1	0	0	N/A
92	Fire Alarm System-Art East	Jackson	04/27/09	04/27/09	5	05/27/09	06/19/09	\$ 8,779	0	3	29	3	3	1	0	N/A
93	Fire Alarm System-ECP	Jackson	04/28/09	04/27/09	5	05/28/09	06/19/09	\$ 11,431	0	3	37	3	3	1	0	N/A
94	Access Drives--Add Gravel		UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
95	Access Drives-Refurbish 8 Cattle Guards	Harney	04/30/09	04/23/09	3	07/12/09		\$ 12,266	2	3	213	5	10	1	3	N/A
96	Hay Barn-Repair Poles		UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
97	Irrigation Mainline - Refurbish	Harney	04/30/09	04/23/09	3	07/12/09		\$ -	0	0	0	0	0	0	0	N/A

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MMWESB working on a project	Estimated Energy Savings (\$)
98	Lab - Re-Side/Paint Building Exterior	Harney	04/30/09	04/28/09	3	07/12/09		\$ -	0	0	0	0	0	0	0	N/A
99	Door Access Control-Theatre	Jackson	05/18/09	04/27/09	5	06/17/09	05/18/09	\$ 23,665	0	7	92	6	1	0	0	N/A
100	Variable Frequency Drive	Jackson	04/20/09	04/22/09	5	05/04/09	06/30/09	\$ 17	0	1	0	1	2	1	1	N/A
101	Dipping Vat Building - Refurbish	Harney	04/30/09	04/28/09	3	07/12/09		\$ -	0	0	0	0	0	0	0	N/A
102	Metabolism Barn-Repl Overhead Doors	Harney	04/28/09	04/28/09	3	06/28/09		\$ 1,050	0	2	0	2	0	0	0	N/A
103	Line Fence - Re-Place Line Fence	Hood River	04/30/09	04/30/09	3	07/12/09		\$ 257	1	2	39	3	1	0	1	N/A
104	Rain Gutters	Lincoln	04/07/09	04/01/09	5	06/07/09	04/20/09	\$ 10,846	0	2	92	2	1	0	1	N/A
105	Seafood Research Ctr-Replace Boiler	Clatsop	12/26/08	12/26/08	5	01/05/09	01/05/09	\$ 34,370	0	3	115	3	7	0	0	N/A
106	Seafood Research Ctr-Refinish Ext Siding	Clatsop	05/26/09	04/29/09	3	07/26/09		\$ 8,920	0	2	248	2	3	0	0	N/A
107	Dock - Replace Floats	Lincoln	02/01/09	02/01/09	5	02/28/09	02/15/09	\$ 25,000	0	4	60	4	2	0	0	N/A
108	Corral - Re-Place Corral & Waterers	Harney	04/30/09	04/27/09	3	07/12/09		\$ 7,256	0	0	0	0	0	0	0	N/A
109	Equipment Shed - Re-Roof	Hood River	04/30/09	04/29/09	3	07/26/09		\$ 13,500	1	3	0	4	3	2	0	N/A
110	Door Access Control-Britt	Jackson	05/18/09	04/27/09	5	06/17/09	05/18/09	\$ 18,306	0	7	72	6	1	0	0	N/A
111	Door Access Library	Jackson	05/18/09	04/27/09	5	06/17/09	05/18/09	\$ 15,580	0	7	76	6	1	0	0	N/A
112	Fire Alarm System Replacement	Jackson	05/04/09	04/27/09	3	06/03/09		\$ 1,360	0	5	4	5	4	2	1	N/A
113	Equipment Shed - Reroof	Hood River	04/30/09	04/24/09	3	07/26/09		\$ -	0	0	0	0	0	0	0	N/A
114	Elevator Upgrade-CH	Jackson	04/20/09	04/17/09	5	05/20/09	06/18/09	\$ 57,641	0	7	676	6	5	3	1	N/A
115	Elevator Upgrade-EP	Jackson	05/04/09	04/17/09	3	06/03/09		\$ 36,432	0	7	54	6	5	3	1	N/A
116	Lab - Refurbish HVAC System	Harney	05/13/09	05/13/09	3	07/12/09		\$ 640	0	0	0	0	1	1	0	N/A
117	Refurb Chem Storage/Mixing Area	Hood River	04/30/09	04/29/09	3	07/12/09		\$ -	0	0	0	0	0	0	0	N/A
118	HVAC Upgrade MN	Jackson	06/15/09	04/30/09	3	08/14/09		\$ 50	0	2	0	2	2	1	1	\$ 100
119	Rice-Replace Motors w/ High Eff., VFD	Polk	04/22/09	04/22/09	3	08/31/09		\$ 24,030	0	5	146	5	1	0	0	N/A
120	Expanded Digital Control	Klamath	03/13/09	04/15/09	3	08/15/09		\$ 41,303	0	4	82	4	1	0	0	N/A
121	Exterior Lighting	Jackson	06/15/09	04/20/09	5	07/30/09	06/24/09	\$ 31,338	0	4	628	4	3	1	0	N/A
122	Exterior Door and Hardware Replacement	Lincoln	04/30/09	02/16/09	3	07/12/09		\$ 6,036	0	5	0	5	1	1	0	N/A
123	Drying Bldg - Refurbish Chem Storage	Harney	05/01/09	05/01/09	3	07/26/09		\$ 1,852	3	2	44	5	9	2	0	N/A
124	Roof replacement-CE	Jackson	06/15/09	04/16/09	3	07/15/09		\$ 4,596	0	6	0	6	1	0	1	N/A
125	Storm Water drainage Improvements	Jackson	06/15/09	04/22/09	5	07/15/09	07/06/09	\$ 21,735	0	4	273	3	2	0	0	N/A
126	Office - ADA Access & Refurbish Siding	Hood River	04/30/09	04/28/09	3	07/26/09		\$ 6,141	1	6	383	7	16	9	1	N/A
127	Roof Replacement-Music	Jackson	06/15/09	04/30/09	3	07/30/09		\$ 55,465	0	4	0	4	3	1	2	N/A
128	Theatre Roof Replacement	Jackson	06/15/09	04/15/09	5	08/15/09	07/30/09	\$ 137,787	7	10	836	13	3	0	1	N/A
129	Campbell-convert from steam to hydronics	Polk	04/22/09	04/22/09	3	08/31/09		\$ 37,574	2	0	146	2	8	2	1	N/A
130	Parking lot paving	Lincoln	04/30/09	04/14/09	3	07/26/09		\$ 10,869	0	9	370	9	12	5	0	N/A
131	Extension Office - Refurbish	Hood River	04/30/09	04/24/09	3	07/12/09		\$ 1,277	0	3	82	3	4	1	0	N/A
132	Learning Resources Ctr: Interior Finishes	Klamath	03/16/09	04/02/09	3	07/01/09		\$ 123,593	0	5	125	5	2	1	1	N/A
133	Fire Alarm System replacement	Jackson	05/04/09	04/27/09	3	06/03/09		\$ 2,711	0	5	11	5	4	2	1	N/A
134	Classroom Modernization CH	Jackson	06/08/09	04/27/09	3	08/30/09		\$ 50,476	6	15	385	18	27	13	1	N/A
135	Toilet Upgrades-Science Bldg	Jackson	06/15/09	04/30/09	3	08/14/09		\$ 33,673	0	5	359	5	10	6	1	N/A

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MMWESB working on a project	Estimated Energy Savings (\$)
136	Code & Safety Compliance Improvements	Lane	06/15/09	03/30/09	3	11/27/09		\$ 72,396	0	7	713	7	2	0	7	N/A
137	Roof replacement McNeal	Jackson	06/15/09	04/30/09	3	08/14/09		\$ 66,309	0	7	208	7	3	1	1	N/A
138	Replacement Direct Burial 12,000V Elec.	Klamath	04/15/09	04/15/09	3	10/15/09		\$ 163,940	0	12	1,085	12	8	2	1	N/A
139	Boiler replacement phase 2	Jackson	06/01/09	04/30/09	3	08/30/09		\$ 100,475	0	13	701	13	10	8	0	N/A
140	Seismic Upgrades	Lincoln	04/30/09	04/19/09	3	09/30/09		\$ 7,701	1	5	229	6	4	3	0	N/A
141	Exterior Building Repairs	Lane	06/16/09	04/06/09	3	09/15/09		\$ 332,073	3	36	2,949	39	30	7	1	N/A
142	Replace plumbing building 900	Lincoln	04/30/09	04/28/09	3	08/15/09		\$ 22,236	0	12	9	12	6	4	0	N/A
143	0143-Renov Labs in Ed Wing-HMSC	Lincoln	04/30/09	04/13/09	3	08/01/09		\$ 20,800	0	4	75	4	4	2	1	N/A
144	Strand Ag 1st Floor SE Bathrooms/Lab	Benton	05/07/09	05/07/09	3	01/01/10		\$ -	0	0	0	0	0	0	0	N/A
145	Gill Coliseum - exterior paint	Benton	04/30/09	12/15/08	3	07/04/09		\$ 84,175	15	89	316	82	10	1	0	N/A
146	AB Acad. Modern. & Access.	Multnomah	02/11/09	02/11/09	3	11/01/09		\$ 297,199	0	13	1,769	11	17	8	2	N/A
147	Electrical Upgrades and Replacements	Lane	04/30/09	04/13/09	3	11/20/09		\$ 144,193	0	5	317	5	6	1	0	N/A
148	Programmatic Modifications	Lane	04/30/09	04/13/09	4	11/15/09		\$ 29,658	0	2	0	2	0	0	0	N/A
149	Seawater system effluent treatment	Lincoln	04/30/09	04/27/09	3	07/15/09		\$ 54,004	2	14	206	13	12	3	1	N/A
150	Mechanical Upgrades and Replacements	Lane	06/16/09	04/13/09	3	01/31/10		\$ 28,442	0	2	19	2	3	1	0	N/A
151	Pierce Library Roof Repair / Replacement	Union	04/14/09	04/17/09	5	09/15/09		\$ 107,511	0	7	0	7	2	0	0	N/A
152	Roof Replacement, Owens, Semon, Boivin	Klamath	04/15/09	04/03/09	3	07/15/09		\$ 459,012	3	7	2,000	8	1	0	2	N/A
153	Deferred Interior Finish Replacements	Lane	04/13/09	04/06/09	3	01/31/10		\$ 415,648	2	29	2,627	31	8	4	2	N/A
154	Dorion Hall Demolition & Site Improvements	Union	04/14/09	04/17/09	3	09/15/09		\$ 627,406	36	28	7,372	26	11	3	1	N/A
155	Academic Modernization	Klamath	04/30/09	04/15/09	3	09/15/09		\$ 111,926	0	19	254	19	20	10	0	N/A
156	NH Acad Modernization and Accessibility	Multnomah	03/31/09	03/31/09	3	10/31/09		\$ 116,331	7	43	3,040	41	24	12	4	N/A
157	CH Classroom Upgrades	Multnomah	04/01/09	04/01/09	3	10/31/09		\$ 189,998	11	48	2,258	46	41	13	7	N/A
158	Campus-Steamline Phase II	Polk	04/30/09	04/20/09	3	09/15/09	09/15/09	\$ 173,676	0	15	841	11	15	3	7	N/A
159	LH Academic & Program Improvements	Multnomah	03/30/09	03/23/09	3	10/31/10		\$ 117,716	7	58	2,027	32	18	9	1	N/A
160	Strand Ag-Bldg repipe/upgrade plumbing	Benton	05/07/09	05/07/09	3	01/01/10		\$ 50,020	1	28	801	24	25	4	1	N/A
161	Waldo Hall - 4th floor renovation	Benton	03/25/09	03/25/09	3	01/01/10		\$ 10,571	0	7	803	7	1	0	0	N/A
162	Campus Roof Repair and Replacement	Multnomah	04/01/09	03/30/09	3	11/30/09		\$ 935,893	5	60	5,435	54	34	8	2	N/A
163	E&G Bldg. Code, Life Safety Improvements	Multnomah	04/01/09	04/01/09	3	10/31/09		\$ 343,634	6	66	6,235	63	70	31	17	N/A
164	Reed Hall-Sys Upgrades & Renov	Benton	02/26/09	02/26/09	3	10/01/09		\$ 26,340	1	24	758	25	3	2	2	N/A
165	Heckart Hall-Sys Upgrades & Renov	Benton	12/31/08	12/31/08	3	04/01/10		\$ 225,480	1	75	1,118	72	1	0	1	N/A
166	Science Building 2 Modernization	Multnomah	03/01/08	03/26/08	3	04/01/10		\$ 274,988	2	8	28	9	8	1	1	N/A
167	Health & Wellness Center	Polk	02/24/09	04/15/09	3	01/04/11	12/31/06	\$ 87,696	38	13	407	29	7	2	1	N/A
168	Classroom, Office Bldg	Polk	02/24/09	04/15/09	3	01/04/11		\$ 68,644	53	27	616	45	7	2	1	N/A
								\$ 7,830,602	254	1,068	57,698	1,077	639	223	87	\$ 214,213

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion
0) UF / UA
UF =Unfunded Projects UA = Unassigned Project



**SB 338 Report
August 17, 2009**



OJD

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
169	Supreme Court Re-Roofing Project	Marion	04/24/09	04/27/09	3	09/30/09		\$ 358,208	2	28	1,857	30	16	3	1	N/A

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion
 0) UF / UA
 UF =Unfunded Projects UA = Unassigned Project



SB 338 Report August 17, 2009



OMD

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
170	Hillsboro Armory Storage Building	Washington	05/01/09	04/29/09	5	06/26/09		\$ 28,895	0	7	140	7	11	5	1	N/A
171	Roseburg Armory Floor Replacement	Douglas	04/24/09	04/23/09	5	06/14/09		\$ 37,525	3	6	246	6	1	1	1	N/A
172	Hermiston HVAC For Drill Floor	Umatilla	05/04/09	04/27/09	3	06/22/09		\$ 131,227	0	10	215	10	4	2	0	N/A
173	COUTES - Restroom Remodel	Deschutes	05/01/09	04/30/09	3	08/02/09		\$ 84,320	8	6	1,908	8	14	5	6	N/A
174	LaGrande Armory Back Up Generator	Union	05/01/09	04/30/09	5	07/10/09		\$ 127,452	2	43	469	43	5	2	4	N/A
175	Bend Armory Back Up Generator	Deschutes	05/01/09	04/20/09	5	07/17/09		\$ 73,012	0	43	554	43	5	2	1	N/A
176	Camp Withycombe Bld.6101 Reroof	Clackamas	05/04/09	04/27/09	3	08/01/09		\$ 564,482	0	14	824	12	6	2	0	N/A
177	Salem Armory Floor Tile Replacement	Marion	04/28/09	04/27/09	3	06/22/09		\$ 105,711	13	12	0	12	2	1	0	N/A
178	Jackson Armory Door Replacement	Multnomah	04/13/09	04/13/09	3	06/05/09		\$ 69,412	0	20	129	9	9	3	2	\$ 30,000
179	Camp Rilea Replace Roofing & Siding	Clatsop	05/04/09	04/21/09	3	08/14/09		\$ 55,830	0	1	350	1	5	2	1	\$ 25,000
180	Hood River Armory Storage Building	Hood River	05/01/09	04/20/09	3	08/29/09		\$ 519,059	0	15	843	6	10	6	0	\$ 45,000
181	Armory Parking Lot Upgrade	Josephine	05/01/09	04/30/09	3	06/22/09		\$ 154,538	0	20	959	20	7	3	0	N/A
182	Kleiver Armory Parking Lot Upgrade	Multnomah	05/01/09	04/29/09	5	07/29/09	07/20/09	\$ 147,463	0	14	623	12	2	1	1	N/A
183	Armory Compound Improvem'ts	Hood River	05/01/09	04/30/09	5	06/29/09	06/29/09	\$ 215,203	0	17	755	16	6	2	1	N/A
184	Hood River Armory Interior Remodel	Hood River	05/01/09	04/30/09	3	10/29/09		\$ 91,116	28	46	1,825	36	38	14	2	N/A
185	Blak Restroom & Shower Facility	Crook	05/01/09	05/01/09	3	10/28/09		\$ 245,275	7	6	999	6	24	10	0	N/A
186	Coos Bay Armory - Interior Remodel	Coos	05/01/09	05/01/09	3	07/29/09		\$ 505,023	0	28	1,685	28	15	10	0	\$ 50,000
187	Prineville CORC - Interior Remodel	Crook	06/15/09	08/04/09	3	No Date		\$ 2,233	0	0	0	0	0	0	0	\$ 144,000
								\$ 3,157,775	61	308	12,524	275	164	71	20	\$ 294,000

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion 0) UF /
 UA
 UF =Unfunded Projects UA = Unassigned Project



**SB 338 Report
August 17, 2009**



OPRD

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
188	Beverly Beach S.P. Playground	Lincoln	01/30/09	01/02/09	5	05/20/09	05/29/09	\$ 29,932	0	6	156	6	3	0	0	N/A
189	Tumalo State Park Playground	Deschutes	04/30/09	02/05/09	5	05/31/09	04/17/09	\$ 21,760	0	15	16	9	5	4	0	N/A
190	Arizona Beach SP Restroom	Curry	04/30/09	02/05/09	3	08/30/09		\$ 40,425	0	18	193	2	3	1	0	N/A
191	Carl Washburn SP Paving	Lane	04/06/09	02/05/09	5	04/20/09	04/28/09	\$ 145,172	0	10	750	10	3	3	0	N/A
192	Bullards Beach SP Paving	Coos	04/30/09	02/05/09	5	05/15/09	05/28/09	\$ 159,140	0	10	815	10	2	2	0	N/A
193	Wallowa Lake SP Docks	Wallowa	04/30/09	02/05/09	3	08/30/09		\$ 36,024	0	2	1,050	2	0	0	0	N/A
194	Sarah Helmick SP Paving	Polk	04/30/09	02/05/09	5	05/15/09	05/22/09	\$ 140,794	0	8	700	8	2	2	0	N/A
195	Champoeg SP Restroom	Marion	04/06/09	01/02/09	5	05/31/09	05/21/09	\$ 356,041	0	76	900	25	3	0	0	N/A
								\$ 929,288	0	145	4,580	72	21	12	0	\$ -

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion
0) UF / UA
UF =Unfunded Projects UA = Unassigned Project



**SB 338 Report
August 17, 2009**



DSL

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
196	fence removal	Deschutes	4/10/09	No Date	5	8/31/09	4/11/09	\$ 9,600	0	3	0	3	0	0	0	N/A
197	juniper removal	Deschutes/Harney	4/8/09	4/2/09	5	10/31/09	6/30/09	\$ 40,804	4	10	0	10	2	0	0	N/A
198	Portland Harbor Boundary Survey	Multnomah	6/8/09	6/8/09	3	6/1/10		\$ 6,920	0	10	109	10	0	0	0	N/A
199	Chiller Replacement	Marion	3/19/09	4/24/09	5	6/30/09	6/30/09	\$ 160,123	0	6	8	6	5	2	2	\$ 3,709
								\$ 217,447	4	29	117	29	7	2	2	\$ 3,709

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion
0) UF / UA
UF =Unfunded Projects UA = Unassigned Project



SB 338 Report August 17, 2009



ODOT

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
200	93rd SE Yamhill Air Monitor Station Door	Multnomah	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
201	Salem Building U Replace OH Door	Marion	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
202	Santiam River SB Replace Locks	Marion	03/23/09	03/24/09	5	03/30/09	03/30/09	\$ 359	0	1	8	1	0	0	1	N/A
203	Sweet Home MS Roof Moss Treatment	Linn	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
204	Soda Mt. MW Bldg Seal Roof Vents/Elec	Jackson	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
205	Reedsport MS Replace Shingles, Door	Douglas	Cancelled	Cancelled	6	Cancelled	Cancelled	\$ -	0	0	0	0	0	0	0	N/A
206	Baker City OSP Office Exterior Repairs	Baker	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
207	Humbug MS Install Elect Outlets	Clatsop	03/04/09	03/04/09	5	03/04/09	03/06/09	\$ 1,207	0	1	10	1	1	0	0	N/A
208	SRA Replace Door and Gutter	Baker	03/31/09	03/31/09	5	05/22/09	06/15/09	\$ 3,850	0	2	56	2	2	0	1	N/A
209	Moro MS Deferred Maintenance	Sherman	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
210	Corvallis MS Replace Window Panes	Benton	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
211	Rocky Point Scale Misc Repairs	Multnomah	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
212	Seaside MS Replace O/H Dorr Panels	Clatsop	04/27/09	05/01/09	5	06/15/09	06/08/09	\$ 3,002	1	1	8	2	1	0	0	N/A
213	District 13 Office Secure Crawl Space	Union	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
214	Elgin MS Bldg Replace Flooring	Union	05/01/09	05/01/09	5	06/05/09	05/30/09	\$ 5,500	0	2	24	2	2	0	0	N/A
215	Manning MS Stor C Doors	Washington	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
216	Baker City MS Repair Roof	Baker	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
217	Condon MS Replace Garage Door	Gilliam	04/15/09	No Date	5	04/17/09	04/17/09	\$ 1,790	0	2	6	2	3	1	0	N/A
218	Salem MS Replace Window Flooring	Marion	05/01/09	05/01/09	4	07/20/09		\$ -	0	0	0	0	0	0	0	N/A
219	Astoria DMV Repair Roof Damage	Clatsop	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
220	C. Reynolds Repair Water Line/Boring	Union	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
221	Fall River Scoop Shed Metal Siding	Deschutes	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
222	Farewell Bend POE Repair Siding	Malheur	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
223	I5-228 Sand Shed Siding Repairs	Linn	04/03/09	04/02/09	5	04/08/09	04/10/09	\$ 1,506	0	1	32	1	2	0	0	N/A
224	Salem Signal Bldg Replace Carpet	Marion	05/01/09	05/01/09	5	06/15/09	05/16/09	\$ 6,493	0	10	32	10	4	1	1	N/A
225	Walterville Scale Gutters Paneling ADA	Lane	04/06/09	No Date	5	05/01/09	04/24/09	\$ 2,311	1	1	40	0	0	0	0	N/A
226	Sisters Scale Hs Window/Roof	Deschutes	03/17/09	03/17/09	5	03/18/09	03/18/09	\$ 1,108	0	1	9	1	4	0	1	N/A
227	Baker City Scale House Replace Roof	Baker	04/07/09	04/09/09	5	04/01/09	04/14/09	\$ 4,813	1	5	48	4	3	1	0	N/A
228	McMinnville MS Replace N Window	Yamhill	04/13/09	No Date	5	06/01/09	05/29/09	\$ 8,786	0	1	47	1	2	0	1	N/A
229	Woodburn POE Deferred Maintenance	Marion	04/20/09	No Date	5	04/25/09	04/18/09	\$ 6,270	0	5	64	5	6	5	0	N/A
230	Brothers Oasis SRA Replace Shelters	Deschutes	04/20/09	No Date	5	04/30/09	05/01/09	\$ 10,221	0	3	114	2	6	1	0	N/A
231	Chas Reynolds SRA Deferred Maint	Union	05/01/09	No Date	5	05/01/09	04/28/09	\$ 3,792	3	1	86	4	1	0	0	N/A

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
232	Noti Scale House ADA Ele Gutters	Lane	04/06/09	03/26/09	5	04/02/09	04/02/09	\$ 2,141	0	4	41	4	6	2	0	N/A
233	Cave Jct MS Replace Windows	Josephine	04/08/09	No Date	5	03/23/09	04/16/09	\$ 5,054	0	2	30	2	3	0	0	N/A
234	District 10 Office Replace Windows	Deschutes	04/20/09	No Date	5	05/22/09	06/01/09	\$ 49,600	1	2	288	3	3	0	0	N/A
235	Lagrande DMV Deferred Maint	Union	05/01/09	05/01/09	4	05/29/09		\$ 7,270	0	1	0	1	1	0	1	N/A
236	Wolf Creek Storage Replace Floor	Douglas	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
237	Sand Shed Replace Broken Joists	Klamath	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
238	Salem Bldg Q Replace OH Doors	Marion	04/13/09	No Date	5	05/13/09	05/01/09	\$ 5,920	0	3	16	3	1	0	0	N/A
239	Weatherby SRA Replace Roof	Baker	03/10/09	03/12/09	5	03/25/09	03/27/09	\$ 10,688	3	2	63	5	4	1	4	N/A
240	Sandy MS Deferred Maintenance	Clackamas	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	1	N/A
241	Pendleton MS Deferred Maintenance	Umatilla	04/20/09	No Date	5	04/30/09	05/24/09	\$ 9,200	0	4	130	4	3	0	1	N/A
242	Woodburn MS Deferred Maintenance	Marion	04/06/09	No Date	5	04/20/09	05/08/09	\$ 1,480	1	1	16	2	2	0	1	N/A
243	Richland Shed Replace OH Doors	Baker	Cancelled	Cancelled	6	Cancelled	Cancelled	\$ -	0	0	0	0	0	0	0	N/A
244	Rose Lodge MS RR Vinyl Walls	Lincoln	03/18/09	03/18/09	5	03/18/09	03/18/09	\$ 2,297	0	2	12	2	2	1	2	N/A
245	Spray Sand Shed Interior Repairs	Wheeler	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
246	Coaledo Scale House Roof & Siding	Coos	04/06/09	No Date	5	04/30/09	04/14/09	\$ 1,870	0	2	13	2	2	0	1	N/A
247	Tillamook DMV Deferred Maintenance	Tillamook	03/19/09	03/19/09	5	03/19/09	03/19/09	\$ 3,420	0	3	16	3	5	2	3	N/A
248	Myrtle Point Scale Roof Siding Floor	Coos	03/03/09	03/03/09	5	03/10/09	03/13/09	\$ 6,978	0	4	90	4	5	2	4	N/A
249	Ashland Scale House Siding	Jackson	03/23/09	03/23/09	5	03/30/09	04/01/09	\$ 7,581	0	2	60	2	3	0	2	N/A
250	Suncrest SRA Replace Elec Boxes	Jackson	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	3	N/A
251	Troutdale MS Deferred Maintenance	Multnomah	04/08/09	No Date	5	04/30/09	04/30/09	\$ 3,423	1	1	19	2	1	0	1	N/A
252	Gateway OSP Bldg Misc Repairs	Lane	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
253	e. Portland Illuminate Gateway	Multnomah	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
254	Memaloose SRA Deferred Maintenance	Wasco	04/16/09	04/16/09	5	04/16/09	04/16/09	\$ 7,616	0	2	16	2	1	0	0	N/A
255	Canyonville MS Stormwater System	Douglas	04/30/09	04/01/09	5	04/30/09	04/21/09	\$ 5,610	0	2	15	2	3	1	1	N/A
256	Ona Beach MS Deferred Maintenance	Lincoln	04/06/09	No Date	5	04/07/09	05/01/09	\$ 5,984	0	6	24	6	2	0	1	N/A
257	Reg 1 Bldg Replace Carpet	Multnomah	04/16/09	No Date	5	05/22/09	05/15/09	\$ 18,055	0	8	48	8	3	1	0	N/A
258	Stanfield SRA Deferred Maintenance	Umatilla	03/17/09	03/17/09	5	03/20/09	03/30/09	\$ 9,297	0	1	0	1	2	0	1	N/A
259	Glenwood MS Electrical Changes	Lane	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
260	Hermiston MS Replace Fencing	Umatilla	04/07/09	No Date	5	05/07/09	04/30/09	\$ 10,780	1	2	72	3	0	0	0	N/A
261	LaGrande Sand Shed Misc Repairs	Union	04/17/09	No Date	5	04/30/09	05/08/09	\$ 11,484	1	3	145	4	3	1	1	N/A
262	Stanton Blvd Sand Shed Deferred Maint	Baker	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	2	N/A
263	LaGrande MS Storage - replace roof	Union	05/01/09	No Date	5	05/08/09	05/11/09	\$ 2,750	0	5	20	5	2	0	0	N/A
264	Mitchell MS Covered Timber Storage	Wheeler	04/28/09	No Date	5	05/04/09	05/14/09	\$ 22,857	2	8	388	3	1	1	0	N/A
265	Estacada MS Deferred Maintenance	Clackamas	03/30/09	No Date	5	04/24/09	04/21/09	\$ 9,900	2	1	134	3	3	1	0	N/A
266	Coos Bay DMV Deferred Maintenance	Coos	04/01/09	No Date	5	04/30/09	04/23/09	\$ 28,977	0	12	139	12	7	2	0	N/A
267	Barlow School Deferred Maintenance	Multnomah	04/06/09	04/03/09	5	05/15/09	05/15/09	\$ 13,080	0	7	181	7	3	0	1	N/A
268	Ashland MS Replace Carpet	Jackson	03/16/09	03/16/09	5	03/31/09	03/20/09	\$ 5,293	0	7	32	7	2	0	0	N/A
269	East Portland MS Decant Cover	Multnomah	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
270	Hunter Cr MS Replace Water Line	Curry	03/23/09	03/23/09	5	03/31/09	03/22/09	\$ 14,139	0	3	40	3	4	2	2	N/A
271	North Portland MS Decant Cover	Multnomah	04/15/09	No Date	5	05/22/09	05/15/09	\$ 19,946	2	3	240	5	5	0	1	N/A
272	Salem Building E Repair Roof	Marion	02/16/09	03/09/09	5	02/17/09	03/16/09	\$ 15,000	0	8	152	8	4	2	0	N/A
273	Shaniko MS Shop Repair/Replace OH	Wasco	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
274	Distict 12 Office Deferred Maintenance	Umatilla	04/15/09	04/02/09	5	05/15/09	07/10/09	\$ 32,135	0	6	324	4	7	1	0	N/A
275	Spray MS Deferred Maintenance	Wheeler	05/01/09	No Date	5	05/04/09	05/08/09	\$ 14,284	1	3	64	4	2	0	1	N/A
276	Glide Scale Deferred Maintenance	Douglas	03/26/09	No Date	5	04/30/09	04/20/09	\$ 13,780	0	2	200	2	8	4	1	N/A
277	C locks Sand Shed Replace Metal	Hood River	04/01/09	No Date	5	04/24/09	04/15/09	\$ 5,769	0	2	41	2	1	0	0	N/A
278	Coos Bay Br. Bldg Replace Roof	Coos	04/30/09	No Date	5	05/08/09	05/05/09	\$ 10,019	0	4	70	4	3	0	0	N/A
279	Coos Bay Sign Stor Replace Roof	Coos	04/30/09	No Date	5	05/08/09	05/05/09	\$ 10,019	0	4	70	4	3	0	0	N/A
280	Richland MS Shop Replace Roof	Baker	04/07/09	03/20/09	5	05/17/09	05/11/09	\$ 32,994	3	6	282	3	3	0	1	N/A
281	Gettings Cr Deferred Maintenance	Lane	04/27/09	04/29/09	5	06/18/09	06/19/09	\$ 15,550	0	6	39	6	5	2	1	N/A
282	Baldock SRA Replace Roof	Clackamas	03/10/09	03/10/09	5	03/19/09	03/19/09	\$ 13,212	0	5	150	5	3	1	0	N/A
283	Silver Lake MS Deferred Maintenance	Lake	03/03/09	03/16/09	5	04/02/09	03/17/09	\$ 8,079	0	3	22	3	3	1	1	N/A
284	Grand Rhond Stor OH Door Window	Polk	03/10/09	03/10/09	5	04/06/09	04/06/09	\$ 3,697	0	3	16	3	2	1	3	N/A
285	Reith Stockpile - install security fence	Umatilla	04/22/09	No Date	5	04/28/09	04/30/09	\$ 12,000	0	1	50	1	5	0	1	N/A
286	Ashland POE Deferred Maintenance	Jackson	03/23/09	03/19/09	5	03/30/09	03/25/09	\$ 8,971	0	10	60	10	4	2	10	N/A
287	Bend MS Sand Shed Replace Roof	Deschutes	04/20/09	04/20/09	4	05/20/09		\$ -	0	0	0	0	1	1	1	N/A
288	C. Point MS Upgrade Water Line	Jackson	03/23/09	03/09/09	5	03/31/09	03/20/09	\$ 9,365	0	5	143	4	10	4	2	N/A
289	Austin MS Deferred Maintenance	Grant	04/29/09	No Date	5	05/08/09	05/10/09	\$ 13,834	1	6	162	3	6	4	1	N/A
290	Juntura MS Deferred Maintenance	Harney	04/24/09	No Date	5	04/10/09	04/13/09	\$ 14,772	2	0	277	1	6	2	2	N/A
291	Jantzen Shop Bldg Deferred Maint	Multnomah	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	1	N/A
292	Klamath Falls MS Deferred Maintenance	Klamath	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	0	N/A
293	Lapine MS Replace Doors/Floor	Deschutes	03/18/09	No Date	5	04/18/09	05/01/09	\$ 49,983	1	11	384	12	4	2	1	N/A
294	Burns MS Deferred Maintenance	Harney	04/22/09	No Date	5	05/01/09	05/06/09	\$ 3,745	0	2	32	2	2	1	1	N/A
295	Salem Dock Bldg F Roof	Marion	03/23/09	No Date	5	04/13/09	04/22/09	\$ 40,376	0	5	557	5	0	0	5	N/A
296	Seneca MS Shop Replace Doors	Grant	Cancelled	Cancelled	6	Cancelled	Cancelled	\$ -	0	0	0	0	0	0	1	N/A
297	Dist 14 Office Deffered Maintenance	Malhour	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	1	N/A
298	Basque MS Deferred Maintenance	Malheur	04/20/09	No Date	5	04/25/09	04/13/09	\$ 12,117	0	4	185	2	3	1	1	N/A
299	Lawnfield Bldg Seal Roof/Gutters	Clackamas	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	0	0	1	N/A
300	Coquille Deferred Maintenance	Coos	04/01/09	No Date	5	04/30/09	04/21/09	\$ 19,721	0	10	200	10	9	4	2	N/A
301	Maples SRA ADA Upgrades	Marion	04/13/09	04/13/09	5	05/22/09	06/24/09	\$ 11,609	0	3	101	3	4	0	0	N/A
302	R5 Bldg Deferred Maintenance	Union	04/30/09	05/01/09	4	06/30/09		\$ 12,435	0	0	0	0	0	0	0	N/A
303	Stinking Water Sand Roof and Repairs	Harney	04/15/09	No Date	5	05/01/09	05/03/09	\$ 27,856	1	6	372	3	4	2	1	N/A
304	Bend Bldg J Deferred Maintenance	Deschutes	04/24/09	04/24/09	5	05/15/09		\$ 12,870	0	5	94	5	3	1	1	N/A
305	Baldock MS Deferred Maintenance	Washington	04/08/09	No Date	5	04/30/09	05/06/09	\$ 23,145	0	3	172	3	2	1	1	N/A
306	Sisters MS Shop OH Doors	Deschutes	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	1	1	1	N/A
307	Bachelor Butte Sand Shed Repl Roof	Deschutes	05/01/09	05/01/09	4	05/26/09		\$ 14,500	0	0	0	0	5	5	0	N/A

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
308	Florance MS Deferred Maintenance	Lane	04/06/09	03/31/09	5	04/06/09	04/07/09	\$ 8,472	1	1	131	2	1	0	1	N/A
309	Alkali Lake Deferred Maintenance	Harney	04/30/09	No Date	5	05/22/09	05/19/09	\$ 36,132	3	7	534	10	11	1	1	N/A
310	Lakeview MS Deferred Maintenance	Lake	04/27/09	04/16/09	5	05/30/09	04/24/09	\$ 32,483	2	6	345	8	6	3	0	N/A
311	Boardman Deferred Maintenance	Morrow	04/06/09	04/24/09	5	05/29/09	07/08/09	\$ 169,455	3	4	967	4	5	2	2	N/A
312	Bend Shop Roof/OH Doors	Deschutes	04/15/09	No Date	5	04/28/09	04/29/09	\$ 28,694	6	3	144	9	5	3	2	N/A
313	Ontario MS Repair Water Filter System	Malheur	03/31/09	No Date	5	05/13/09	05/13/09	\$ 35,835	2	2	416	4	0	0	1	N/A
314	Ukiah Sand Shed Replace Roof	Umatilla	UF/UA	UF/UA	0	UF/UA	UF/UA	\$ -	0	0	0	0	2	2	0	N/A
315	Milwaukie Stone Bldg Replace Roof	Clackamas	04/06/09	No Date	5	05/01/09	04/29/09	\$ 46,554	7	4	1,093	7	5	2	0	N/A
316	The Dalles MS Deferred Maintenance	Wasco	04/27/09	No Date	5	05/05/09	05/05/09	\$ 51,145	0	4	261	4	2	0	0	N/A
317	Oak Grove SRA Deferred Maintenance	Linn	04/27/09	No Date	5	06/18/09		\$ 53,967	0	11	284	11	8	0	0	N/A
318	Port Orford MS Deferred Maintenance	Curry	04/27/09	No Date	4	05/31/09		\$ -	0	0	0	0	0	0	1	N/A
319	Boswell Spgs Deferred Maintenance	Douglas	03/31/09	No Date	5	05/15/09	04/25/09	\$ 60,965	2	0	291	2	7	0	0	N/A
320	Davis Slough Deferred Maintenance	Coos	05/01/09	05/01/09	4	07/30/09		\$ -	0	0	0	0	0	0	1	N/A
321	Baker City Sand Shed Roof & Siding	Baker	04/15/09	No Date	5	04/30/09	05/15/09	\$ 45,231	0	4	319	4	1	0	1	N/A
322	S. Umpqua SRA Deferred Maintenance	Douglas	10/01/09	No Date	1	No Date		\$ -	0	0	0	0	0	0	0	N/A
323	Cow Creek SRA Deferred Maintenance	Douglas	10/01/09	No Date	1	No Date		\$ -	0	0	0	0	0	0	0	N/A
324	Brothers MS Deferred Maintenance	Deschutes	05/01/09	05/01/09	5	06/01/09	05/27/09	\$ 101,422	0	29	790	29	2	0	0	N/A
325	Central Point MS Deferred Maintenance	Jackson	04/30/09	04/30/09	5	05/22/09	06/18/09	\$ 99,599	0	20	237	20	4	0	0	N/A
326	Warrenton MS Deferred Maintenance	Clatsop	04/06/09	No Date	5	06/01/09	05/15/09	\$ 39,841	0	5	510	0	3	0	0	N/A
327	Chemult MS Deferred Maintenance	Klamath	05/01/09	04/29/09	4	06/12/09		\$ 116,118	0	0	0	0	0	0	0	N/A
328	Region 3 Bldg Deferred Maintenance	Douglas	04/06/09	04/16/09	5	05/29/09	06/12/09	\$ 149,823	0	32	766	32	2	0	1	N/A
329	Cabin Cr SRA Deferred Maintenance	Douglas	04/27/09	04/29/09	3	08/18/09		\$ 9,782	0	0	0	0	0	0	0	N/A
330	Shady MS Deferred Maintenance	Douglas	05/01/09	04/27/09	4	05/26/09		\$ 93,781	0	0	0	0	0	0	0	N/A
331	LaGrande Shop Deferred Maintenance	Union	05/01/09	05/01/09	4	06/30/09		\$ 180,041	0	0	0	0	0	0	1	N/A
332	Manzanita SRA Deferred Maintenance	Josephine	05/01/09	04/13/09	5	06/29/09	06/18/09	\$ 248,731	0	10	1,044	10	4	1	1	N/A
333	Rail Station	Marion	04/15/09	No Date	5	04/29/09	04/29/09	\$ 24,496	0	1	25	1	2	0	0	\$ 10,920
								\$ 2,458,102	55	406	15,247	417	302	83	95	\$ 10,920

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion
0) UF / UA
UF =Unfunded Projects UA = Unassigned Project



**SB 338 Report
August 17, 2009**



OYA

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
334	Agency Wide Central Control	Clatsop	05/01/09	02/09/09	3	11/30/09		\$ 88,500	2	6	91	6	7	1	0	N/A
335	Agency-wide Central Control Renovation	Linn	05/01/09	02/09/09	3	11/30/09		\$ 50,640	2	9	110	9	5	1	0	N/A
336	Agency-wide Central Control Renovation	Union	05/01/09	02/09/09	3	11/30/09		\$ 50,307	2	7	83	7	3	0	0	N/A
337	Agency-wide Central Control Renovation	Josephine	05/01/09	02/09/09	3	11/30/09		\$ 1,935	2	1	0	3	0	0	0	N/A
338	Agency-wide Central Control	Tillamook	05/01/09	02/09/09	3	11/30/09		\$ 2,005	2	1	0	3	0	0	0	N/A
339	Agencywide Central Control	Harney	05/01/09	02/09/09	3	11/30/09		\$ 2,319	2	1	0	3	0	0	0	N/A
340	Agencywide HVAC Renovation and Repair	Clatsop	05/01/09	02/09/09	3	08/31/09		\$ 1,620	2	0	0	2	0	0	0	\$ 48,000
341	Agencywide HVAC Renovation and Repair	Josephine	05/01/09	02/09/09	3	08/31/09		\$ 253	2	0	0	2	0	0	0	\$ 48,000
342	Agencywide HVAC Renovation and Repair	Linn	05/01/09	02/09/09	3	08/31/09		\$ 1,922	2	1	0	2	1	0	0	\$ 48,000
343	Agencywide HVAC Renovation and Repair	Harney	05/01/09	02/09/09	3	08/31/09		\$ 321	2	0	0	2	0	0	0	\$ 48,000
344	Agencywide HVAC Renovation and Repair	Union	05/01/09	02/09/09	3	08/31/09		\$ 331	2	0	0	2	0	0	0	\$ 48,000
345	Camp Tillamook Appliance Replacement	Tillamook	05/01/09	02/09/09	3	08/31/09		\$ 8,091	2	0	0	2	1	0	0	N/A
346	Rogue Valley YCF Fire Barrier...	Josephine	05/01/09	02/09/09	4	06/30/09		\$ 276	2	4	0	4	1	0	0	N/A
347	Agency-wide End of Life Appliance Rep.	Various	05/01/09	02/09/09	3	11/30/09		\$ 684	4	7	13	9	6	1	0	N/A
348	Hillcrest Walk-in Complex Replacement	Marion	05/01/09	02/09/09	3	08/31/09		\$ 1,008	2	13	0	12	2	1	1	N/A
349	RiverBend Facility Sewage Lagoon	Union	05/01/09	02/09/09	3	11/30/09		\$ 5,934	2	5	0	5	2	0	0	N/A
350	MacLaren Campus Gas HVAC Conv	Marion	05/01/09	02/09/09	3	01/31/10	01/31/10	\$ 12,385	2	13	0	12	2	1	1	\$ 1,500,000
351	Hillcrest - Zeta Living Unit Renovation	Marion	05/01/09	02/09/09	3	05/31/10		\$ 8,283	2	21	0	19	3	1	0	N/A
352	Tillamook YCF School House Const	Tillamook	05/01/09	02/09/09	3	11/30/09		\$ 15,485	2	3	0	5	6	5	0	N/A
353	Corvallis House Replacement	Linn	05/01/09	02/09/09	3	05/31/10		\$ 208,632	21	14	68	19	18	8	1	N/A
354	MacLaren Deferred Maintenance	Marion	05/01/09	02/09/09	3	05/31/10		\$ 159,323	13	18	695	16	21	7	2	N/A
355	Hillcrest Deferred Maintenance	Marion	05/01/09	02/09/09	3	02/28/09		\$ 10,203	2	6	0	5	2	0	1	N/A
356	Unassigned		U/A	U/A	0	U/A	U/A	\$ -	0	0	0	0	0	0	0	
357	Fire Barrier/Perimeter Fence Rd	Linn	05/01/09	02/09/09	4	06/30/09		\$ 276	2	4	0	4	0	0	0	N/A
358	Hillcrest Gymnasium Renovation	Marion	05/01/09	02/09/09	3	11/30/09		\$ 450	2	10	0	9	0	0	1	N/A
359	Hillcrest High School (see below)	Marion	05/01/09	02/09/09	3	11/30/09		\$ 2,651	2	10	0	9	1	0	1	N/A
360	MacLaren High School (see below)	Marion	05/01/09	02/09/09	3	11/30/09		\$ 2,651	2	10	0	9	0	0	1	N/A
								\$ 636,484	84	164	1,060	180	81	26	9	\$ 1,740,000

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion

0) UF / UA

UF =Unfunded Projects UA = Unassigned Project



**SB 338 Report
August 17, 2009**



CCWD

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
361	BM: Safety and Security	Umatilla	04/30/09	04/22/09	3	07/01/10		\$ 230,000	0	25	688	12	2	2	1	N/A
362	BM: Aging Infrastructure	Umatilla	04/30/09	04/27/09	3	07/01/10		\$ -	0	14	238	8	2	1	2	\$ 1,160,000
363	BM: Aging Infrastructure	Umatilla	04/30/09	04/27/09	3	07/01/09		\$ 115,000	0	8	337	6	1	1	0	\$ 4,600,000
364	CE: New parking spaces	Deschutes	02/05/09	02/05/09	3	08/31/09		\$ 81,365	0	19	284	19	8	4	1	N/A
365	CE: Replace Electrical Distribution System	Deschutes	02/05/09	02/05/09	3	10/30/09		\$ 57,627	0	30	0	25	2	0	1	N/A
366	CE: Disability Access	Deschutes	02/05/09	02/05/09	3	10/31/10		\$ 54,405	1	15	69	16	7	2	2	N/A
367	CE: Roadway Repair	Deschutes	02/05/09	02/05/09	3	07/30/09		\$ 72,831	0	8	110	8	6	3	0	N/A
368	CE: Sidewalk/Hand Rail Replacement	Deschutes	02/05/09	02/05/09	3	04/30/09		\$ 52,454	5	5	102	8	9	1	1	N/A
369	CE: Fire Reduction	Deschutes	04/30/09	04/20/09	3	09/30/09		\$ 9,535	3	2	153	5	11	0	0	N/A
370	CE: Painting, Flooring, Roof Maintenance	Deschutes	02/26/09	03/23/09	3	08/31/10		\$ 58,055	1	7	208	8	9	4	0	N/A
371	CE: Building Weatherization	Deschutes	04/22/09	04/28/09	3	07/31/09		\$ 24,949	0	7	391	7	0	0	0	N/A
372	CE: Air conditioning suppression systems	Deschutes	02/05/09	02/05/09	3	09/30/09		\$ 19,596	3	15	12	15	6	2	0	N/A
373	CE: retrofit buildings	Deschutes	02/05/09	02/05/09	3	11/30/09		\$ 392,873	2	19	2,349	19	17	10	1	N/A
374	CH: Replace failing roof.	Marion	04/20/09	04/28/09	3	08/27/09		\$ 436,752	0	34	2,520	34	18	3	0	N/A
375	CH: Renovate building	Marion	03/20/09	03/20/09	3	11/16/09		\$ 71,812	1	11	478	11	11	2	0	N/A
376	CH: Replace failing storage barn	Marion	04/20/09	04/09/09	3	10/01/09		\$ 65,039	0	20	430	20	4	2	0	N/A
377	CH: HVAC and mechanical system	Marion	04/13/09	04/29/09	3	12/01/09		\$ 86,550	0	15	202	12	16	7	0	N/A
378	CH: Upgrade utility infrastructure	Marion	04/20/09	04/29/09	3	08/31/09		\$ 30,087	0	6	322	6	12	1	0	N/A
379	CH: Front entry roadway re-build.	Marion	04/20/09	04/22/09	3	09/15/09		\$ 594,076	31	4	1,804	20	16	8	3	N/A
380	CH: Upgrade primary electrical distribution	Marion	04/20/09	04/27/09	3	08/30/10		\$ 268,384	0	8	837	8	7	2	0	N/A
381	CH: Replace aged rooftop air handlers	Marion	04/20/09	04/09/09	3	08/31/09		\$ 83,320	0	9	380	9	6	2	0	N/A
382	CH: Upgrade elevators	Marion	04/20/09	04/27/09	3	08/31/09		\$ 201,958	0	3	923	3	5	0	0	N/A
383	CH: Replace handicapped doors.	Marion	03/31/09	04/24/09	5	05/29/09	05/18/09	\$ 8,870	0	4	36	4	1	0	0	N/A
384	CH: Upgrade exterior lighting systems.	Marion	03/16/09	02/20/09	5	05/29/09	03/10/09	\$ 9,373	0	2	88	2	2	0	0	N/A
385	CH: Upgrade air doors	Marion	03/31/09	04/28/09	3	06/30/09		\$ 6,179	0	4	41	4	1	0	0	N/A
386	CH: Replacement Space	Marion	03/16/09	03/16/09	3	09/01/09		\$ 665,383	5	12	4,139	14	15	10	0	N/A
387	CH: Replace deteriorated fire station.	Marion	04/27/09	04/20/09	3	08/17/09		\$ 446,752	0	18	4,080	18	12	9	0	N/A
388	CH: Replace shelter quarters.	Marion	03/02/09	03/02/09	3	10/15/09		\$ 107,849	0	13	405	13	7	0	0	N/A
389	CH: Create classroom	Polk	02/20/09	02/20/09	3	11/20/09		\$ 364,193	9	22	1,545	22	27	8	1	N/A
390	CH: Replace failing metal roof	Yamhill	04/20/09	04/29/09	3	07/10/09		\$ 316,277	2	23	941	23	10	4	0	N/A
391	CH: Re-roof Santiam Center	Marion	04/20/09	04/28/09	3	07/15/09		\$ 181,985	0	21	1,507	21	6	3	1	N/A
392	CL: Replace communications infrastructure	Clackamas	05/01/09	04/22/09	3	08/31/09		\$ 672,693	0	13	1,143	13	8	1	1	N/A
393	CL: Complete duct cleaning.	Clackamas	04/27/09	04/06/09	5	04/30/09	04/08/09	\$ 8,469	0	2	68	2	2	0	1	N/A
394	CL: Install roll up security doors	Clackamas	05/01/09	04/24/09	3	08/28/09		\$ 11,060	0	2	28	2	0	0	0	N/A
395	CL: Replace Industrial wing roll up doors.	Clackamas	05/01/09	04/24/09	5	06/30/09	06/30/09	\$ 24,875	0	3	160	3	0	0	0	N/A

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
396	CL: Repair/renovate	Clackamas	05/01/09	04/09/09	3	08/31/09		\$ 4,395	0	2	25	1	2	0	0	\$ 2,936
397	CL: Energy efficiency to HVAC system.	Clackamas	04/27/09	04/09/09	3	08/31/09		\$ -	0	2	0	1	2	0	0	\$ 1,670
398	CL: Repair blue Rails, exterior doors.	Clackamas	05/01/09	04/17/09	5	07/01/09	04/27/09	\$ 13,950	3	0	47	1	2	0	0	N/A
399	CL: Ceiling tiles replacement.	Clackamas	05/01/09	04/20/09	5	06/19/09	06/01/09	\$ 35,051	2	3	110	4	3	1	1	N/A
400	CL: Patch, paint interior walls throughout.	Clackamas	05/01/09	04/23/09	3	07/24/09		\$ 1,210	0	2	58	2	1	0	0	N/A
401	CL: Carpet and linoleum replacement	Clackamas	05/01/09	04/27/09	5	07/31/09	07/22/09	\$ 1,366	0	8	218	8	5	3	0	N/A
402	CL: Energy efficiency to HVAC system.	Clackamas	05/01/09	04/22/09	5	05/08/09	05/08/09	\$ 10,847	0	2	89	1	2	0	0	\$ 396
403	CL: Patch,paint interior walls throughout.	Clackamas	05/01/09	04/27/09	5	07/24/09	06/19/09	\$ 23,165	8	2	60	4	3	0	1	N/A
404	CL: Replace floor	Clackamas	05/01/09	04/28/09	5	07/31/09	06/19/09	\$ -	0	7	126	7	5	3	0	N/A
405	CL: Energy efficiency HVAC system.	Clackamas	03/27/09	03/27/09	5	04/03/09	03/27/09	\$ 19,886	0	2	70	1	4	2	0	\$ 298
406	CL: Energy efficiency controls HVAC system	Clackamas	04/13/09	04/17/09	5	04/30/09	04/24/09	\$ 13,818	0	2	50	1	2	0	0	\$ 1,972
407	CL: Energy efficiency HVAC system.	Clackamas	04/13/09	04/14/09	5	04/30/09	04/21/09	\$ 14,676	0	2	48	1	2	0	0	\$ 1,972
408	CL: Install new fire alarm system.	Clackamas	05/01/09	04/13/09	5	05/29/09	05/21/09	\$ 27,480	1	6	90	6	3	0	0	N/A
409	CL: Repair/renovate	Clackamas	05/01/09	04/22/09	3	09/04/09		\$ 119,812	12	4	210	6	9	3	2	N/A
410	CL: Building wide air test and balance	Clackamas	05/01/09	04/22/09	3	09/30/09		\$ -	0	1	0	1	1	0	0	N/A
411	CL: Energy efficiency HVAC system.	Clackamas	05/01/09	04/17/09	3	09/04/09		\$ -	0	2	0	1	2	0	0	\$ 2,400
412	CL: Repair/renovate	Clackamas	05/01/09	04/22/09	3	09/04/09		\$ 46,232	12	8	343	10	13	3	3	TBD
413	CL: Ceiling tile replacement	Clackamas	05/01/09	04/20/09	5	06/19/09	06/01/09	\$ 12,704	2	7	63	8	4	1	2	N/A
414	CL: Patch paint interior walls throughout.	Clackamas	05/01/09	04/27/09	5	07/24/09	06/15/09	\$ 40,694	23	5	284	12	3	1	2	N/A
415	CL: Floor tile replacement	Clackamas	05/01/09	04/27/09	5	07/31/09	06/18/09	\$ -	0	7	48	7	5	3	0	N/A
416	CL: Repair/renovate a	Clackamas	05/01/09	04/22/09	3	09/04/09		\$ 29,715	12	9	64	11	11	3	3	TBD
417	CL: Energy efficiency HVAC system.	Clackamas	05/01/09	04/17/09	3	09/04/09		\$ -	0	2	0	1	2	0	0	\$ 1,100
418	CL: Energy efficiency HVAC system.	Clackamas	05/01/09	04/06/09	5	05/08/09	04/15/09	\$ 13,082	0	2	32	1	2	0	0	\$ 196
419	CL: Energy efficiency HVAC system.	Clackamas	05/01/09	04/20/09	5	07/24/09	07/17/09	\$ -	0	2	113	1	2	0	0	\$ 1,690
420	CL: Various electrical improvements.	Clackamas	04/15/09	04/06/09	3	08/28/09		\$ 151,003	0	35	662	32	5	1	1	N/A
421	CT: Visual Arts Building	Clatsop	04/27/09	04/27/09	3	09/01/09		\$ 73,269	0	3	283	3	10	7	1	\$ 2,150
422	CT: Library Building	Clatsop	04/27/09	04/27/09	3	09/01/09		\$ 100,972	0	0	299	0	5	5	1	\$ 3,100
423	CT: MERTS I	Clatsop	04/15/09	04/30/09	3	07/30/09		\$ 128,554	0	5	234	4	10	2	1	\$ 950
424	CT: Alder Hall	Clatsop	04/27/09	04/27/09	3	09/01/09		\$ 37,255	0	0	0	0	1	1	0	\$ 830
425	CT: Patriot Hall	Clatsop	06/10/09	04/20/09	3	08/14/09		\$ 34,268	0	3	80	3	2	1	0	\$ 7,650
426	CT: Campus-Wide	Clatsop	04/16/09	04/16/09	3	07/10/09		\$ 91,428	0	14	847	14	7	2	1	\$ 14,045
427	CT: Performing Arts Center	Clatsop	04/27/09	04/30/09	3	08/15/09		\$ 30,368	0	0	267	0	1	1	1	N/A
428	CT: Forerunner Teaching Vessel	Clatsop	04/22/09	04/22/09	3	02/26/10		\$ 8,747	0	0	8	0	1	0	0	N/A
429	CT: Forerunner Teaching Vessel	Clatsop	04/28/09	05/07/09	5	05/29/09	06/03/09	\$ 15,072	0	0	115	0	0	0	0	N/A
430	CT: Josie Peper Building	Clatsop	04/27/09	04/30/09	3	07/30/09		\$ 20,873	0	0	88	0	1	1	1	\$ 75
431	CG: heating/ventilation system components	Wasco	04/30/09	04/14/09	3	09/11/09		\$ 37,139	0	9	498	9	0	0	0	N/A
432	CG: Upgrade HVAC system	Wasco	04/30/09	04/14/09	3	09/11/09		\$ 22,969	0	9	488	9	0	0	0	N/A
433	CG: windows	Wasco	04/30/09	04/22/09	5	09/30/09	06/26/09	\$ 33,000	0	3	88	3	1	0	0	N/A
434	CG: windows	Wasco	04/30/09	04/22/09	5	09/30/09	06/26/09	\$ 100,800	0	3	261	3	1	0	0	N/A
435	CG: fire sprinkler system	Wasco	04/30/09	04/24/09	3	No Date		\$ 5,216	0	1	5	1	1	0	0	N/A
436	CG: Replace AC condenser units.	Wasco	04/30/09	04/14/09	3	No Date		\$ 22,284	0	8	480	8	0	0	0	N/A

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
437	KL: Concrete repair	Klamath	04/27/09	04/28/09	4	07/17/09		\$ 19,078	6	15	635	16	4	2	0	N/A
438	KL: Replace locks	Klamath	04/30/09	04/29/09	3	08/31/09		\$ 76,439	1	7	185	8	6	2	0	N/A
439	KL: Pipe irrigation canal	Klamath	04/01/09	03/17/09	5	04/17/09	04/17/09	\$ 444,149	2	7	418	9	5	2	1	N/A
440	KL: Paint	Klamath	04/27/09	04/30/09	5	07/01/09	06/26/09	\$ 8,482	2	3	296	3	3	1	0	N/A
441	KL: Parking lot	Klamath	04/30/09	04/28/09	5	07/24/09	07/31/09	\$ 238,644	6	14	1,592	18	11	4	1	N/A
442	KL: Carpeting	Klamath	04/27/09	04/29/09	5	07/15/09	06/28/09	\$ 29,782	0	11	343	11	6	1	1	N/A
443	KL: Windows, doors	Klamath	04/30/09	04/30/09	4	10/15/09		\$ 852	0	1	0	1	0	0	0	\$ 6,000
444	KL: Re-side	Klamath	04/30/09	04/30/09	4	10/15/09		\$ 10,939	1	6	21	6	3	1	0	N/A
445	LA: ADA Compliance	Lane	04/28/09	04/04/09	3	03/01/10		\$ 263,712	6	19	1,494	21	56	9	2	N/A
446	LA: security lighting	Lane	04/28/09	04/30/09	3	03/01/10		\$ 93,810	1	3	698	3	13	3	0	N/A
447	LA: carpeting	Lane	04/27/09	04/10/09	3	03/01/10		\$ 14,707	0	9	9	9	3	1	0	N/A
448	LA: preparation to install card access	Lane	04/28/09	04/16/09	3	03/01/10		\$ 427,101	4	8	211	8	8	1	0	N/A
449	LA: Remove asbestos insulation	Lane	04/28/09	04/30/09	3	03/01/10		\$ 110,305	0	10	890	10	8	1	0	N/A
450	LA: I Installation emergency communication	Lane	04/28/09	04/30/09	3	03/01/10		\$ 319,737	1	9	1,333	10	2	0	0	N/A
451	LA: electrical system, water, sub-metering	Lane	04/28/09	04/30/09	3	03/01/10		\$ 108,767	0	4	357	4	5	2	0	N/A
452	LA: Electrical upgrades -	Lane	04/03/09	04/03/09	3	03/01/10		\$ 1,047,535	70	55	19,698	58	40	4	0	N/A
453	LA: sewer piping	Lane	04/29/09	04/30/09	3	03/01/10		\$ 3,657	0	3	0	3	2	0	0	N/A
454	LA: roofs	Lane	04/29/09	04/30/09	3	03/01/10		\$ 568,890	0	12	583	12	4	2	4	N/A
455	LA: restrooms	Lane	04/29/09	04/30/09	3	03/01/10		\$ 109,203	1	11	708	11	25	10	0	N/A
456	LA: utility and infrastructure improvements	Lane	04/29/09	04/30/09	3	03/01/10		\$ 109,735	0	16	1,213	16	16	4	1	N/A
457	LA: audio and technical infrastructure	Lane	04/29/09	04/29/09	3	03/01/10		\$ 17,048	0	7	0	7	3	1	0	N/A
458	LA: paint spray booth	Lane	04/29/09	04/30/09	3	03/01/10		\$ 175,147	0	11	0	11	7	1	0	N/A
459	LA: Replace tile	Lane	04/29/09	04/30/09	3	03/01/10		\$ 314,072	8	4	1,254	8	6	0	0	N/A
460	LB: HVAC	Linn	03/24/09	03/25/09	5	06/30/09	06/18/09	\$ 129,365	0	8	753	8	14	2	0	\$ 59,100
461	LB: insulation, glazing	Linn	03/17/09	03/18/09	5	06/30/09	07/12/09	\$ 168,774	9	25	1,706	30	23	11	2	\$ 443,280
462	LB: electrical transformers	Linn	03/27/09	03/31/09	4	06/30/09		\$ 1,572	0	2	16	2	2	0	1	N/A
463	LB: Upgrade exterior corridor lighting.	Linn	03/27/09	03/31/09	5	06/30/09	07/15/09	\$ 86,377	0	3	252	3	4	0	0	N/A
464	LB: Upgrade sidewalk lighting.	Linn	03/27/09	03/30/09	4	06/30/09		\$ 9,771	0	3	46	3	2	0	0	\$ 10,000
465	LB: Tile and carpet replacement	Linn	03/09/09	03/11/09	4	06/30/09		\$ 124,150	0	11	1,198	11	7	3	0	N/A
466	LB: energy management/HVAC control system	Linn	03/27/09	03/30/09	4	06/30/09		\$ 214,241	3	7	678	7	3	0	0	\$ 1,063,920
467	LB: Upgrade hot water circulating pumps	Linn	03/27/09	03/30/09	5	06/30/09	05/18/09	\$ 27,707	1	3	34	3	3	0	1	\$ 15,000
468	LB: Improve lighting fixtures on existing pole	Linn	03/27/09	03/30/09	5	06/30/09	05/13/09	\$ 12,885	0	3	20	3	3	1	1	N/A
469	LB: rigging system	Linn	03/19/09	03/20/09	5	06/30/09	06/25/09	\$ 150,250	2	17	638	13	2	1	0	N/A
470	LB: Ceiling, lighting, wall surface and flooring	Linn	03/17/09	03/18/09	5	06/30/09	06/25/09	\$ 168,794	1	15	1,451	9	8	5	1	N/A
471	LB: Asphalt road and parking lot	Linn	03/27/09	03/30/09	5	06/30/09	06/10/09	\$ 41,965	0	12	133	12	4	2	0	N/A
472	LB: Connect to city water system	Linn	03/27/09	03/30/09	5	06/30/09	07/22/09	\$ 214,651	0	10	412	10	10	4	1	N/A
473	LB: kitchen	Linn	03/26/09	03/31/09	4	06/30/09		\$ 76,606	0	6	99	6	7	2	0	N/A
474	MH: Stage Rehabilitation	Multnomah	04/30/09	04/29/09	3	09/30/09		\$ 24,386	4	5	47	6	16	8	0	N/A
475	MH: Classroom Painting, Flooring Upgrades	Multnomah	04/01/09	04/15/09	3	08/31/09		\$ 100,324	0	11	5	11	3	0	0	N/A
476	MH: Restroom ADA Upgrades	Multnomah	04/06/09	04/29/09	3	09/30/09		\$ 8,521	4	5	42	6	20	10	0	N/A
477	MH: Roof Replacement	Multnomah	04/06/09	04/15/09	3	09/30/09		\$ 702,920	3	37	6,000	35	8	3	2	N/A

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWFSB working on a project	Estimated Energy Savings (\$)
478	MH: Reconfigurations	Multnomah	04/01/09	04/29/09	3	09/30/09		\$ 40,632	4	5	382	6	18	9	0	N/A
479	MH: Science Labs ADA Upgrades	Multnomah	04/06/09	04/29/09	3	09/30/09		\$ 26,423	4	5	218	6	16	8	0	N/A
480	MH: Dental Labs ADA Upgrades	Multnomah	04/06/09	04/29/09	3	09/30/09		\$ 37,046	4	5	330	6	18	9	1	N/A
481	OC: security cameras	Lincoln	04/01/09	03/19/09	3	08/12/09		\$ 93,727	0	4	950	4	3	1	0	N/A
482	OC: Notification system and PA system	Lincoln	04/01/09	03/19/09	3	08/31/09		\$ 8,375	0	4	1	4	2	1	0	N/A
483	OC: Generator	Lincoln	04/01/09	03/19/09	3	08/19/09		\$ 135,955	0	4	198	4	2	1	0	N/A
484	OC: Add access hardware for Audubon door	Lincoln	04/01/09	03/19/09	5	06/10/09	06/25/09	\$ 2,879	0	2	9	2	2	1	0	N/A
485	OC: Add access hardware at patio door.	Lincoln	04/01/09	03/19/09	5	05/15/09	05/22/09	\$ 2,018	0	2	13	2	2	1	0	N/A
486	PO: Mass Notification System	Multnomah	02/18/09	03/23/08	3	03/31/10		\$ 162,494	5	14	0	12	5	1	1	N/A
487	PO: ADA Upgrades	Multnomah	03/31/09	05/08/09	3	09/01/10		\$ 31,890	5	3	436	6	3	0	1	N/A
488	PO: Voice over IP	Multnomah	03/19/09	03/31/09	3	06/30/11		\$ 56,947	0	14	231	8	6	0	2	N/A
489	PO: centralized clock system	Multnomah	03/18/09	04/09/09	3	09/15/09		\$ 80,118	0	4	50	2	2	1	1	N/A
490	PO: Fire/Life Safety Upgrades	Multnomah	03/30/09	03/31/09	3	03/30/10		\$ 75,155	3	2	581	3	2	1	1	N/A
491	PO: Electrical Upgrades	Multnomah	03/05/09	03/05/09	3	02/01/10		\$ 32,289	6	13	10	15	0	0	1	N/A
492	PO: Environmental Maintenance/Upgrades	Multnomah	04/01/09	04/01/09	3	09/30/09		\$ 24,611	0	11	261	11	18	9	7	N/A
493	PO: Energy Management System	Multnomah	03/31/09	03/31/09	3	09/30/10		\$ -	0	1	0	1	0	0	0	N/A
494	PO: water supply lines	Multnomah	04/15/09	04/30/09	3	12/31/09		\$ 249,052	38	20	1,395	20	25	6	2	N/A
495	PO: repairs/Seismic Upgrades	Multnomah	06/01/09	05/05/09	4	06/01/10		\$ 190,756	12	20	2,304	20	5	1	1	N/A
496	PO: Roadways/Parking lots	Multnomah	03/23/09	03/23/09	5	06/30/09	06/30/09	\$ 778,937	0	37	1,583	33	20	12	3	N/A
497	PO: T-12 lighting	Multnomah	03/23/09	04/30/09	3	09/05/09		\$ 69,570	7	3	264	5	2	1	1	\$ 10,338
498	PO: boilers	Multnomah	04/08/09	04/30/09	3	10/31/09		\$ 8,975	2	4	0	5	1	0	0	\$ 15,500
499	PO: Gym flooring	Multnomah	06/20/09	04/23/09	3	09/01/09		\$ 15,804	0	3	204	3	2	1	1	N/A
500	PO: swimming pool decking	Multnomah	05/09/09	04/29/09	3	09/09/09		\$ 21,500	2	2	194	2	5	0	0	N/A
501	PO: Grounds Greenhouse & Shade house	Multnomah	04/08/09	04/13/09	3	09/30/09		\$ 17,789	2	2	0	3	2	0	1	N/A
502	PO: Skylight Replacements	Multnomah	04/15/09	04/03/09	3	09/09/09		\$ 85,258	2	93	113	77	18	2	0	N/A
503	PO: boilers	Multnomah	04/08/09	04/30/09	3	10/31/09		\$ 19,938	7	6	0	12	0	0	0	\$ 10,000
504	PO: Parking Lot Lighting	Multnomah	03/16/09	04/30/09	3	04/02/10		\$ 446	0	4	8	4	1	0	1	N/A
505	RO: Replacement of electrical panels.	Josephine	06/01/09	04/02/09	3	07/31/09		\$ -	0	4	3	4	2	0	1	N/A
506	RO: Replacement of Aging HVAC Units -	Josephine	04/01/09	03/03/09	3	01/31/10		\$ -	7	21	1,194	26	31	9	3	\$ 161,463
507	RO:replacements for ADA and safety reason	Josephine	05/01/09	04/16/09	3	01/31/10		\$ -	4	8	1,064	8	4	0	1	N/A
508	RO: maintenance and sidewalk replacement	Josephine	05/01/09	04/24/09	3	10/31/09		\$ -	2	10	884	11	11	3	0	N/A
509	RO: Instructional space.	Josephine	04/01/09	04/01/09	3	12/31/09		\$ -	1	5	160	6	5	2	2	N/A
510	RO: Flooring Replacement.	Josephine	04/01/09	04/06/09	3	09/30/09		\$ -	0	1	0	1	0	0	0	N/A
511	RO: Window Replacement	Josephine	05/01/09	04/29/09	3	12/31/09		\$ -	6	4	935	8	10	3	0	\$ 282,139
512	RO: Illinois Valley	Josephine	04/01/09	04/29/09	3	09/30/09		\$ -	1	5	82	5	3	2	0	N/A
513	RO: Asphalt overlay	Josephine	04/01/09	03/18/09	3	07/31/10		\$ -	3	46	648	48	10	3	1	N/A
514	RO: Replace network	Josephine	04/01/09	04/24/09	3	12/31/10		\$ -	1	2	15	3	3	0	0	N/A
515	RO: Roof replacement	Josephine	04/01/09	04/21/09	3	10/31/09		\$ -	2	24	1,216	24	7	2	1	N/A
516	SW: Roofing repairs.	Coos	05/01/09	04/24/09	3	No Date		\$ 86,123	2	18	141	7	6	1	0	N/A
517	SW: Replace roadway lighting.	Coos	05/01/09	04/27/09	3	No Date		\$ 17,664	0	7	58	7	9	0	0	N/A
518	SW: Repair dryrot	Coos	05/01/09	04/22/09	3	No Date		\$ 73,087	14	6	189	14	4	3	1	N/A

Project Number	Project Name	County	Planned Project Start Date	Actual Project Start Date	Project Status	Scheduled Project Completion Date	Actual Project Completion Date	Expenditures to Date	Number of New Jobs Created	Number of Existing Jobs Sustained	Construction Hrs	Number of Oregon residents employed on a project	Oregon Vendors providing required goods or services	Oregon Subcontractors Hired	MWESB working on a project	Estimated Energy Savings (\$)
519	SW: Repair screen vents	Coos	05/01/09	04/20/09	3	No Date		\$ 9,677	0	4	17	4	1	0	0	N/A
520	SW: HVAC repairs.	Coos	05/01/09	04/27/09	3	No Date		\$ 98,908	1	6	346	6	1	0	0	\$ 128,620
521	SW: Structural repairs	Coos	05/01/09	04/21/09	3	No Date		\$ 37,527	1	5	135	5	1	0	1	N/A
522	SW: HVAC upgrade	Coos	05/01/09	04/27/09	3	No Date		\$ 105,344	3	7	348	7	4	0	0	\$ 150,740
523	SW: Sidewalks, asphalt repairs.	Coos	05/01/09	04/24/09	3	No Date		\$ 8,446	0	11	49	11	3	0	0	N/A
524	SW: Flooring	Coos	05/01/09	04/25/09	3	No Date		\$ 22,143	0	5	5	5	2	0	0	N/A
525	SW: Paint buildings	Coos	05/01/09	04/24/09	3	No Date		\$ 93,935	11	7	213	12	5	2	0	N/A
526	SW: Clean and seal building	Coos	05/01/09	04/30/09	3	No Date		\$ 7,876	0	3	0	3	0	0	0	N/A
527	SW: Remodel 4 ADA compliance	Coos	05/01/09	04/21/09	3	No Date		\$ 162,715	3	7	667	7	8	2	0	N/A
528	TB: renovation of Building	Tillamook	05/11/09	05/18/09	3	08/14/09		\$ 175,000	0	11	1,825	11	6	4	1	N/A
529	TV: Paving gravel lots	Malheur	04/30/09	04/28/09	3	09/18/09		\$ 66,456	0	16	772	7	3	2	0	N/A
530	TV: Repair asphalt parking lots	Malheur	04/21/09	04/10/09	3	09/04/09		\$ 20,598	0	7	732	0	1	0	0	N/A
531	TV: HVAC and energy efficiency	Malheur	04/23/09	04/16/09	3	09/18/09		\$ 249,982	4	8	242	6	2	1	0	N/A
532	TV: Restroom refurbish and upgrade	Malheur	04/21/09	04/10/09	5	09/03/09	07/31/09	\$ 238,122	1	25	2,047	18	17	6	1	N/A
533	TV: Roofing upgrade	Malheur	04/28/09	04/17/09	5	09/03/09	07/31/09	\$ 149,521	4	6	1,195	7	4	0	0	N/A
534	TV: install visual and audible alarms	Malheur	04/28/09	04/28/09	3	09/03/09		\$ 7,601	0	3	32	2	2	1	0	N/A
535	TV: ADA upgrades	Malheur	04/28/09	04/08/09	3	11/16/09		\$ 19,300	0	2	20	2	1	0	0	N/A
536	TV: Replace sidewalk	Malheur	04/21/09	04/16/09	5	06/30/09	05/08/09	\$ 19,914	0	5	112	5	5	2	0	N/A
537	TV: Replace sidewalk	Malheur	04/21/09	04/15/09	5	06/30/09	05/08/09	\$ 38,200	3	5	140	4	4	1	0	N/A
538	UM: Replace pool filtering system	Douglas	04/01/09	04/06/09	3	09/30/09		\$ 54,171	8	5	535	8	9	2	0	N/A
539	UM: ADA/Title 9 compliance issues	Douglas	04/01/09	02/16/09	3	09/30/09		\$ 151,580	12	18	1,848	25	27	9	4	\$ 62,743
540	UM: Remodel food service area	Douglas	04/01/09	02/16/09	3	09/30/09		\$ 18,883	0	9	194	9	4	0	0	N/A
541	UM: Replacement asbestos abatement	Douglas	04/01/09	03/23/09	3	06/30/09		\$ 98,485	9	10	972	13	11	4	2	N/A
542	UM: Remove hard water deposits	Douglas	04/20/09	04/30/09	3	09/30/09		\$ 267,865	6	7	1,595	8	10	0	0	N/A
543	UM: Restroom upgrades	Douglas	04/27/09	04/30/09	3	01/31/10		\$ 95,000	1	10	866	11	11	1	0	N/A
544	UM: Replace electrical panels	Douglas	04/27/09	04/30/09	3	11/30/09		\$ 80,490	1	7	798	7	3	0	0	N/A
545	UM: Replace sidewalks	Douglas	04/01/09	03/20/09	3	09/30/09		\$ 1,155,946	12	64	5,141	65	22	8	4	N/A
546	UM: Walkway security lighting	Douglas	04/27/09	04/29/09	3	06/30/09		\$ 31,261	1	1	49	2	2	0	0	N/A
547	UM: New motors and pumps	Douglas	04/20/09	04/29/09	5	06/30/09	06/30/09	\$ 57,859	0	6	106	6	3	2	1	N/A
								\$ 19,935,237	501	1,761	116,649	1,771	1,234	381	105	\$ 8,222,273

Project Status = 1) Not Started 3) On Schedule 4) Behind Schedule 5) Completed 6) Terminated Without Completion
0) UF / UA
UF =Unfunded Projects UA = Unassigned Project



SB 338 Report

August 17, 2009

Project Notes



#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
1	DAS				
2	DAS				
3	DAS	Carpet Replacement		This contract has been let but the work will not start until other Go Oregon construction work at this facility is complete. The work is staged in this manner to prevent any damage to the new carpet.	
4	DAS	L&I Bldg. Domestic Water Pipe Replacement			
5	DAS	Exterior Canopy- Pendleton 202		The numbers reported in line items 26 through 49 above include the design efforts for three projects that were combined under one design contract. The three projects that were combined are: -DAS_0005 Exterior Canopy - Pendleton 202 -DAS_0006 Chille...	
6	DAS	Chiller Replacement - Pendleton 201		The numbers to be reported in line items 26 through 49 are for construction activity only. The design effort for this project is listed in DAS_0005 - Exterior Canopy - Pendleton 202 because the design efforts for three projects were combined into one...	
7	DAS				
8	DAS				
9	DAS	Painting/Ceiling Tile/Restroom Improvement.		The numbers to be reported in line items 26 through 49 are for construction activity only. The design effort for this project is listed in DAS_0005 - Exterior Canopy - Pendleton 202 because the design efforts for three projects were combined into one...	The scope of work for this project includes replacement of all ceiling tile, repainting of all walls and doors, and renovation to 6 restrooms.
10	DAS	PSOB Fire System Upgrade - Ph. 2		This is a design build contract. The contractor is currently designing (engineering) the project and is expected to start work on site next month. No payment invoices have been submitted yet. This project is Phase 2 of the Portland State Office Building	This project is Phase 2 of the Portland State Office Building Fire Panel Replacement Project. Phase 2 is required by the City of Portland Fire Marshall to bring the rest of the buildings fire system up to code. Phase 1 replaced the fire panel under...
11	DOC	Replace Freezer Lighting at CDC		Contract Complete, paid contractor final payment. All material and labor paid.	

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
12	DOC				
13	DOC	Replace backup electrical system		Energy savings and CO2 savings will be calculated after determination of solar panel output. Issued design contract to Sunlight Solar for \$20,000. Design in progress, waiting for design documents. No billing received from Contractor yet.	
14	DOC	Install solar system		Energy savings and CO2 savings will be calculated after determination of solar panel output. Contract awarded to Christenson Electric. No billing received from contractor yet.	and food bank buildings at TRCI
15	DOC	Replace out of date Security System		Contract awarded to Portland Engineering. No billing received & paid in July.	out of date systems at TRCI.
16	DOC	Replace failing unit door control sys		Contract awarded to Portland Engineering. No billing received and paid in July.	systems with computer based system.
17	DOC	Replace warehouse Lighting at CDC		During construction on this contract, contractor encountered numerous electric deficiency's requiring correction to ensure compliance with Oregon Electrical Code. Change orders issued to correct deficiency's.	Efficient fluorescent lighting.
18	DOC	Electrical panel upgrades		Contract awarded to Robert A. Amey, work in progress. No billing received from contractor yet.	On electrical distribution panels for code compliance at all institutions. Project to be accomplished at SRCI in Ontario, PRCF in Baker City, EOCI in Pendleton, TRCI in Umatilla, CRCI in Portland, CCCF in Wilsonville, SFFC in Tillamook, DRCI in Madras...
19	DOC	Replace electronic security network	Tested existing fiber for reuse.	Contractor Act Cascades awarded fiber cabling testing to determine suitability for re-use. PLC software upgrade in process for award. Met on site with vendors to evaluate portions of system. No billing received for month of July.	Network at SRCI.
20	DOC	Replace Lighting for energy efficiency		Contract for first site (EOCI) awarded to Pendleton Electric. Project in close out, no billing received for month of July. Began solicitation for second site (Lakeview) anticipate work commencing in August.	Efficient LED fixtures in non inmate handling areas at all institutions. Project to be accomplished at SRCI in Ontario, PRCF in Baker City, EOCI in Pendleton, TRCI in Umatilla, CRCI in Portland, CCCF in Wilsonville, SFFC in Tillamook, DRCI in Madras, SCC
21	ODFW	Sandy Hatchery Parking Lot Construction			
22	ODFW	Denman Storage Bldg	Permit approved 07/20/09. Will begin work on project 08/04/09		

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
23	ODFW	PW Schneider Storage Bldg			
24	ODFW	Sauvie Island Storage Bldg	Construction is on schedule. Expected Completion Date is 08/10/09		
25	ODFW	Enterprise District Office Elevator	No work performed in the month of July.		
26	ODFW	New Bldg at Hatfield Marine Science Ctr			
27	ODFW				
28	ODFW				
29	ODFW				
30	ODFW				
31	ODFW				
32	ODFW	Salmon River Hatchery Heat Pumps			
33	ODFW	South Willamette District Office Replace Electric	Additional work required- need to submit request for change order to this contract.		
34	ODFW	Southwest Region Office HVAC System Upgrade			
35	ODFW	Cascade Hatchery Electrical Panel Upgrade			
36	ODFW	Oxbow Hatchery Electrical Service and Panel Upgrade	Entire Job was completed in June. All labor and material costs were incurred in June; no activity for July.		
37	ODFW				
38	ODFW				
39	ODFW	Rock Creek Hatchery Supply Pipeline Replacement			
40	ODFW	Salmon River Hatchery New Residence	No activity on this project in July. Just waiting for home to be constructed.		
41	ODFW	EE Wilson Wildlife Area Residence Replacement			
42	ODFW	Willamette Falls Fishway Entrance 1 Foundation Settlement Repair - Phase 1			
43	ODFW	North Nehalem Hatchery Supply Pipeline Replacement			
44	ODFW	Canyon Creek Meadows Dam Removal Project - Phase 1	These figures have been estimated and will be adjusted after July billings have been generated.		
45	ODF				
46	ODF				
47	ODF				
48	ODF				

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
49	ODF	Replace vinyl flooring, refinish casewk			
50	ODF				
51	ODF				
52	ODF				
53	ODF				
54	ODF				
55	ODF				
56	ODF				
57	ODF	Replace electrical distribution & service		First phase of project complete. Awaiting materials for 2nd phase.	
58	ODF	Repair soffits at loading dock - Processing			
59	ODF	Replace siding, repaint ODFW office			
60	ODF				
61	ODF	Replace siding, repaint Warehouse			
62	ODF	Replace roof and structural repairs			
63	ODF	COD John Day/Sisters Relocation Project			
64	OUS	Owens Hall Comprehensive Renovation	Invoice date: 7/31/09 Services provided through June 25, 2009	Klamath County Community Development: \$1630.35 Cash Way: \$51.20 Pro-Grass: \$200.00 \$1570 of SELP was from work performed in June 2009.	
65	OUS	Campus Loop Phase II			
66	OUS				
67	OUS	Physical Education Building			
68	OUS				
69	OUS				
70	OUS				
71	OUS				
72	OUS				
73	OUS				
74	OUS				
75	OUS				
76	OUS				
77	OUS				
78	OUS				
79	OUS				
80	OUS				

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
81	OUS				
82	OUS				
83	OUS				
84	OUS				
85	OUS				
86	OUS				
87	OUS				
88	OUS	HVAC upgrade-CPS	Project completed, nothing to report		
89	OUS				
90	OUS				
91	OUS	Door Access Control-classrooms	Project completed, nothing to report	Project completed, nothing to report	
92	OUS	Fire Alarm System-Art East			
93	OUS	Fire Alarm System-ECP			
94	OUS				
95	OUS				
96	OUS				
97	OUS				
98	OUS				
99	OUS				
100	OUS	Variable Frequency Drive		Contractor has not billed. Project manager will contact them	
101	OUS				
102	OUS				
103	OUS				
104	OUS				
105	OUS				
106	OUS				
107	OUS				
108	OUS				
109	OUS				
110	OUS				
111	OUS				
112	OUS	Fire Alarm System Replacement			
113	OUS				
114	OUS	Elevator Upgrade-CH			
115	OUS	Elevator Upgrade-EP	The project is progressing well.		
116	OUS				
117	OUS				
118	OUS	HVAC Upgrade MN	No work performed on the project this month.	No work performed in July per project manager.	
119	OUS				

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
120	OUS	Expanded Digital Control			
121	OUS				
122	OUS				
123	OUS				
124	OUS	Roof replacement-CE	No work was done in July, no report received from contractor	Per project manager, no work done on this project in July	Henris Roofing invoice for materials only was received 5/1/09, will be paid next month, May
125	OUS	Storm Water drainage Improvements			
126	OUS				
127	OUS	Roof Replacement-Music	Job was scheduled for June 15th. We were postponed until Aug 10 due to school activities. We could only deliver product and we did on June 15th. No progress will occur in the month of July.		
128	OUS	Roof Replacement Theatre			
129	OUS	Campbell-Convert Steam to Hydronic			
130	OUS				
131	OUS				
132	OUS				
133	OUS	Fire Alarm System replacement			
134	OUS	Classroom Modernization CH			
135	OUS	Toilet Upgrades-Science Bldg			
136	OUS				
137	OUS	Roof replacement McNeal			
138	OUS				
139	OUS				
140	OUS				
141	OUS	Exterior Building Repairs			
142	OUS				
143	OUS				
144	OUS				
145	OUS				
146	OUS	AB Acad. Modern. & Access.			
147	OUS	Electric Upgrades and Rplcment			
148	OUS				
149	OUS				
150	OUS	Mechanical Upgrades and Replacement			

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
151	OUS	Pierce Library Roof Repair / Replacement		Roof Repair and Replacement Underway. Project approx. 30% complete. On Schedule. WC Construction data did not load for July. WC Construction (Contractor) data for July to be entered next report period.	
152	OUS				
153	OUS	Deferred Interior Finishes			
154	OUS	Dorion Hall Demolition & Site Improvements	Funding was released for Building Demo, Sitework and Electrical. Due to late approval of funds in EWA #2 and EWA #3 project is 3 weeks behind schedule. Building Demo is 50% complete through July. Electrical Equipment has been ordered with an estimated lea	Building Demolition is estimated at 50% complete at end of July. Site Electrical Equipment has been ordered. With release of EWA #2 and EWA #3, contractor estimates approx. 3 wks delay in original completion date. Project is still expected to be substanti	
155	OUS	Academic Modernization			Shaw Library: HVAC Replacement, Semon Hall: Dental Hygiene Reception Area Remodel, Boivin Hall: Acid Drain Replacement, Chemical Storage Room Renovation, Chemistry Lab Renovation
156	OUS	NH Acad Modernization and Accessibility			New and expanded instructional space
157	OUS	CH Classroom Upgrades			abate and upgrading old classrooms
158	OUS	Campus-Steamline Phase II			
159	OUS	LH Academic & Program Improvements			
160	OUS				
161	OUS				
162	OUS	Campus Roof Repair and Replacement			
163	OUS	E&G Bldg. Code and Life Safety Improvements			
164	OUS	Reed Hall-Sys Upgrades & Renov		Project Management, Lori Fulton - \$924.00, VF430836 Construction Management, Hayley Brown - \$10.00, VF430836	
165	OUS				
166	OUS	Science Building 2 Modernization			
167	OUS				
168	OUS				

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
169	OJD	Supreme Court Re-Roofing Project	The hours, labor dollars and material supply information listed on this form are only for Anderson Roofing. Construction dollars include the req'd prevailing wages plus benefits.	The repairs to the roof of the Supreme Court Building are complete. However, the building's courtroom ceiling and the bailiff station located inside the courtroom sustained some damage during the project. The Contractor is coordinating repair of the...	
170	OMD				
171	OMD	Roseburg Armory Floor Tile Replacement	No work was done, just the final payment was made on 31 July 2009.	The COP is the to date paid out by OMD. The non labor \$244.75 Rodda, \$1374.00 Armorgarage.	
172	OMD	Hermiston HVAC For Drill Floor		The COP is the to date total paid out by OMD. The non labor is \$133.25 DJC, \$3750.00 design, \$815.82 American Matrix.	
173	OMD	Redmond COUTES - Restroom Remodel	Project substantially completed on July 25, 2009.	The COP is the to date total that has been paid out by OMD. The non labor is \$250.00 BOLI, \$3750.00 design.	
174	OMD	LaGrande Armory Back Up Generator	This project is complete. Final payment was made in Aug. so the next report will reflect such.	The COP is the to date pay out by OMD. The non labor \$660.39 is to Waldrop Oil. This project is complete. OMD made the final payment on 5 Aug. and next report will reflect that.	
175	OMD	Bend Armory Back Up Generator	Other Misc costs combine 'Misc costs' (\$1881) and 'Non Labor & Material' (\$1453). Job completed July 09.	This project is substantially complete. This means the contractor has finished work on the project site. The only thing OMD is waiting on is the close out documents from the contractor. Then OMD's project manager can close out the project to include final	
176	OMD	Camp Withycombe Bld.6101 Reroof	Project 100% complete.	The COP is the to date paid out by OMD. The non labor is \$133.25 and \$43.13 to DOJ.	
177	OMD	Salem Armory Floor Tile Replacement	3 Kings performed no work in the month of July under this contract. Work NOT complete.	The COP is the to date paid out by OMD. The non labor is \$2068.53 DJC, \$3665.78 Coastwide, \$244.78 Rodda, \$1775.00 Sparkle & Clean, \$3555.00 Cascade Sound, \$250.00 BOLI.	
178	OMD	Jackson Armory Door Replacement	This project is complete and paid in full on the 27th of July 2009.	The COP is the to date paid out by OMD.	
179	OMD	Camp Rilea Replace Roofing & Siding	Project scope of work completed pending finalpunchilis. Richart Family Inc resident contractor Sherwood, Oregon.	The COP is the to date payout by OMD. The Non Labor & Material Costs: \$2,646.00 DOJ, \$133.25 DJC, \$340.37 US Bank.	
180	OMD	Hood River Armory Storage Building	Contractor is Hale Construction NW, Hood River, Oregon. Contract is \$470,720. The \$270K not funded for this project will be funded from two other stimulus projects at this site and from existing budget.	The COP is the to date paid out by OMD. The non labor is BOLI \$470.72.	

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
181	OMD	Grants Pass Armory Parking Lot Upgrade	Work is completed. The reported hours and costs are from subcontractors completing the conversion of gas appliances for the project. All parking lot work, including the 20 jobs sustained for Copeland Sand and Gravel Inc. represent hours worked in June an	The COP is the to date paid out by OMD. The non labor is \$143.50 DJC, \$4900.00 for design.	
182	OMD	Kleiver Armory Parking Lot Upgrade	project completed 20 Jul 09. The "other" \$250.00 is BOLI fees that OMD paid.	The COP total is a to date expenditure. There is still \$107,728.67 remaining to be spent.	Excavate, install fabric and rock, replace degated spots. Crack seal and 2" overlay on remaining parking lot.
183	OMD	Hood River Armory Compound Improvem'ts	The contractor completed work in July and has not yet submitted a SB338 (13 Aug. 09)	The COP is the to date total paid out by OMD. The non labor is \$138.38 DJC, \$2280.60 DOJ, \$250.00 BOLI. This project was substantially complete on 17 July 2009. The contractor finished up the punch list items in July. OMD is waiting on final admin papers	
184	OMD	Hood River Armory Interior Remodel	Plumbing, electrical, concrete, misc iron, and wall framing work proceeded in July. Contractor applied to DEQ per asbestos abatement. Interior remodel of kitchen, finishes throughout armory, complete data/telecom rewire, new doors/windows...	The COP is the total to date that OMD has paid out. The Non Labor & Material Cost: \$133.25 is DJC, \$18.17 UPS, \$16,899.00 PP&L, \$469.90 BOLI.	Interior remodel of kitchen, finishes throughout armory, complete data/telecom rewire, new doors/window, utilities and HVAC system.
185	OMD	BIAK Restroom & Shower Facility		The COP is the to date total that OMD has paid out. The non labor is BOLI \$133.25, Miller Consulting \$2,700.00	This project adds a new 2165 square foot restroom and shower facility (male/female).
186	OMD	Coos Bay Armory - Interior Remodel	This July 09 report, dated 7/28/09, includes materials adn labor costs from subcontractors: Johnson Rock, Umpqua Sheet Metal, GB Reese Electric, Bay Area Door, Fieldstone Excavation, CA Mesa Plumbing and R.E. Noah an Co.	The COP is the total stimulus to date that has been paid out by OMD. The Non Labor is: \$143.50 DJC, \$716.70 Salem Blue, \$1361.20 City of Coos Bay, \$489.69 BOLI.	This project remodels the female restroom and adds shower and locker room area. The project replaces single pane windows and upgrades lighting throughout. The project improves the parking to include ADA signage and parking, and expands the vehicle...
187	OMD	Prineville CORC - Interior Remodel		The COP is the total to date paid out by OMD. The Non labor is \$745.02 Salem Blue, \$169.13 DJC, \$642.00 Campbell Communications, \$677.00 BOLI.	
188	OPRD				
189	OPRD				
190	OPRD				
191	OPRD				
192	OPRD				
193	OPRD	Wallowa Lake SP Docks			
194	OPRD				

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
195	OPRD				
196	DSL				
197	DSL	juniper removal			
198	DSL	Portland Harbor Boundary Survey			
199	DSL				
200	ODOT				
201	ODOT				
202	ODOT				
203	ODOT				
204	ODOT				
205	ODOT				
206	ODOT				
207	ODOT				
208	ODOT				
209	ODOT				
210	ODOT				
211	ODOT				
212	ODOT				
213	ODOT				
214	ODOT				
215	ODOT				
216	ODOT				
217	ODOT				
218	ODOT				
219	ODOT				
220	ODOT				
221	ODOT				
222	ODOT				
223	ODOT				
224	ODOT				
225	ODOT				
226	ODOT				
227	ODOT				
228	ODOT				
229	ODOT				
230	ODOT				
231	ODOT				
232	ODOT				
233	ODOT				
234	ODOT				

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
235	ODOT				
236	ODOT				
237	ODOT				
238	ODOT				
239	ODOT				
240	ODOT				
241	ODOT				
242	ODOT				
243	ODOT				
244	ODOT				
245	ODOT				
246	ODOT				
247	ODOT				
248	ODOT				
249	ODOT				
250	ODOT				
251	ODOT				
252	ODOT				
253	ODOT				
254	ODOT				
255	ODOT				
256	ODOT				
257	ODOT				
258	ODOT				
259	ODOT				
260	ODOT				
261	ODOT				
262	ODOT				
263	ODOT				
264	ODOT				
265	ODOT				
266	ODOT				
267	ODOT				
268	ODOT				
269	ODOT				
270	ODOT				
271	ODOT				
272	ODOT				
273	ODOT				

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
274	ODOT	Distict 12 Office Deferred Maintenance	Contractor Northwest Building Contractors	Long Material delay. Contractor good to work with. Contractor Northwest Building Contractors ESB firm Cert 6066	
275	ODOT				
276	ODOT				
277	ODOT				
278	ODOT				
279	ODOT				
280	ODOT				
281	ODOT				
282	ODOT				
283	ODOT				
284	ODOT				
285	ODOT				
286	ODOT				
287	ODOT				
288	ODOT				
289	ODOT				
290	ODOT				
291	ODOT				
292	ODOT				
293	ODOT				
294	ODOT				
295	ODOT				
296	ODOT				
297	ODOT				
298	ODOT				
299	ODOT				
300	ODOT				
301	ODOT				
302	ODOT				
303	ODOT				
304	ODOT				
305	ODOT				
306	ODOT				
307	ODOT				
308	ODOT				
309	ODOT				
310	ODOT				

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
311	ODOT	Boardman Deferred Maintenance	Contractor Suniker LLC - ESB, Mintority Business	Contractor Suniker LLC, Good Job, Materials Supply Problems, Long Ship Delays	
312	ODOT				
313	ODOT				
314	ODOT				
315	ODOT				
316	ODOT				
317	ODOT				
318	ODOT				
319	ODOT				
320	ODOT				
321	ODOT				
322	ODOT				
323	ODOT				
324	ODOT				
325	ODOT				
326	ODOT				
327	ODOT				
328	ODOT				
329	ODOT				
330	ODOT				
331	ODOT				
332	ODOT				
333	ODOT				
334	OYA	Agency Wide Central Control Renovation NCYCF			Agency-wide Central Control Room Renovation Project - various locations. Project replaces outdated, end of life access control with programmable logic control (PLC) system in each Central Control Room.
335	OYA	Agency Wide Central Control Renovation OCYCF			Agency-wide Central Control Room Renovation Project - various locations. Project replaces outdated, end of life access control with programmable logic control (PLC) system in each Central Control Room.
336	OYA	Agency Wide Central Control Renovation RiverBend			Agency-wide Central Control Room Renovation Project - various locations. Project replaces outdated, end of life access control with programmable logic control (PLC) system in each control room.

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
337	OYA	Agency Wide Central Control Renovation RYCF			Agency-wide Central Control Room Renovation Project - various locations. Project replaces outdated, end of life access control with programmable logic control (PLC) system in each Central Control Room.
338	OYA	Agency Wide Central Control Renovation TYCF			Agency-wide Central Control Room Renovation Project - various locations. Project replaces outdated, end of life access control with programmable logic control (PLC) system in each Central Control Room.
339	OYA	Agency Wide Central Control Renovation EOYCF			Agency-wide Central Control Room Renovation Project - various locations. Project replaces outdated, end of life access control with programmable logic control (PLC) system in each Central Control Room.
340	OYA	Agency Wide HVAC Renovation and Repair NCYCF			Direct digital controllers (DDC) are at the end of useful life and will be replaced. Where possible and appropriate additional zone controls will be installed to increase energy efficiency.
341	OYA	Agencywide HVAC Renovation and Repair RYCF		project nearing completion	Direct digital controllers (DDC) are at the end of useful life and will be replaced. Where possible and appropriate additional zone controls will be installed to increase energy efficiency.
342	OYA	Agencywide HVAC Renovation and Repair OYCF		project nearing completion.	Direct digital controllers (DDC) are at the end of useful life and will be replaced. Where possible and appropriate additional zone controls will be installed to increase energy and efficiency.
343	OYA	Agency wide HVAC Renovation and Repair EOYCF			Direct digital controllers (DDC) are at the end of useful life and will be replaced. Where possible appropriate additional zone controls will be installed to increase energy efficiency.
344	OYA	Agencywide HVAC Renovation and Repair RiverBend			Replace outdated end of life HVAC unit with energy efficient heat pump system.
345	OYA	Camp Tillamook Appliance Replacement		Phase 1 complete, phase 2 has begun	Camp Tillamook provides centralized food service for both Tillamook YCF and Camp Tillamook. The project replaces end of life kitchen appliance and expands food service capacity. Includes new range and walk-in freezer.

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
346	OYA	Rogue Valley YCF Fire Barrier and Perimeter Fence Road			Rogue Valley YCF Fire Barrier/Perimeter Fence Road; Fields around the facility have had grass fires over the past years. The project provides for a fire barrier and security perimeter road and enhances the functionality of the facility.
347	OYA				
348	OYA	Hillcrest Walk-in Complex Replacement			Replaces walk-in complex of 2 freezers and 2 refrigerators
349	OYA	RiverBend Facility Sewage Lagoon & Effluent Irrigation Expansion			Provides for feasibility study, design services, and construction of expanded effluent irrigation. Expanded irrigation is needed because of short land application window. Project expands sewage lagoon system capacity and replaces end of life system...
350	OYA	MacLaren Campus Gas HVAC Conv.		Gas lines installed to front cottages. Architect is providing plans for each building. Mechanical engineer provided options for various building systems.	Replaces antiquated boiler plant with energy efficient HVAC units at each building.
351	OYA	Hillcrest - Zeta Living Unit Renovation			Renovation of 24 bed high security/mental health facility. The project extends the useful life of the building and adapts the facility to a different use; i.e. a secure intensive treatment living unit. Project will remove hazardous materials, replace room
352	OYA	Tillamook YCF School House Cons Comp			Tillamook YCF School House Construction Completion - This construction project was started in 2006 and never completed. Currently the building is sealed up from the elements and not in use. Camp Tillamook and Tillamook YCF would like to consolidate...
253	OYA				
354	OYA	MacLaren Deferred Maintenance		Project is progressing nicely. Doors installed on south side of block (Phase 1) concrete slabs poured inside cells for bed area, old lighting fixtures removed, wall and floor cracks filled with bondoe. Raceway installed above doors and bondo work...	MacLaren Deferred Maintenance • The project breaks down into various projects • CIU/Geer Phase II - replace doors and exterior windows with maximum security doors, add access control programmable logic control (PLC) system and closed-circuit television...

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
355	OYA	Hillcrest Deferred Maintenance			The project breaks down into various deferred maintenance projects. • Hillside BCP Information Technology (IT) Recovery Site Security • CCTV Expansion • Food Service Building Security Enhancements • Site Improvements (expand parking capacity and revamp...
356	OYA				
357	OYA	Oak Creek Fire Barrier/Perimeter Fence Rd			Oak Creek YCF Fire Barrier/Perimeter Fence Road • Accomplishes work not included in the scope of the 07 09 renovation. Provides fire barrier for facility and security perimeter road enhancing the functionality of the facility.
358	OYA	Hillcrest Gymnasium Renovation			Replace bleachers, provide sound dampening and repaint the interior
359	OYA	Hillcrest High School Interior Paint and Asbestos Floor Tile Replacement	1		Hillcrest High School Interior Paint and Asbestos Floor Replacement • Replace asbestos floor tile and repaint surfaces as needed (the removal of the asbestos floor and the cove base involves damage to the wall surface which will need to be repainted).
360	OYA	MacLaren High School Interior Paint and Asbestos Floor Replacement			Replace asbestos floor tile and repaint surfaces as needed. (The removal of the asbestos floor and the cove base involves damage to the wall surface which will need to be repainted.
361	CCWD	BM: Safety and Security			
362	CCWD	BM: Aging Infrastructure with Primary Safety Implications			
363	CCWD	BM: Aging Infrastructure with Secondary Safety Implications or Principal Energy-Use Implications			
364	CCWD	CE: New parking spaces to deal with current enrollment growth			
365	CCWD	CE: Replace Aging Electrical Distribution System & Electrical Upgrades			
366	CCWD	CE: Disability Access improvements including four elevators for existing buildings			
367	CCWD	CE: Roadway Repair			

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
368	CCWD	CE: Sidewalk/Hand Rail Replacement			
369	CCWD	CE: Fire Reduction			
370	CCWD	CE: Painting, Flooring and Roof Maintenance			
371	CCWD	CE: Building Weatherization - Insulation and Windows			
372	CCWD	CE: Air conditioning and fire suppression systems			
373	CCWD	CE: retrofit buildings to respond to enrollment growth.			
374	CCWD	CH: Replace failing roof.			
375	CCWD	CH: Renovate building 50, expand facility.			
376	CCWD	CH: Replace failing storage barn			
377	CCWD	CH: HVAC and mechanical system capital maintenance.			
378	CCWD	CH: Upgrade utility infrastructure			
379	CCWD	CH: Front entry roadway re-build.			
380	CCWD	CH: Upgrade primary electrical distribution			
381	CCWD	CH: Replace aged rooftop air handlers			
382	CCWD	CH: Upgrade elevators			
383	CCWD	CH: Replace worn handicapped operator doors.			
384	CCWD	CH: Upgrade exterior lighting systems.			
385	CCWD	CH: Upgrade air doors			
386	CCWD	CH: Replacement Space, Training and Economic Center, TI costs only.			
387	CCWD	CH: Replace deteriorated training fire station.			
388	CCWD	CH: Replace shift quarters.			
389	CCWD	CH: Create classroom			
390	CCWD	CH: Replace failing metal roof			
391	CCWD	CH: Re-roof Santiam Center			
392	CCWD	CL: Replace aging college communications infrastructure			

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
393	CCWD	CL: Complete duct cleaning.			
394	CCWD	CL: Install roll up security doors on paint booth.			
395	CCWD	CL: Replace Industrial wing roll up doors.			
396	CCWD	CL: Repair/renovate			
397	CCWD	CL: Energy efficiency controls installed to HVAC system.			Due to the large cost of this work, it has been rolled into Project #396. Costs will therefore be reported on #396 report.
398	CCWD	CL: Repaint courtyard blue handrails and Barlow exterior doors.			
399	CCWD	CL: Ceiling tiles replacement.			
400	CCWD	CL: Patch and paint interior walls throughout.			
401	CCWD	CL: Carpet and linoleum replacement throughout non-remodeled areas.			
402	CCWD	CL: Energy efficiency controls installed to HVAC system.			
403	CCWD	CL: Patch and paint interior walls throughout.			
404	CCWD	CL: Replace floor covering in selected areas.			
405	CCWD	CL: Energy efficiency controls installed into HVAC system.			
406	CCWD	CL: Energy efficiency controls installed into HVAC system.			
407	CCWD	CL: Energy efficiency system installed into HVAC system.			
408	CCWD	CL: Install new fire alarm system.			
409	CCWD	CL: Repair/renovate air handling units, exhaust fans, pumps, fans and controls.	Sub-contractor is registered as ESB.		One of the sub-contractors is Progressive Mechanical and they are an ESB business (#3141).
410	CCWD	CL: Building wide air test and balance			
411	CCWD	CL: Energy efficiency system installed into HVAC system.			
412	CCWD	CL: Repair/renovate air handling units, exhaust fans, pumps, fans and controls.			

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
413	CCWD	CL: Ceiling tile replacement with recessed light fixtures			
414	CCWD	CL: Patch and paint interior walls throughout.			
415	CCWD	CL: Floor tile replacement in all three building.			
416	CCWD	CL: Repair/renovate air handling units, exhaust fans, pumps, fans and controls.			
417	CCWD	CL: Energy efficiency system installed into HVAC system.			
418	CCWD	CL: Energy efficiency system installed into HVAC system.			
419	CCWD	CL: Energy efficiency system installed into HVAC system.			
420	CCWD	CL: Various electrical improvements.			
421	CCWD	CT: Visual Arts Building			
422	CCWD	CT: Library Building			
423	CCWD	CT: MERTS I			
424	CCWD	CT: Alder Hall			
425	CCWD	CT: Patriot Hall			
426	CCWD	CT: Campus-Wide			
427	CCWD	CT: Performing Arts Center			
428	CCWD	CT: Forerunner Teaching Vessel			
429	CCWD	CT: Forerunner Teaching Vessel - Rebuild floating dock			
430	CCWD	CT: Josie Peper Building			
431	CCWD	CG: heating/ventilation system components			
432	CCWD	CG: Upgrade HVAC system			
433	CCWD	CG: windows			
434	CCWD	CG: windows			
435	CCWD	CG: fire sprinkler system			
436	CCWD	CG: Replace AC condenser units.			
437	CCWD	KL: Concrete repair			
438	CCWD	KL: Replace locks			
439	CCWD	KL: Pipe irrigation canal	All project work is completed. Awaiting contract closeout documents and final costs.		

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
440	CCWD	KL: Paint			
441	CCWD	KL: Parking lot			
442	CCWD	KL: Carpeting			
443	CCWD	KL: Windows, doors	This project has been combined with job 444, residing of building 2 & 3 for contracting purposes. Job 443 costs and labor will be tracked and reported separately.		
444	CCWD	KL: Re-side			
445	CCWD	LA: ADA Compliance			
446	CCWD	LA: security lighting			
447	CCWD	LA: carpeting			
448	CCWD	LA: preparation to install card access security			
449	CCWD	LA: Remove asbestos insulation			
450	CCWD	LA: Infrastructure to allow the installation of a college-wide emergency communication system.			
451	CCWD	LA: electrical system, water, sub-metering			
452	CCWD	LA: Electrical upgrades -			
453	CCWD	LA: sewer piping			
454	CCWD	LA: roofs			
455	CCWD	LA: restrooms			
456	CCWD	LA: classroom utility and infrastructure improvements			
457	CCWD	LA: smart class room audio and technical infrastructure			
458	CCWD	LA: paint spray booth			
459	CCWD	LA: Replace tile			
460	CCWD	LB: HVAC mechanical, insulation, ductwork maintenance			
461	CCWD	LB: insulation, glazing			
462	CCWD	LB: electrical transformers	Contractor waiting for materials which are expected in August.		
463	CCWD	LB: Upgrade exterior corridor lighting.	Retrofitted light fixtures.		
464	CCWD	LB: Upgrade sidewalk lighting.	waiting for the rest of the materials in order to be installed		

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
465	CCWD	LB: Tile and carpet replacement			
466	CCWD	LB: Upgrade energy management/HVAC control system network.			
467	CCWD	LB: Upgrade hot water circulating pumps			
468	CCWD	LB: Improve lighting fixtures on existing poles			
469	CCWD	LB: rigging system			
470	CCWD	LB: Ceiling, lighting, wall surface and flooring			
471	CCWD	LB: Asphalt road and parking lot area for student and staff egress.			
472	CCWD	LB: Connect to city water system for drinking water.			
473	CCWD	LB: kitchen	Preparation of concrete floor, leveling & smoothing of area for freezer/cooler. Equipment delivered at end of July. Final install in August.		
474	CCWD	MH: Stage Rehabilitation			
475	CCWD	MH: Classroom Painting and Flooring Upgrades			
476	CCWD	MH: Restroom ADA Upgrades			
477	CCWD	MH: Roof Replacement			
478	CCWD	MH: Reconfigurations			
479	CCWD	MH: Science Labs ADA Upgrades			
480	CCWD	MH: Dental Labs ADA Upgrades			
481	CCWD	OC: security cameras			

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
482	CCWD	OC: Notification system and PA system			Western States is under contract and proceeding with design build development of project.
483	CCWD	OC: Generator			Western States is currently under contract and proceeding with design build work for this project.
484	CCWD	OC: Add access hardware for Audubon door.			
485	CCWD	OC: Add access hardware at patio door.			
486	CCWD	PO: Mass Notification System			NOTE: Items 36 - 57, no invoice received/paid to date; however, P.O. totaling \$67,480 were issued this month and \$25,300 were issued last month.
487	CCWD	PO: ADA Upgrades			Donkin Constr. /ESB, has started modifying curb cuts we expect to let two additional contracts for facilities modifications by end of week. Items 36-57, no invoices received/paid to date.
488	CCWD	PO: Voice over IP			
489	CCWD	PO: centralized clock system			
490	CCWD	PO: Fire/Life Safety Upgrades			No invoices received yet for material or labor costs.
491	CCWD	PO: Electrical Upgrades for Arc Fault protection			NOTE: Work has begun; however, we've received no invoices to date.
492	CCWD	PO: Environmental Maintenance/Upgrades			

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
493	CCWD	PO: Energy Management System			Work has begun; however, no invoices received to date.
494	CCWD	PO: water supply lines			
495	CCWD	PO: Concrete settlement repairs/Seismic Upgrades			Contract was awarded on 5/5/09. Work to begin by end of the week.
496	CCWD	PO: Roadways/Parking lots repaving and seal coats			No new invoices received this month.
497	CCWD	PO: T-12 lighting			Work has begun; however we've received no invoices to date.
498	CCWD	PO: boilers	There was no stimulus work done this month.		
499	CCWD	PO: Gym flooring			No invoices received to date.
500	CCWD	PO: swimming pool decking			New grills for deck are on order, calk joints to be striped and replaced starting 5/9/09.
501	CCWD	PO: Grounds Greenhouse & Shade house	There was no stimulus work done this month.		
502	CCWD	PO: Skylight Replacements			No invoices received to date.
503	CCWD	PO: boilers			
504	CCWD	PO: Parking Lot Lighting	There was no stimulus work done this month.		Contract was awarded on 04/16/09. Work has begun; however we've received no invoices to date.
505	CCWD	RO: Replacement of electrical panels.			
506	CCWD	RO: Replacement of Aging HVAC Units			

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
507	CCWD	RO: Deck and handrail replacements for ADA and safety reasons.			
508	CCWD	RO: Concrete maintenance and sidewalk replacement			
509	CCWD	RO: Instructional space.			
510	CCWD	RO: Flooring Replacement.			
511	CCWD	RO: Window Replacement in Classroom Buildings.			
512	CCWD	RO: Illinois Valley			
513	CCWD	RO: Asphalt overlay and lighting for parking lots and roads.			
514	CCWD	RO: Replace network and communication infrastructure			
515	CCWD	RO: Roof replacement			
516	CCWD	SW: Roofing repairs.			
517	CCWD	SW: Replace roadway and parking lot lighting.			
518	CCWD	SW: Repair dryrot			
519	CCWD	SW: Repair screen vents			
520	CCWD	SW: HVAC repairs.			
521	CCWD	SW: Structural repairs			
522	CCWD	SW: HVAC upgrade			
523	CCWD	SW: Sidewalks, asphalt and concrete repairs.			
524	CCWD	SW: Flooring			
525	CCWD	SW: Paint the classroom buildings and laboratories			
526	CCWD	SW: Clean and seal building			
527	CCWD	SW: Remodel 4 bathrooms for ADA compliance			
528	CCWD	TB: renovation of the Career and Technical Building	Job is progressing on schedule and it is expected to be done on time. At that time, the payment application will be submitted for review and payment made to the General Contractor. Due to the short time-frame for this project, the contractor has requested		TBCC contacted four Local General Contractors to provide a quote for the project. Two of the Contractors dropped out during the first week of the Bid Process and a third dropped out 1 week prior to the due date. Due to the lack of interest in the project

#	Agency	Project Name -	Contractor Comments -	Agency Comments -	Additional Project Information -
529	CCWD	TV: Paving gravel lots			
530	CCWD	TV: Repair asphalt parking lots			
531	CCWD	TV: HVAC and energy efficiency			
532	CCWD	TV: Restroom refurbish and upgrade			
533	CCWD	TV: Roofing upgrade			
534	CCWD	TV: install visual and audible alarms with strobes			
535	CCWD	TV: ADA upgrades			
536	CCWD	TV: Replace sidewalk			
537	CCWD	TV: Replace sidewalk			
538	CCWD	UM: Replace pool filtering system and supporting piping.	Report is for North Umpqua		Demolition complete
539	CCWD	UM: ADA/Title 9 compliance issues	In process.		Architectural plans in process
540	CCWD	UM: Remodel food service area			Demolition complete
541	CCWD	UM: Replacement and asbestos abatement			Demolition complete
542	CCWD	UM: Remove hard water deposits			Completed research of access points.
543	CCWD	UM: Restroom upgrades			Demolition started on 4 restrooms
544	CCWD	UM: Replace electrical panels and main control cabinets			One Building complete
545	CCWD	UM: Replace sidewalks			Sidewalks and paving in process
546	CCWD	UM: Walkway security lighting			removal of pre-existing lighting
547	CCWD	UM: New motors and pumps			The pumps are removed



SB 338 STIMULUS PACKAGE



Go Oregon Agency Contacts

Agency	Name	Phone	Email
DAS	Randy C. Gengler	503-378-2381	randy.gengler@das.state.or.us
DOC	Vern Rowan	503-934-1012	vernon.r.rowan@state.or.us
DSL	Pamela Konstantopoulos	503-986-5283	Pamela.Konstantopoulos@state.or.us
ODF	Bob McKee	503-945-7503	robert.p.mckee@state.or.us
ODFW	Enrique Rodriguez	503-947-6159	Enrique.G.Rodriguez@state.or.us
ODOT	Virginia K. Carey	503-986-5800	virginia.k.carey@state.or.us
OJD	Bob Baxter	(503) 986-6410	Robert.A.Baxter@state.or.us
OMD	Roy Swafford	503-584-3596	roy.swafford@or.ngb.army.mil
OPRD	Bob Reitmajer	503-986-0753	bob.reitmajer@state.or.us
OUS	Bob Simonton	541-346-5728	bob_simonton@ous.edu
OYA	Shawna Hill	503-981-2560	shawna.hill@state.or.us
CCWD	Use Link :		http://www.oregon.gov/CCWD/stimulus/CommunityCollegesProjectContactsList.pdf
