

PSST (SLIP BASE) - FIELD VERIFICATION OF POST LENGTHS

Project Name: _____

Contract No.: _____

Date: _____

Preparer: _____

Refer to Standard Drawings: TM200, TM681, TM688

Hwy./Sta. or M.P. _____
(Per post data table. If different, explain why.)

Sign No. _____


*Post Location: Lt. Ctr. Rt.

*For multi-post installations, use a separate form for each post.

** Note: Enter all measurements in feet to the nearest hundredth.

Post Length Calculation (Ft.)

Primary Sign Height
Space (2") (+) 0.17'
Secondary Sign Height (+)
Elevation D (+)
Elevation B (-)
Stub Height w/plates (3.5") (-) 0.29'
Total (Verified Post Length) ..
Verified Post Size
(Per TM681)

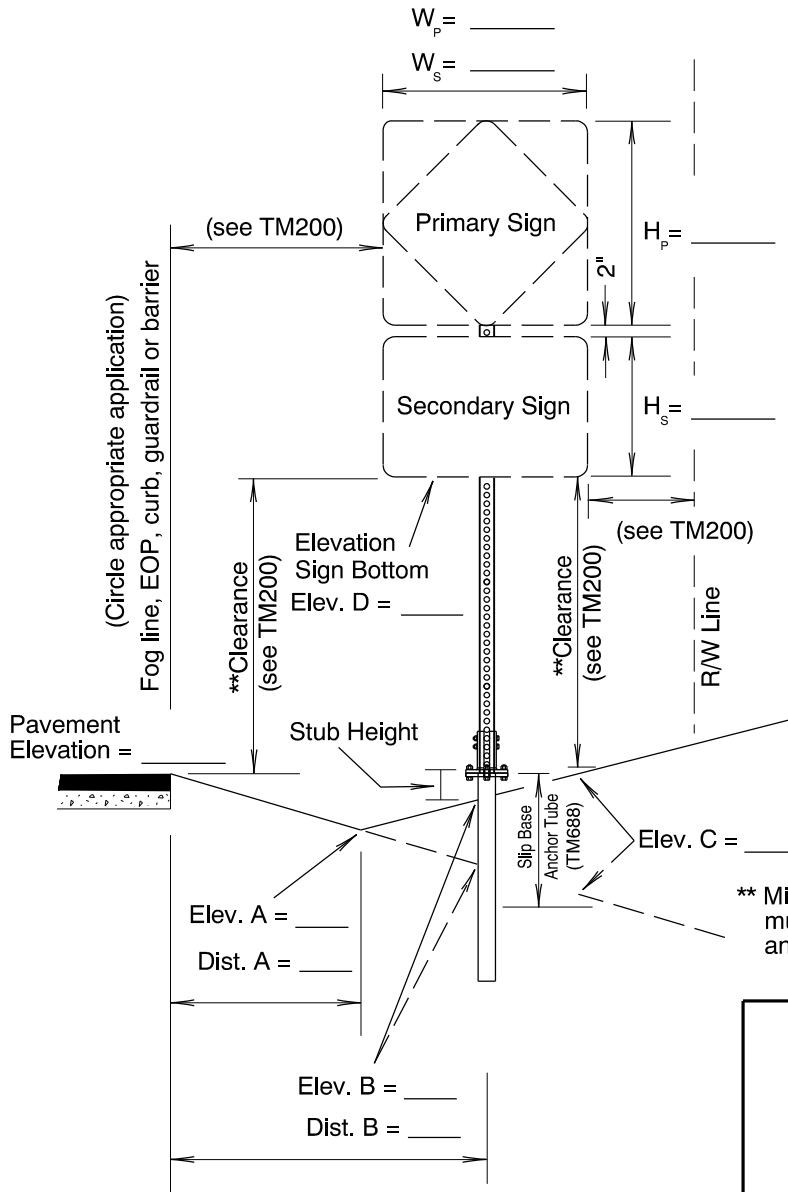

** Minimum vertical clearance requirements (see TM200) must be satisfied with respect to both Edge of Pavement and ground level beneath entire sign.

NOTE: After staking post locations, submit completed form(s) to the Project Manager for review, per Sec. 00150.35(d)(2) of Std. Specs. Project Manager is encouraged to contact Sign Designer for input, as needed.

Approved

Approved as noted

Returned for correction

Name _____

Date _____

Comments:
