COMPANY: NORTHWEST NATURAL GAS

WELL: OM 22-26-65 RD

FIELD: MIST

COUNTY: COLUMBIA STATE: OREGON

COUNTY: COLUMBIA
Field: MIST
Location: 1744.22' SOUTH, 2512.13' EAS
Well: OM 22-26-65 RD
Company: NORTHWEST NATURAL GAS

Schlumberger

ARRAY INDUCTION
BHC SONIC /SP/GR
SCALE: 5" = 100'

LOCATION

1744.22' SOUTH, 2512.13' EAST
FROM THE NW CORNER OF 26

Elev.: K.B. 631 ft
G.L. 621 ft
D.F. 629 ft

Permanent Datum: GROUND LEVEL Elev.: 621 ft
Log Measured From: K.B 10.0 ft above Perm. Datum
Drilling Measured From: K.B

API Serial No.	SECTION	TOWNSHIP	RANGE
36-009-00330	26	6N	5W

Logging Date		21-MAY-2000			
Run Number		1			
Depth Driller		2151 ft			
Schlumberger Depth		2144 ft			
Bottom Log Interval		2136 ft			
Top Log Interval		487 ft			
Casing Driller Size @ Depth		7.000 in @ 487 ft		@	
Casing Schlumberger		487 ft			
Bit Size		6.250 in			
Type Fluid In Hole		DMA			
MUD Density	Viscosity	8.9 lbm/gal	45 s		
Fluid Loss	PH	6.6 cm3	9		
Source Of Sample		FLOWLINE			
RM @ Measured Temperature		1.185 ohm.m @ 76 degF		@	
RMF @ Measured Temperature		1.050 ohm.m @ 72 degF		@	
RMC @ Measured Temperature		0.930 ohm.m @ 76 degF		@	
Source RMF	RMC	PRESS	PRESS		
RM @ MRT	RMF @ MRT	0.954 @ 96	0.805 @ 96	@	@
Maximum Recorded Temperatures		96 degF	96	96	
Circulation Stopped	Time	21-MAY-2000	9:30		
Logger On Bottom	Time	21-MAY-2000	11:50		
Unit Number	Location	3152	SACRAMENTO		
Recorded By		M.KHAN			
Witnessed By		JACK MEYER			

Run 1

Logging Date			
Run Number			
Depth Driller			
Schlumberger Depth			
Bottom Log Interval			
Top Log Interval			
Casing Driller Size @ Depth			@
Casing Schlumberger			
Bit Size			
Type Fluid In Hole			
MUD Density	Viscosity		
Fluid Loss	PH		
Source Of Sample			
RM @ Measured Temperature			@
RMF @ Measured Temperature			@
RMC @ Measured Temperature			@
Source RMF	RMC		
RM @ MRT	RMF @ MRT	@	
Maximum Recorded Temperatures			
Circulation Stopped	Time		
Logger On Bottom	Time		
Unit Number	Location		
Recorded By			
Witnessed By			

@

Run 2

@

@ @ @ @ @

Run 3

@

Run 4

DISCLAIMER
THE USE OF AND RELIANCE UPON THIS RECORDED-DATA BY THE HEREIN NAMED COMPANY (AND ANY OF ITS AFFILIATES, PARTNERS, REPRESENTATIVES, AGENTS, CONSULTANTS AND EMPLOYEES) IS SUBJECT TO THE TERMS AND CONDITIONS AGREED UPON BETWEEN SCHLUMBERGER AND THE COMPANY, INCLUDING: (a) RESTRICTIONS ON USE OF THE RECORDED-DATA; (b) DISCLAIMERS AND WAIVERS OF WARRANTIES AND REPRESENTATIONS REGARDING COMPANY'S USE OF AND RELIANCE UPON THE RECORDED-DATA; AND (c) CUSTOMER'S FULL AND SOLE RESPONSIBILITY FOR ANY INFERENCE DRAWN OR DECISION MADE IN CONNECTION WITH THE USE OF THIS RECORDED-DATA.

OTHER SERVICES1	OTHER SERVICES2
OS1: FMI GR	OS1:
OS2:	OS2:
OS3:	OS3:
OS4:	OS4:
OS5:	OS5:

REMARKS: RUN NUMBER 1

REMARKS: RUN NUMBER 2

RUN 1

SERVICE ORDER #:
PROGRAM VERSION: 9C1-303
FLUID LEVEL: 0 ft

LOGGED INTERVAL	START	STOP

RUN 2

SERVICE ORDER #:
PROGRAM VERSION:
FLUID LEVEL:

LOGGED INTERVAL	START	STOP

EQUIPMENT DESCRIPTION

RUN 1

SURFACE EQUIPMENT

GSR-U/Y
NCT-B
CNB-AB
NCS-VB

WITM (CTS)-A

DOWNHOLE EQUIPMENT

RUN 2

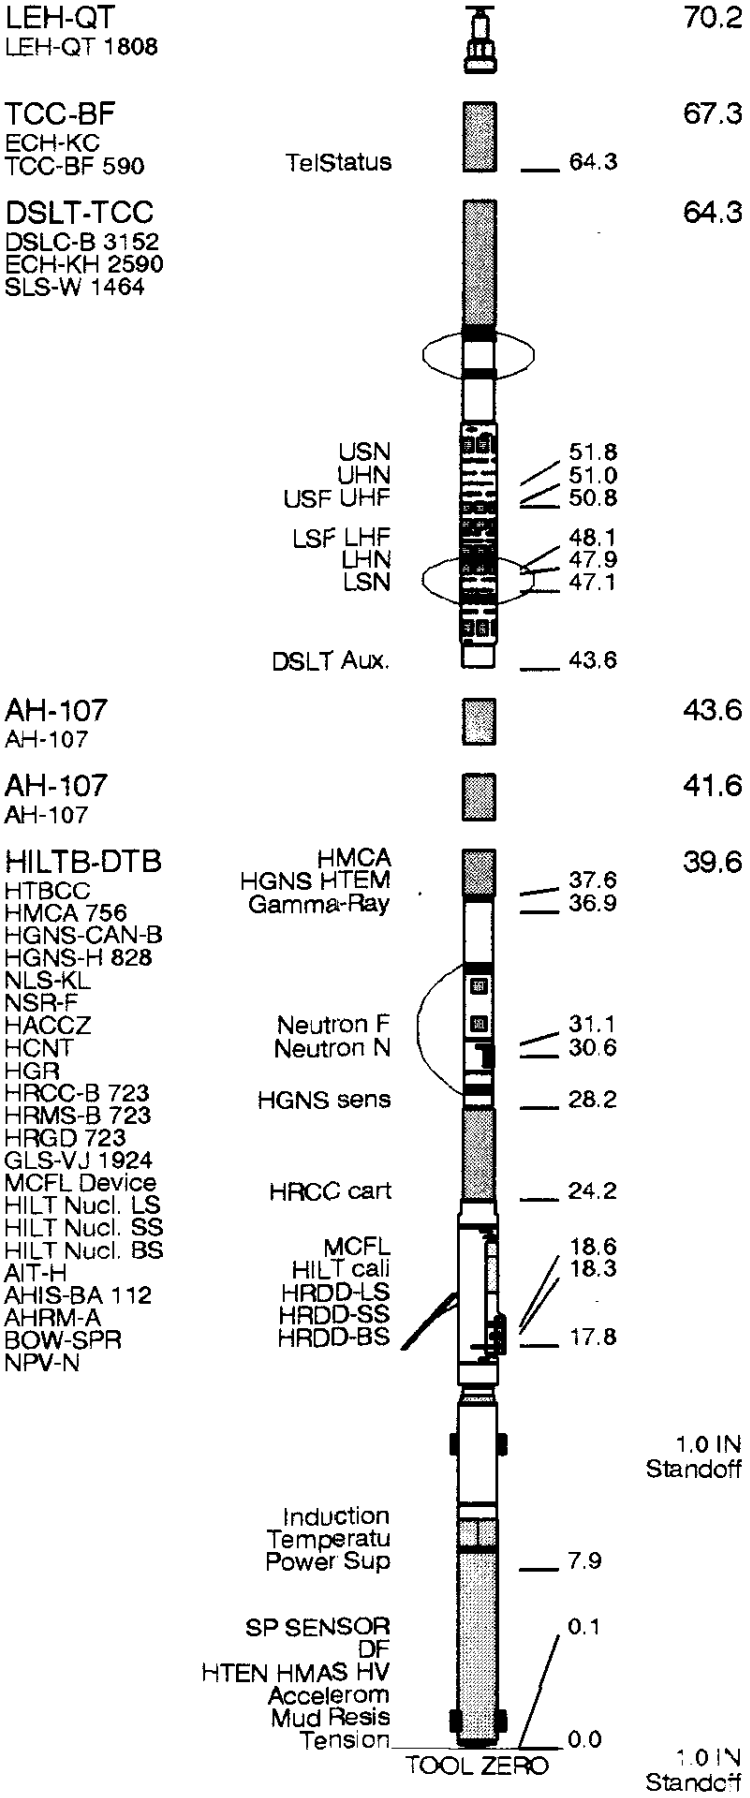

MAXIMUM STRING DIAMETER 5.88 IN
MEASUREMENTS RELATIVE TO TOOL ZERO
ALL LENGTHS IN FEET

Input DLIS Files

DEFAULT	HILTB .006	FN:5	PRODUCER	21-May-2000 12:08	2148.0 FT	0.0 FT

Output DLIS Files

DEFAULT	HILTB .007	FN:6	PRODUCER	21-May-2000 13:30	2153.0 FT	105.0 FT

OP System Version: 9C1-303

MCM

HILTB-DTB	OP91-KP1a	DSLT-TCC	OP91-KP1a
TCC-BF	OP91-KP1a		

PIP SUMMARY

⊣ Integrated Transit Time Minor Pip Every 1 MS
⊣ Integrated Transit Time Major Pip Every 10 MS

■ Time Mark Every 60 S

Gamma Ray (GR)		
0	(GAPI)	150

AIT-H 60 Inch Investigation (AHO60)		
0.2	(OHMM)	20

AIT-H 30 Inch Investigation (AHO30)		
0.2	(OHMM)	20

AIT-H 20 Inch Investigation (AHO20)		
0.2	(OHMM)	20

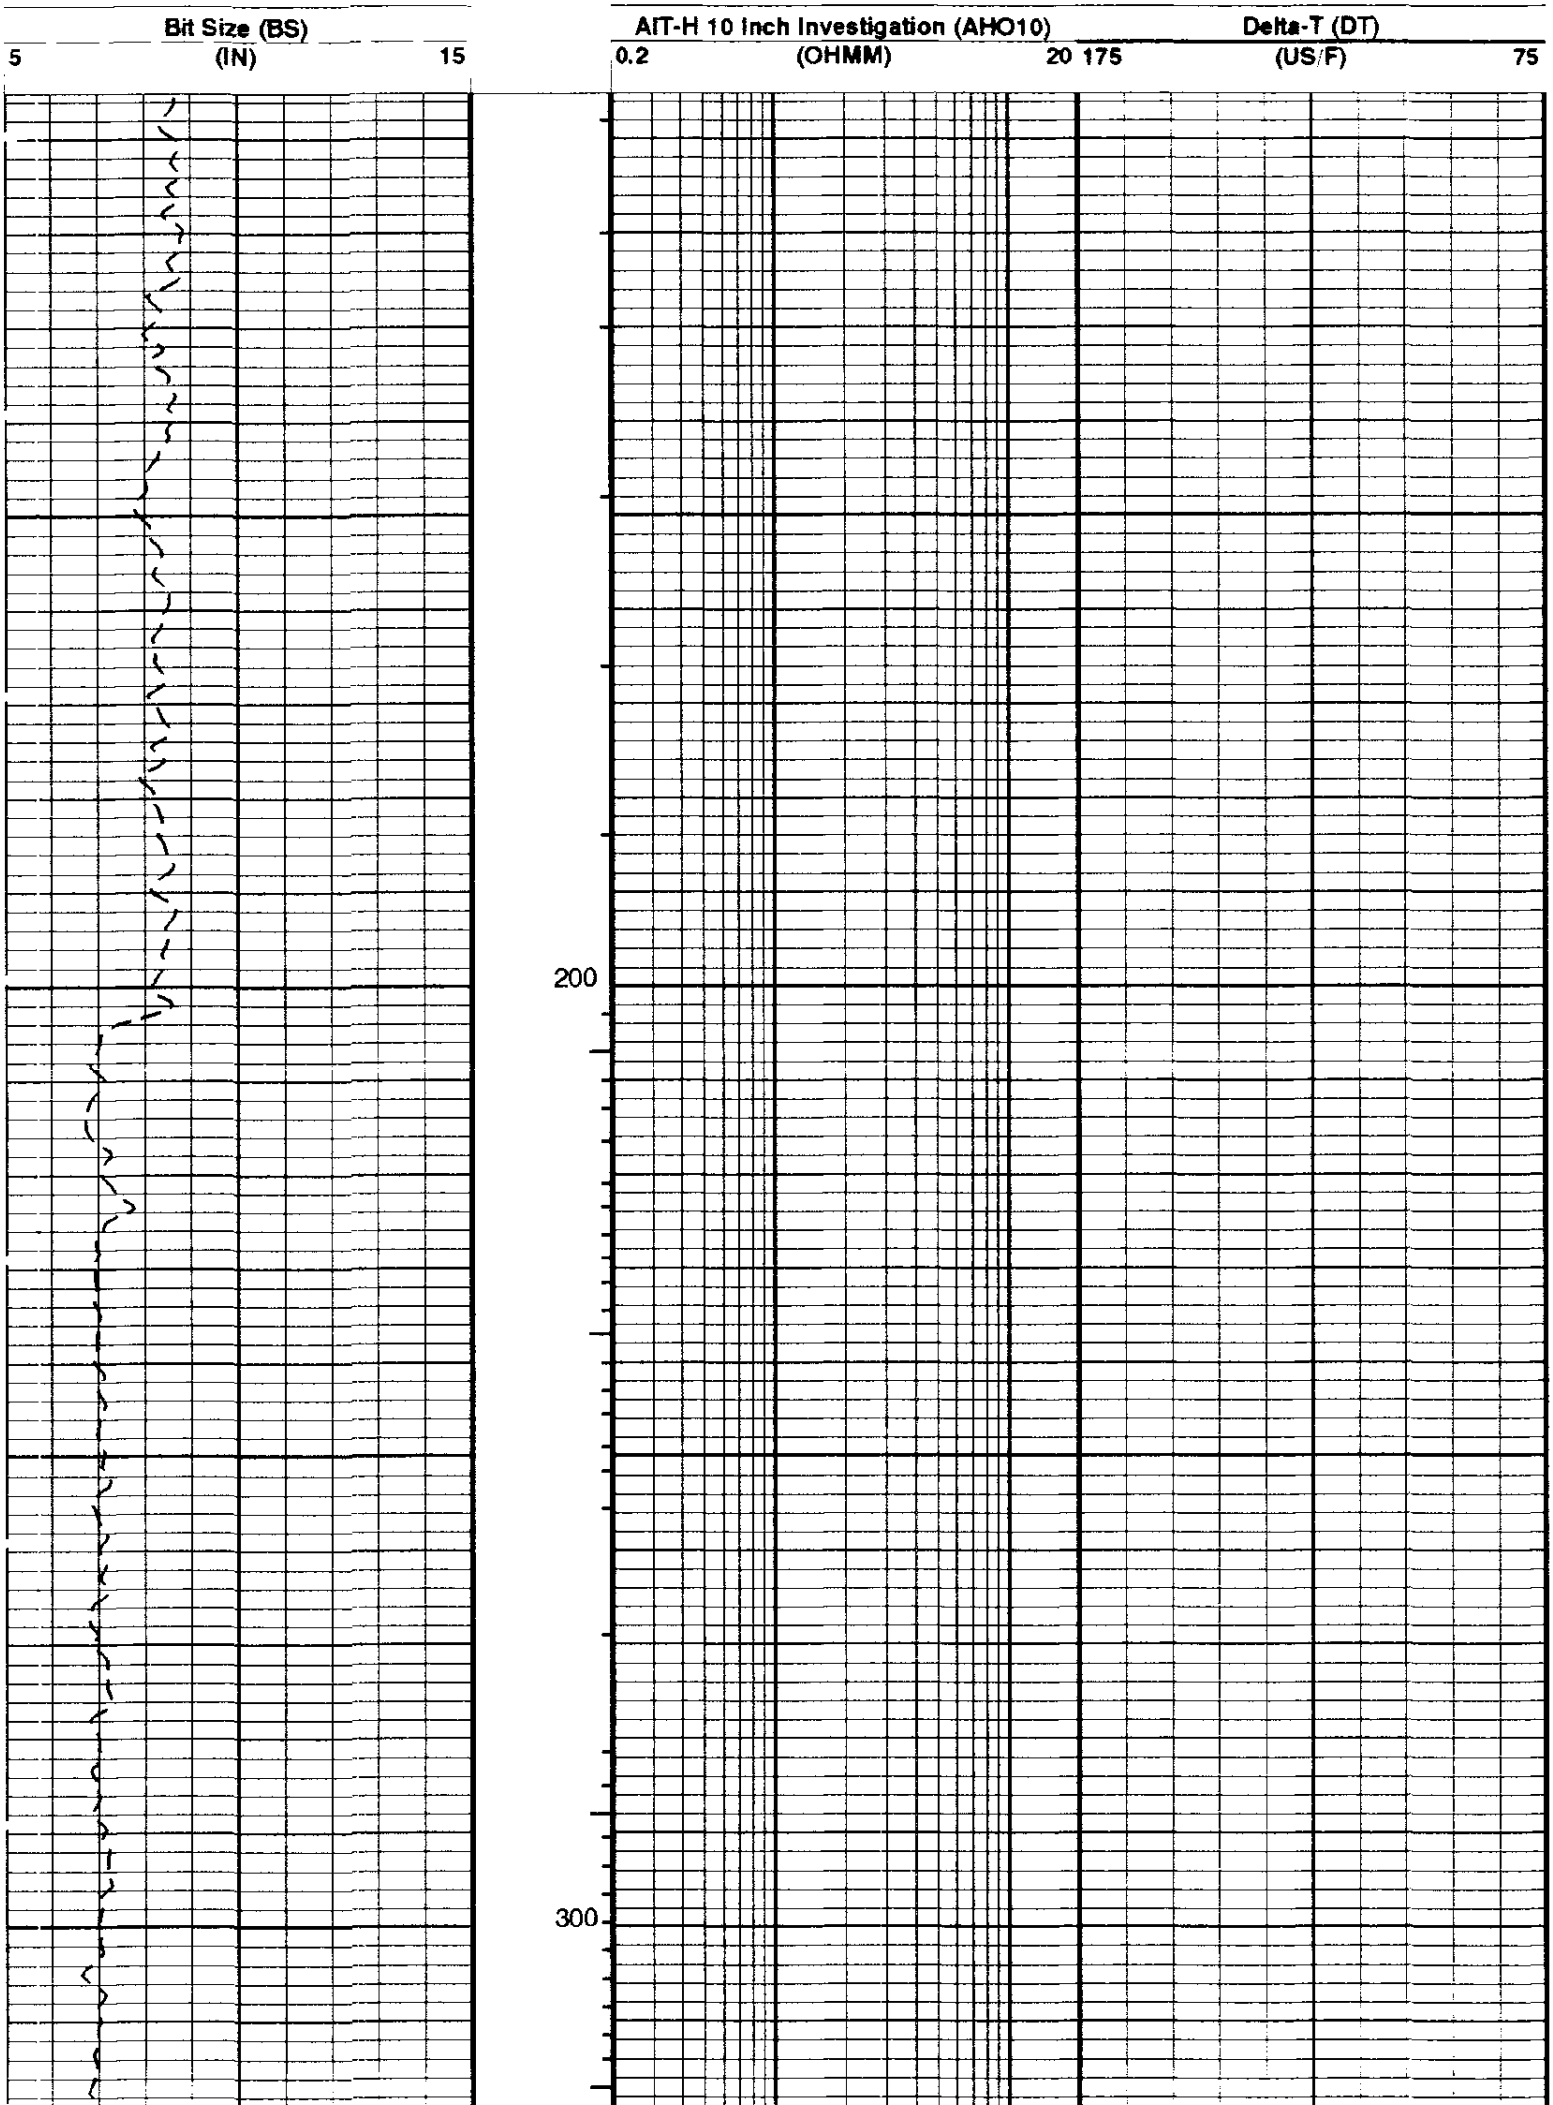

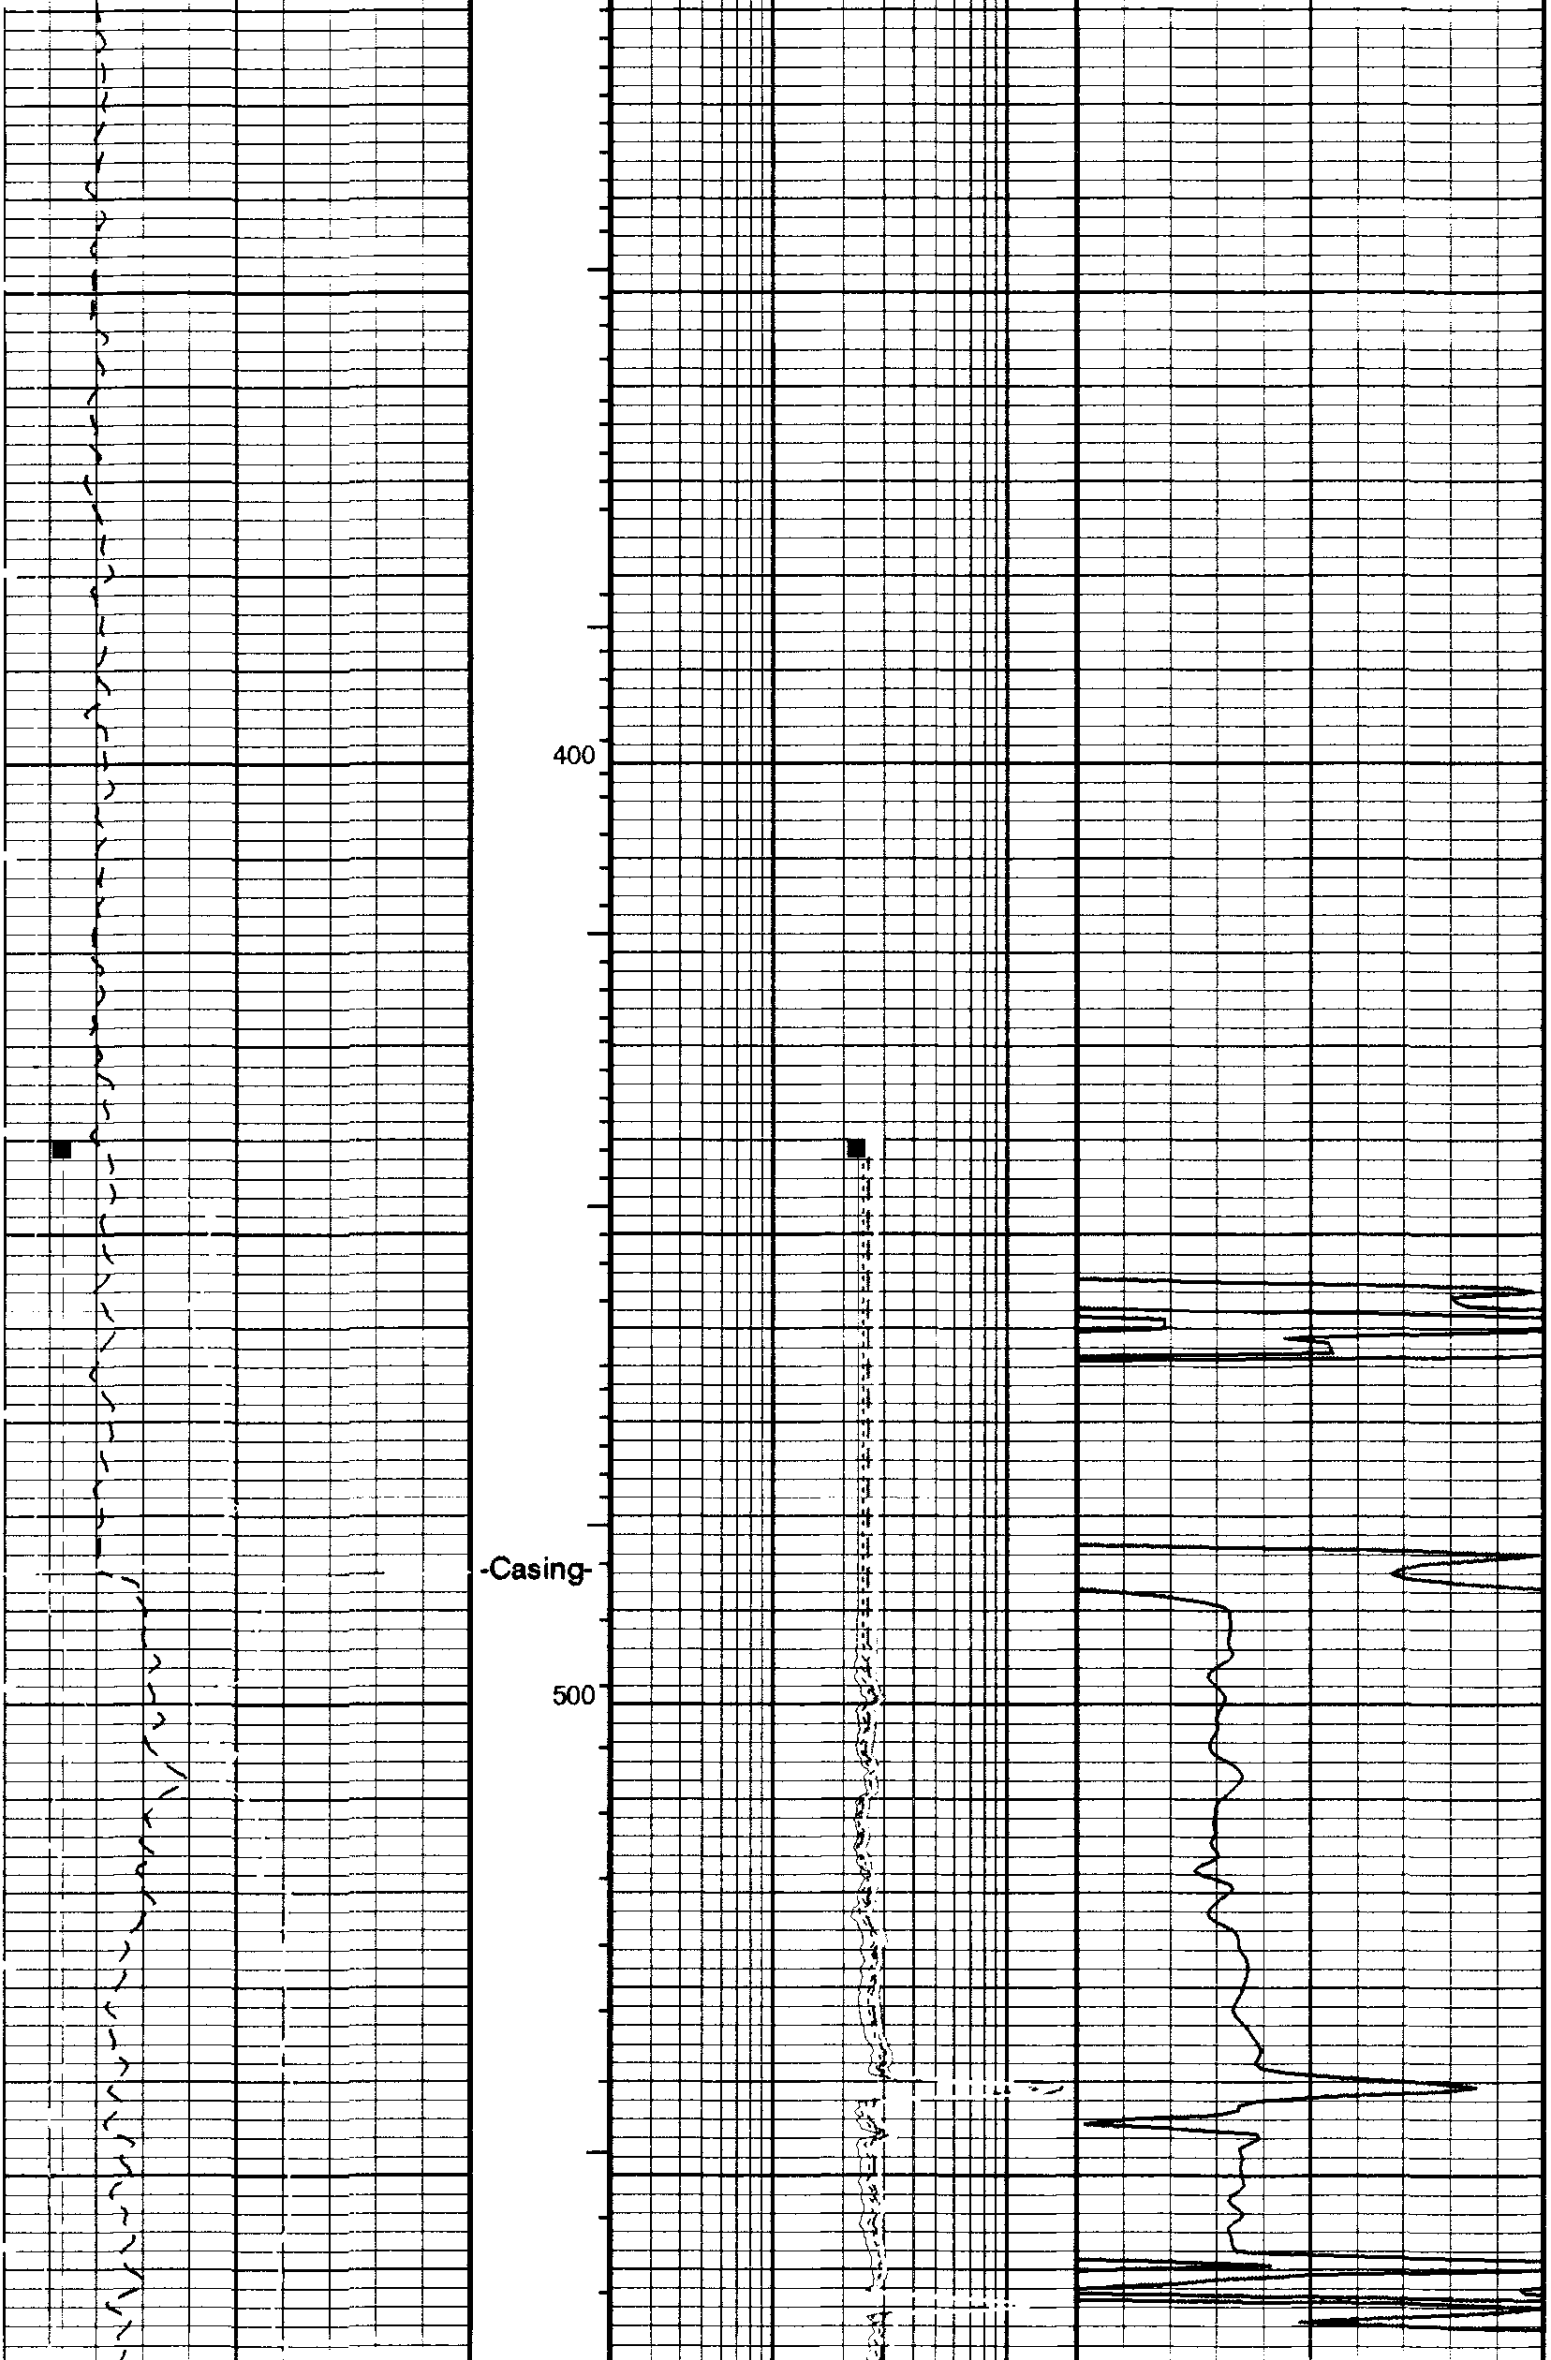

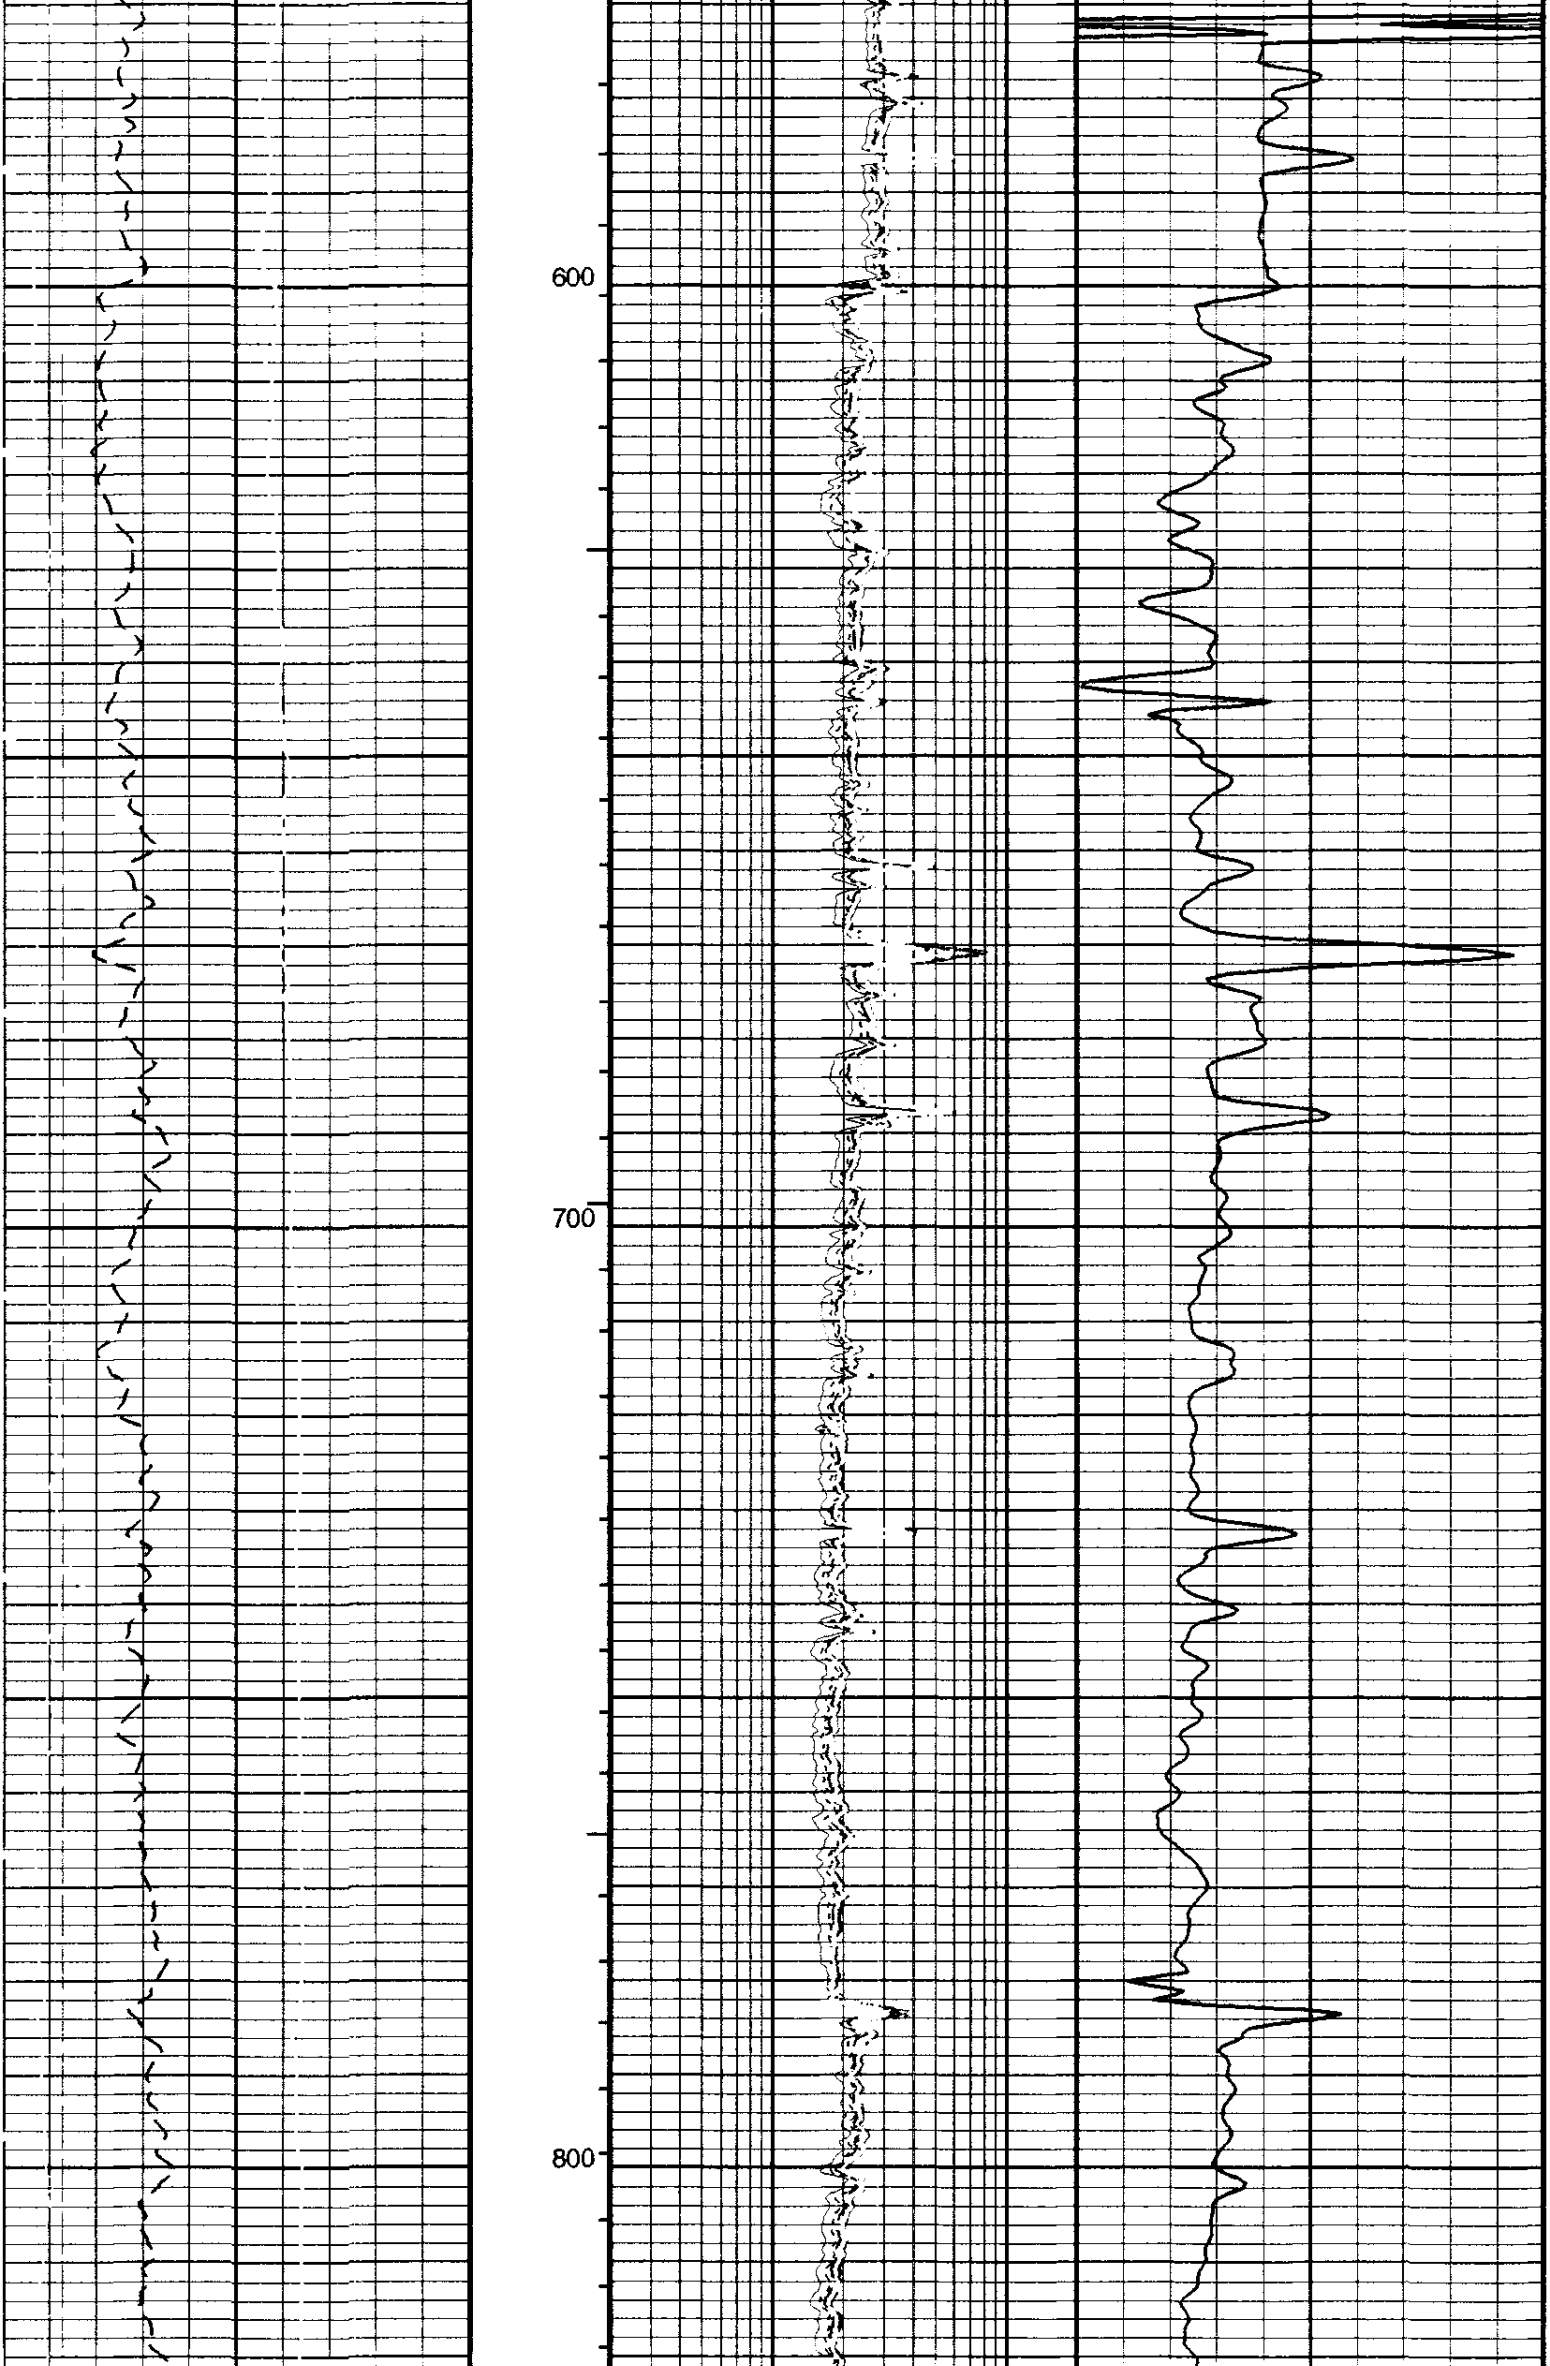

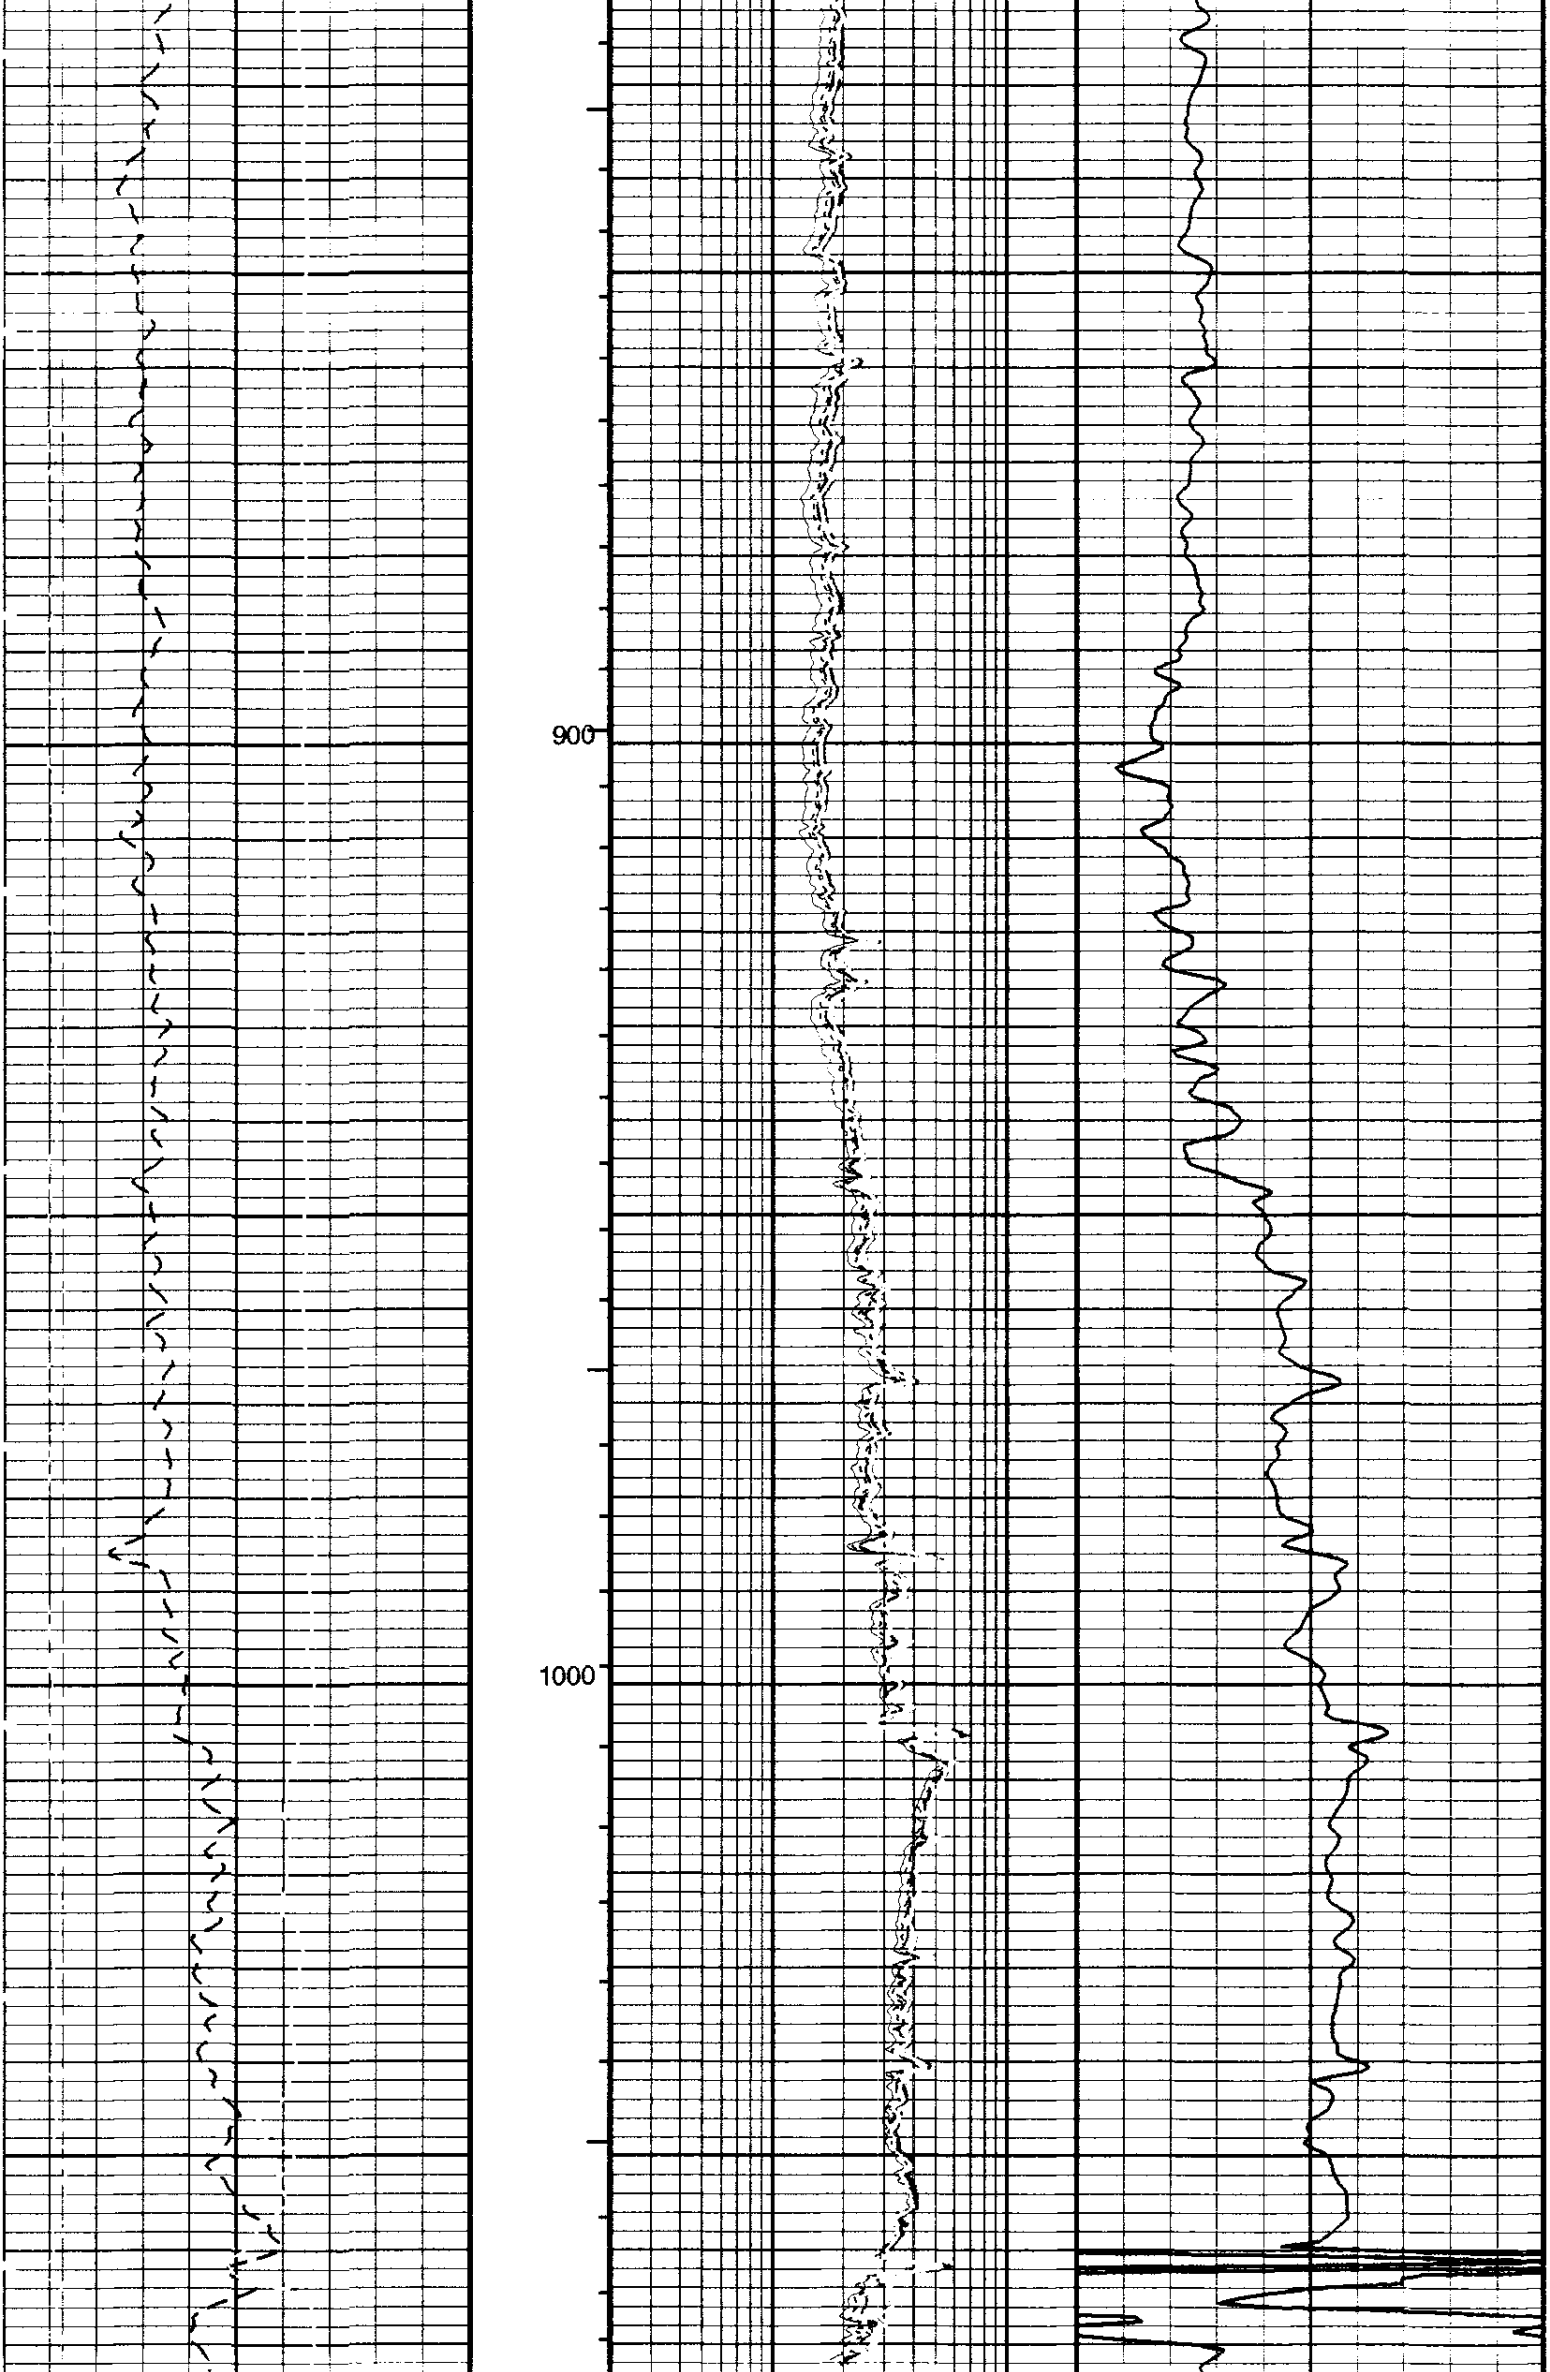

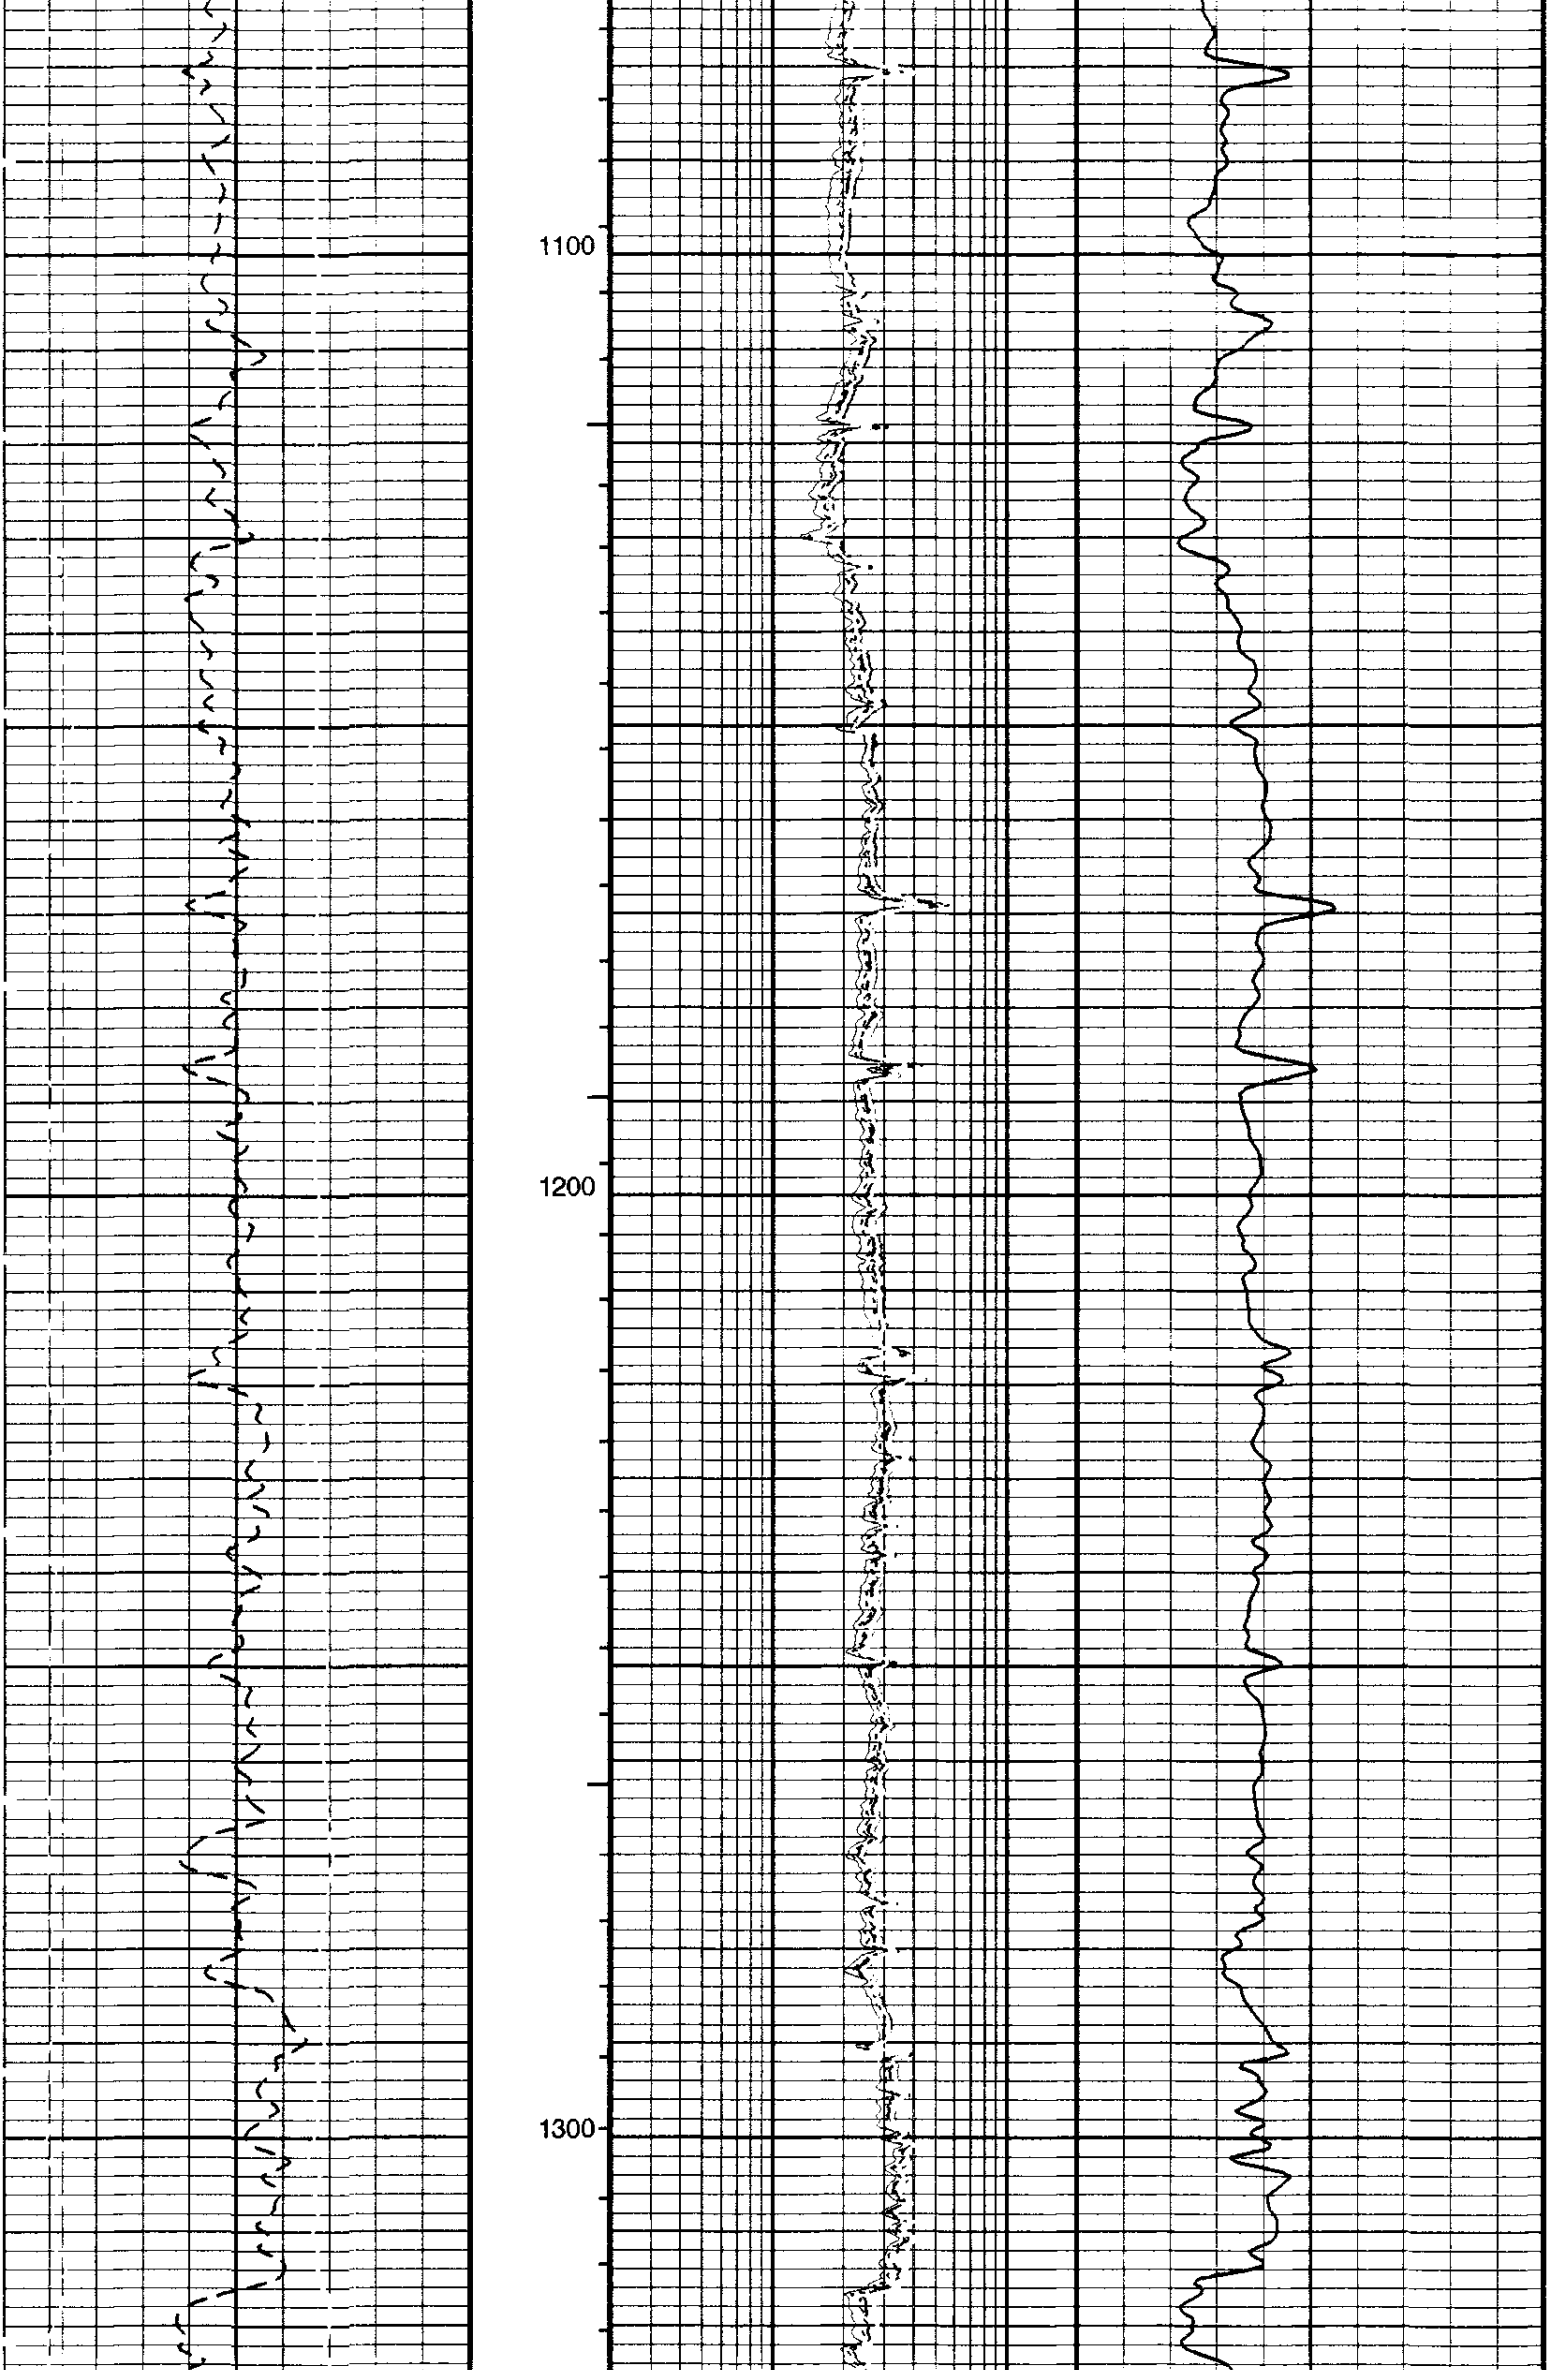

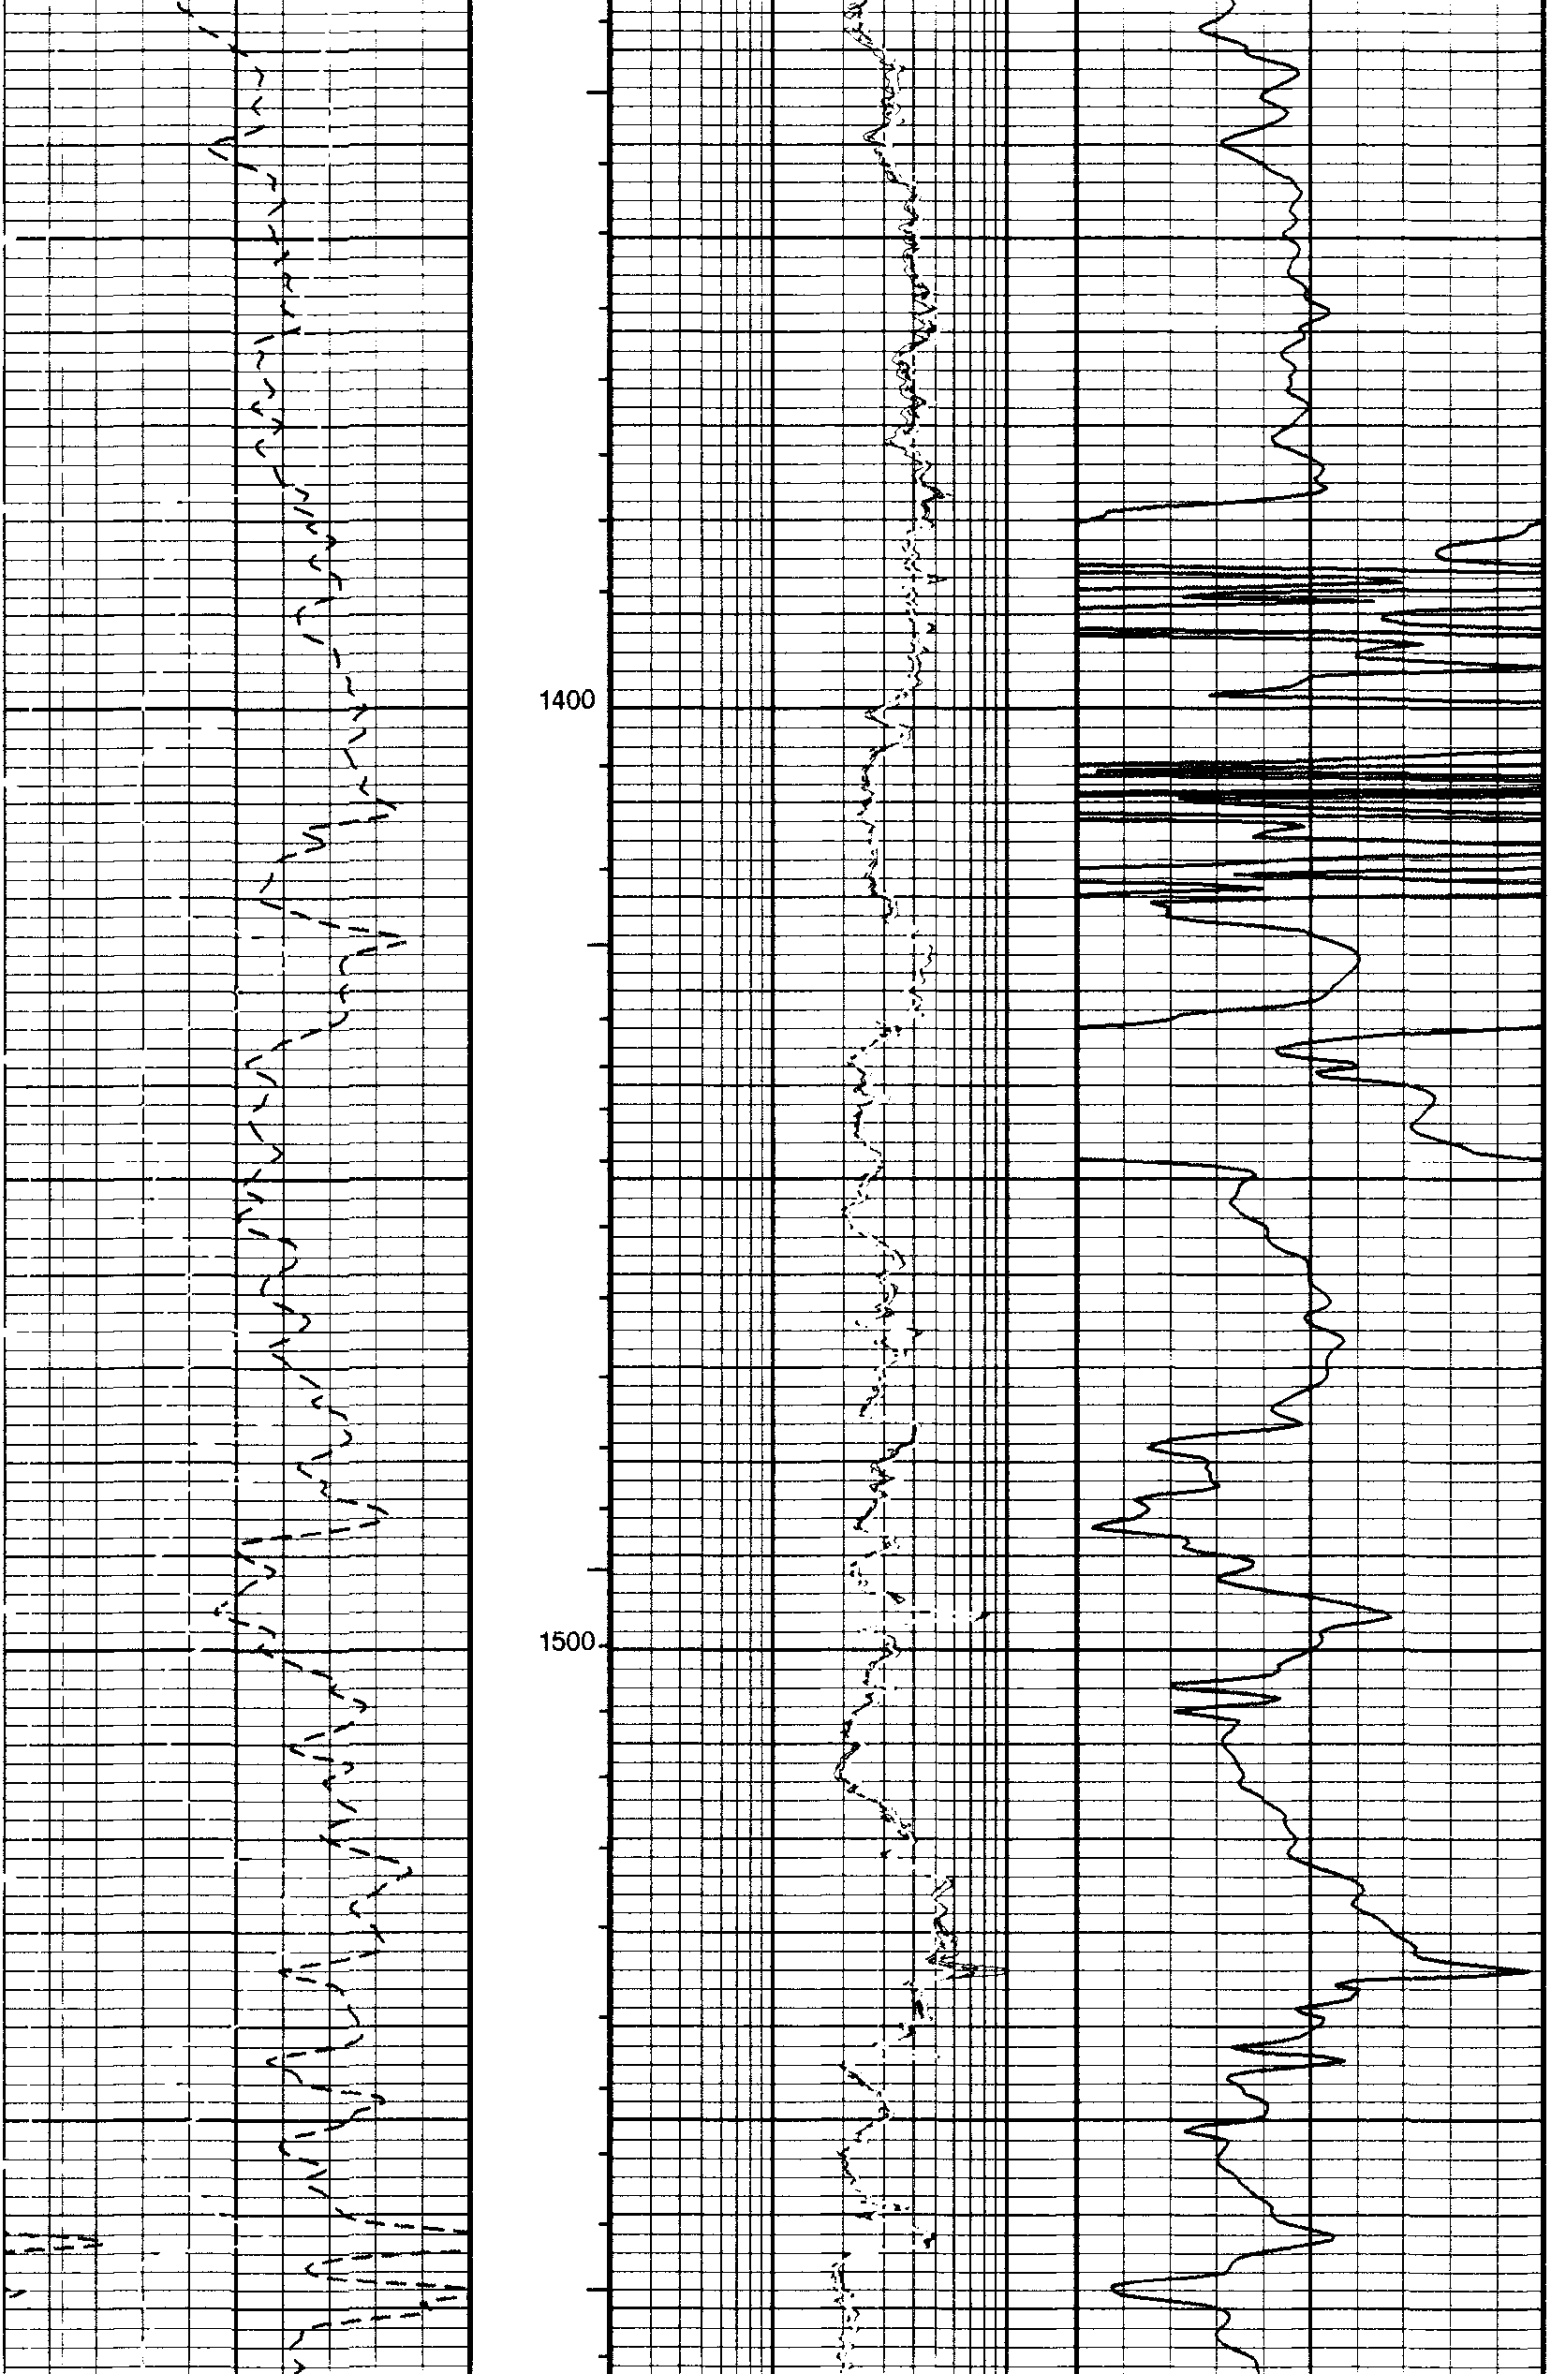

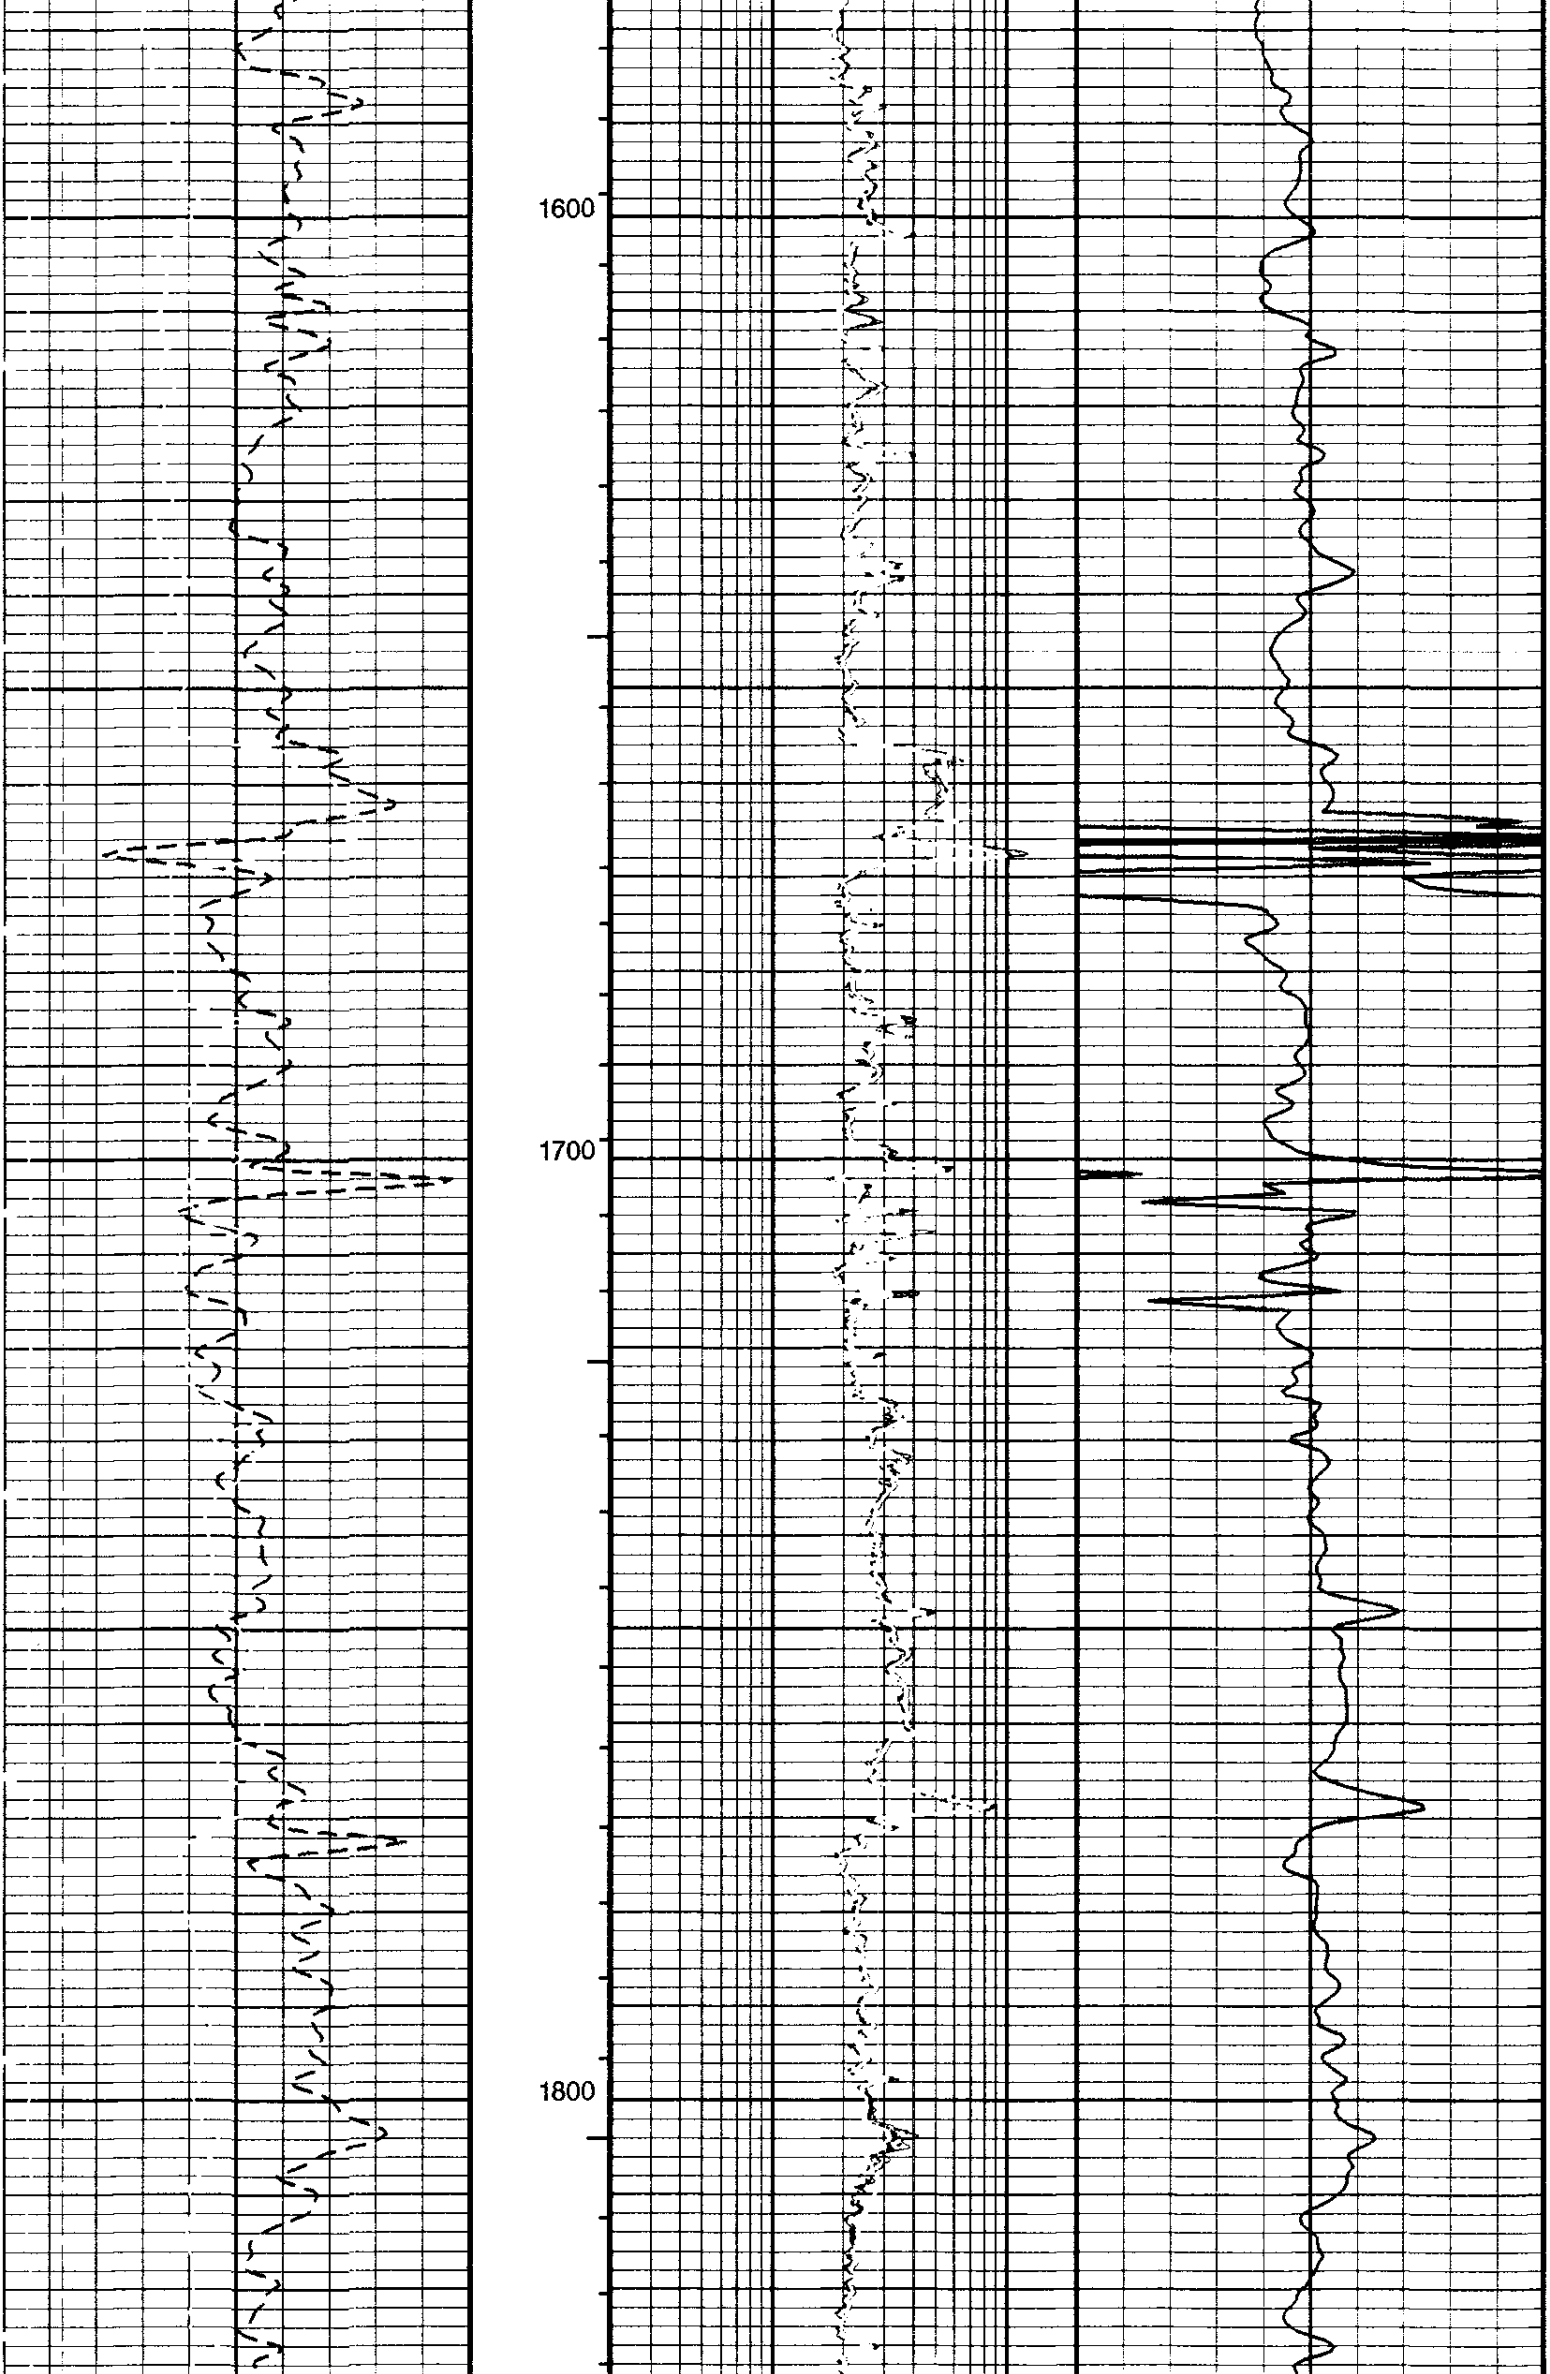

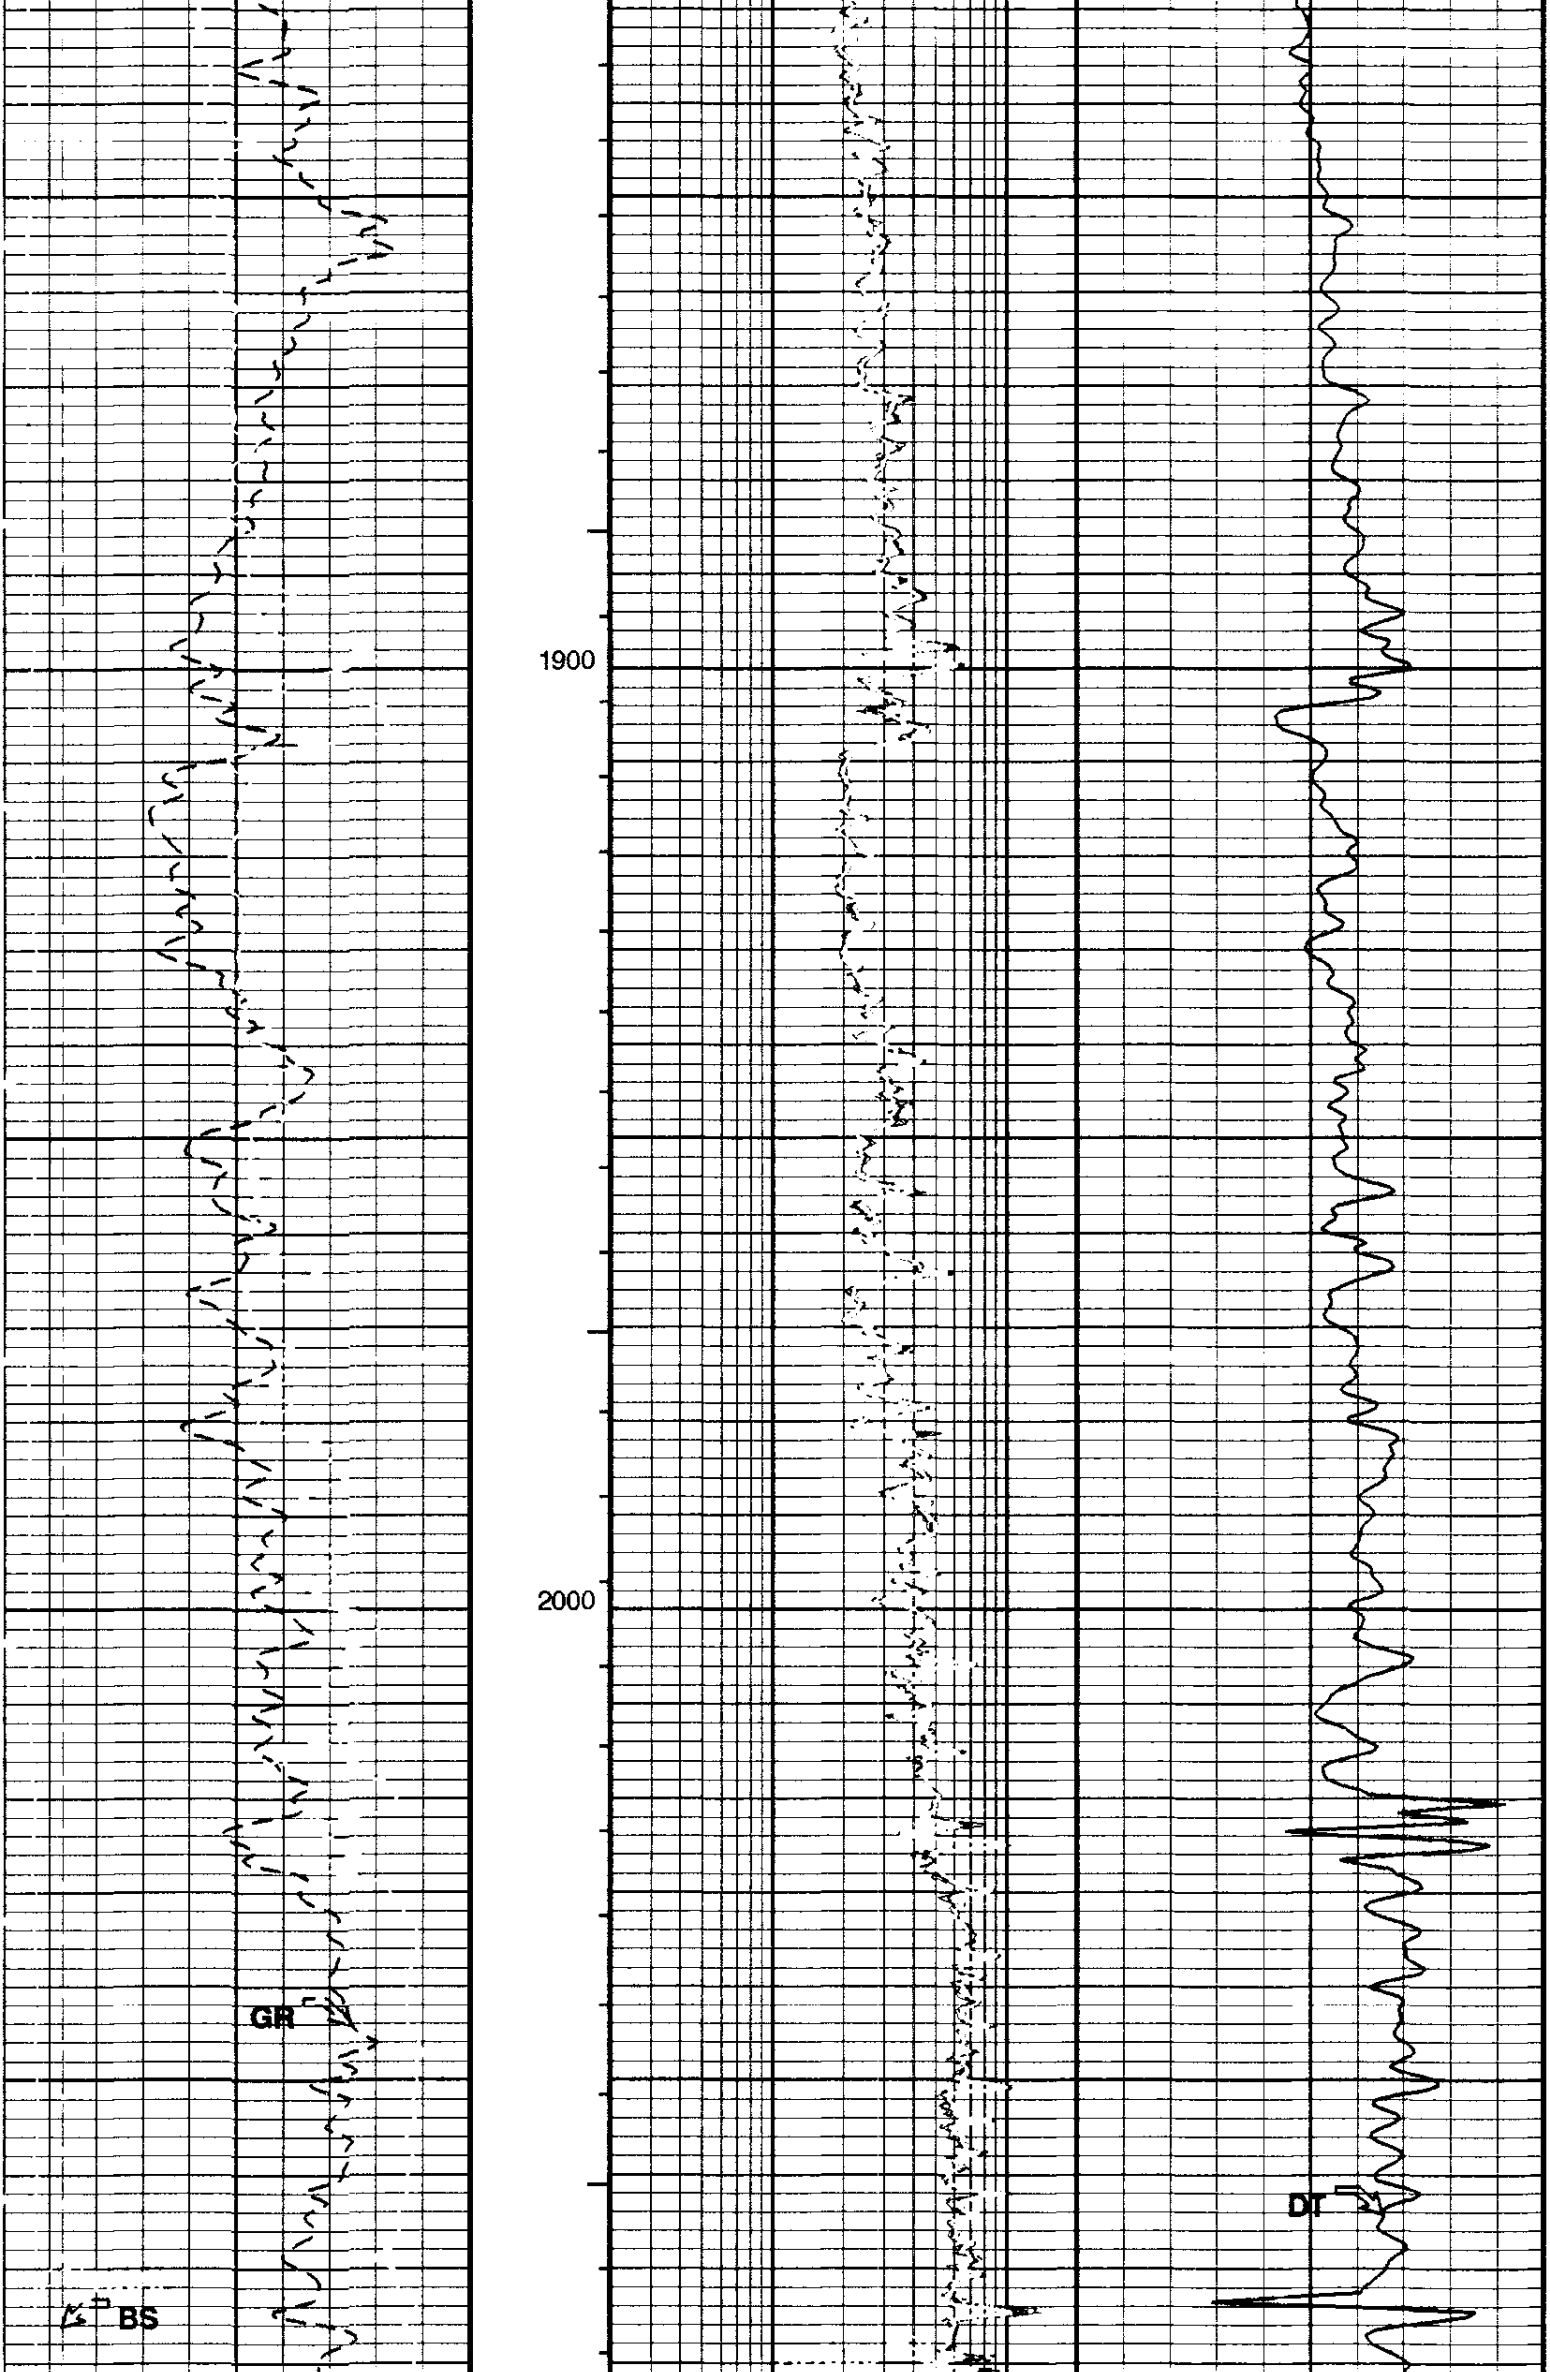

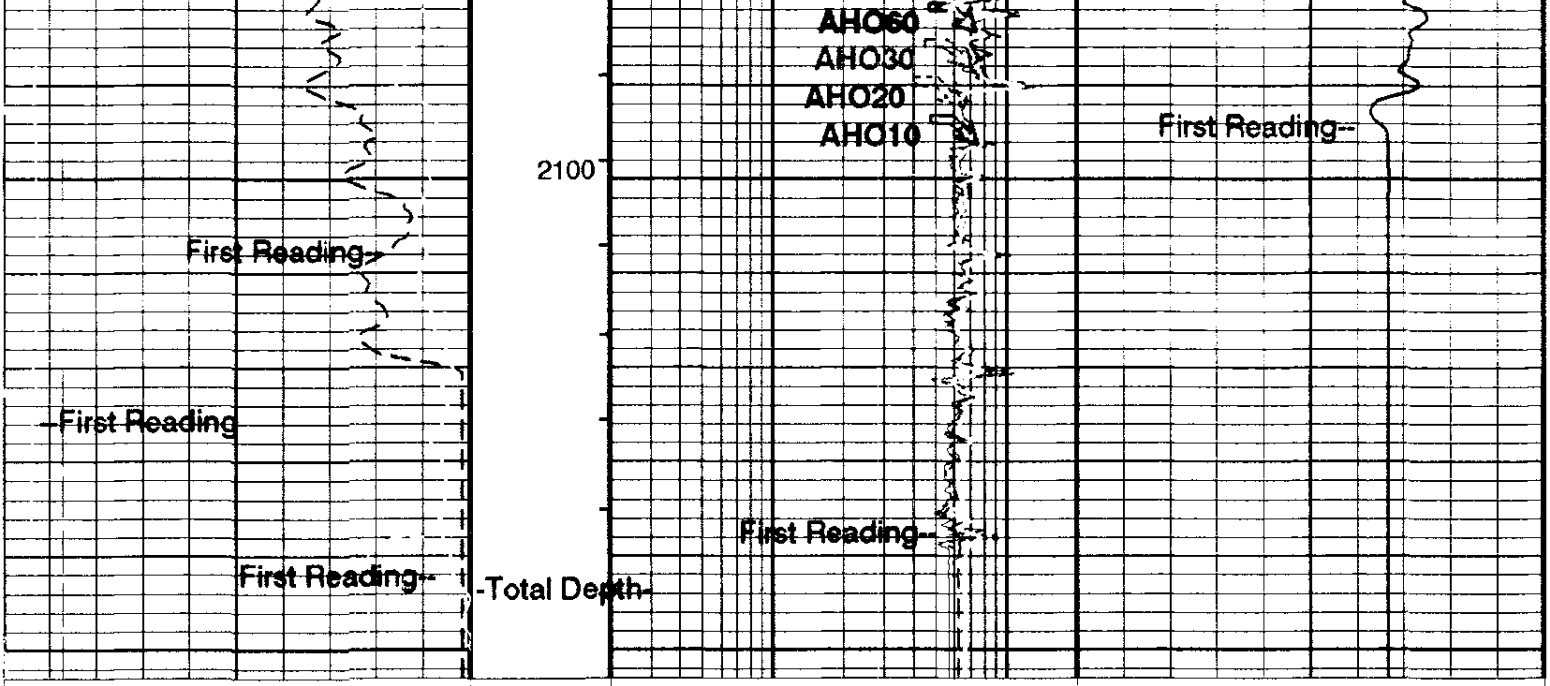

Bit Size (BS) 5 (IN) 15	AIT-H 10 Inch Investigation (AHO10) 0.2 (OHMM) 20	Delta-T (DT) 175 (US/F) 75
	AIT-H 20 Inch Investigation (AHO20) 0.2 (OHMM) 20	
Gamma Ray (GR) 0 (GAPI) 150	AIT-H 30 Inch Investigation (AHO30) 0.2 (OHMM) 20	
	AIT-H 60 Inch Investigation (AHO60) 0.2 (OHMM) 20	

PIP SUMMARY

⊣ Integrated Transit Time Minor Pip Every 1 MS
—⊣ Integrated Transit Time Major Pip Every 10 MS

■ Time Mark Every 60 S

Parameters

DLIS Name	Description	Value	
AHBHM	Array Induction Borehole Correction Mode	2_ComputeStandoff	
AHBHV	Array Induction Borehole Correction Code Version Number	870	
AHBLM	Array Induction Basic Logs Mode	6_One_Two_and_Four	
AHBLV	Array Induction Basic Logs Code Version Number	973	
AHBPO	Array Induction Basic Logs Processing Option	Standard_Processing	
AHCDE	Array Induction Casing Detection Enable	Yes	
AHCEN	Array Induction Tool Centering Flag (in Borehole)	Eccentered	
AHCSED	Array Induction Casing Shoe Estimated Depth	-50000	FT
AHFRSV	Array Induction Response Set Version for Four ft Resolution	30.66.23.11	
AHMRF	Array Induction Mud Resistivity Factor	1	
AHORSV	Array Induction Response Set Version for One ft Resolution	30.66.23.11	
AHRFV	Array Induction Radial Profiling Code Version Number	700	
AHRPV	Array Induction Radial Parametrization Code Version Number	710	
AHSTA	Array Induction Tool Standoff	1.5	IN
AHTRSV	Array Induction Response Set Version for Two ft Resolution	30.66.23.11	
BHT	Bottom Hole Temperature (used in calculations)	86	DEGF
BS	Bit Size	6.250	IN
DFD	Drilling Fluid Density	8.90	LB/G
DO	Depth Offset for Logical Unit 1	5.0	FT
DORL	Depth Offset Repeat Analysis	5.0	FT
DTCM	Delta-T Computation Mode	FULL	
FEXP	Form Factor Exponent	2	
FNUM	Form Factor Numerator	1	
GCSE	Generalized Caliper Selection	HCAL	
GDEV	Average Angular Deviation of Borehole from Normal	12	DEG
GGRD	Geothermal Gradient	0.01	DF/F
GRSE	Generalized Mud Resistivity Selection	AITH_RESIST	
GTSE	Generalized Temperature Selection	LINEAR_ESTIMATE	
HSCM	HILT Speed Correction Mode	NO_SC	
HSTI	STI Uses HILT Acceleration	YES	
MODE	Sonic Firing Mode	BHC	
MST	Mud Sample Temperature	76.00	DEGF
PP	Playback Processing	NORMAL	
SHT	Surface Hole Temperature	68	DEGF
SPNV	SP Next Value	0	MV
TD	Total Depth	2151	FT

Format: AITSON_1FT Vertical Scale: 5" per 100' Graphics File Created: 21-May-2000 13:30

OP System Version: 9C1-303

MCM

HILTB-DTB	OP91-KP1a	DSLT-TCC	OP91-KP1a
TCC-BF	OP91-KP1a		

Input DLIS Files

DEFAULT	HILTB .006	FN:5	PRODUCER	21-May-2000 12:08	2148.0 FT	0.0 FT

Output DLIS Files

DEFAULT	HILTB .007	FN:6	PRODUCER	21-May-2000 13:30

Schlumberger

REPEAT SECTION

MAXIS 500 Field Log

Input DLIS Files

DEFAULT	HILTB .006	FN:5	PRODUCER	21-May-2000 12:08	2148.0 FT	0.0 FT
DEFAULT	HILTB .004	FN:3	PRODUCER	21-May-2000 11:50	2154.0 FT	1826.2 FT

Output DLIS Files

DEFAULT	HILTB .007	FN:6	PRODUCER	21-May-2000 13:30

OP System Version: 9C1-303

MCM

HILTB-DTB	OP91-KP1a	DSLT-TCC	OP91-KP1a
TCC-BF	OP91-KP1a		

PIP SUMMARY

⊣ Integrated Transit Time Minor Pip Every 1 MS
⊣ Integrated Transit Time Major Pip Every 10 MS

▶ Time Mark Every 60 S

AHT60_REP Curve (AHT60_REP)
0.2 (OHMM) 20

RWA_REP Curve (RWA_REP)
0 (OHMM) 3

AHT30_REP Curve (AHT30_REP)
0.2 (OHMM) 20

GR_REP Curve (GR_REP)
0 (GAPI) 150

AHT10_REP Curve (AHT10_REP)
0.2 (OHMM) 20

Bit Size (BS)
5 (IN) 15

AHT90_REP Curve (AHT90_REP)
0.2 (OHMM) 20

DT_REP Curve (DT_REP)
175 (US/F) 75



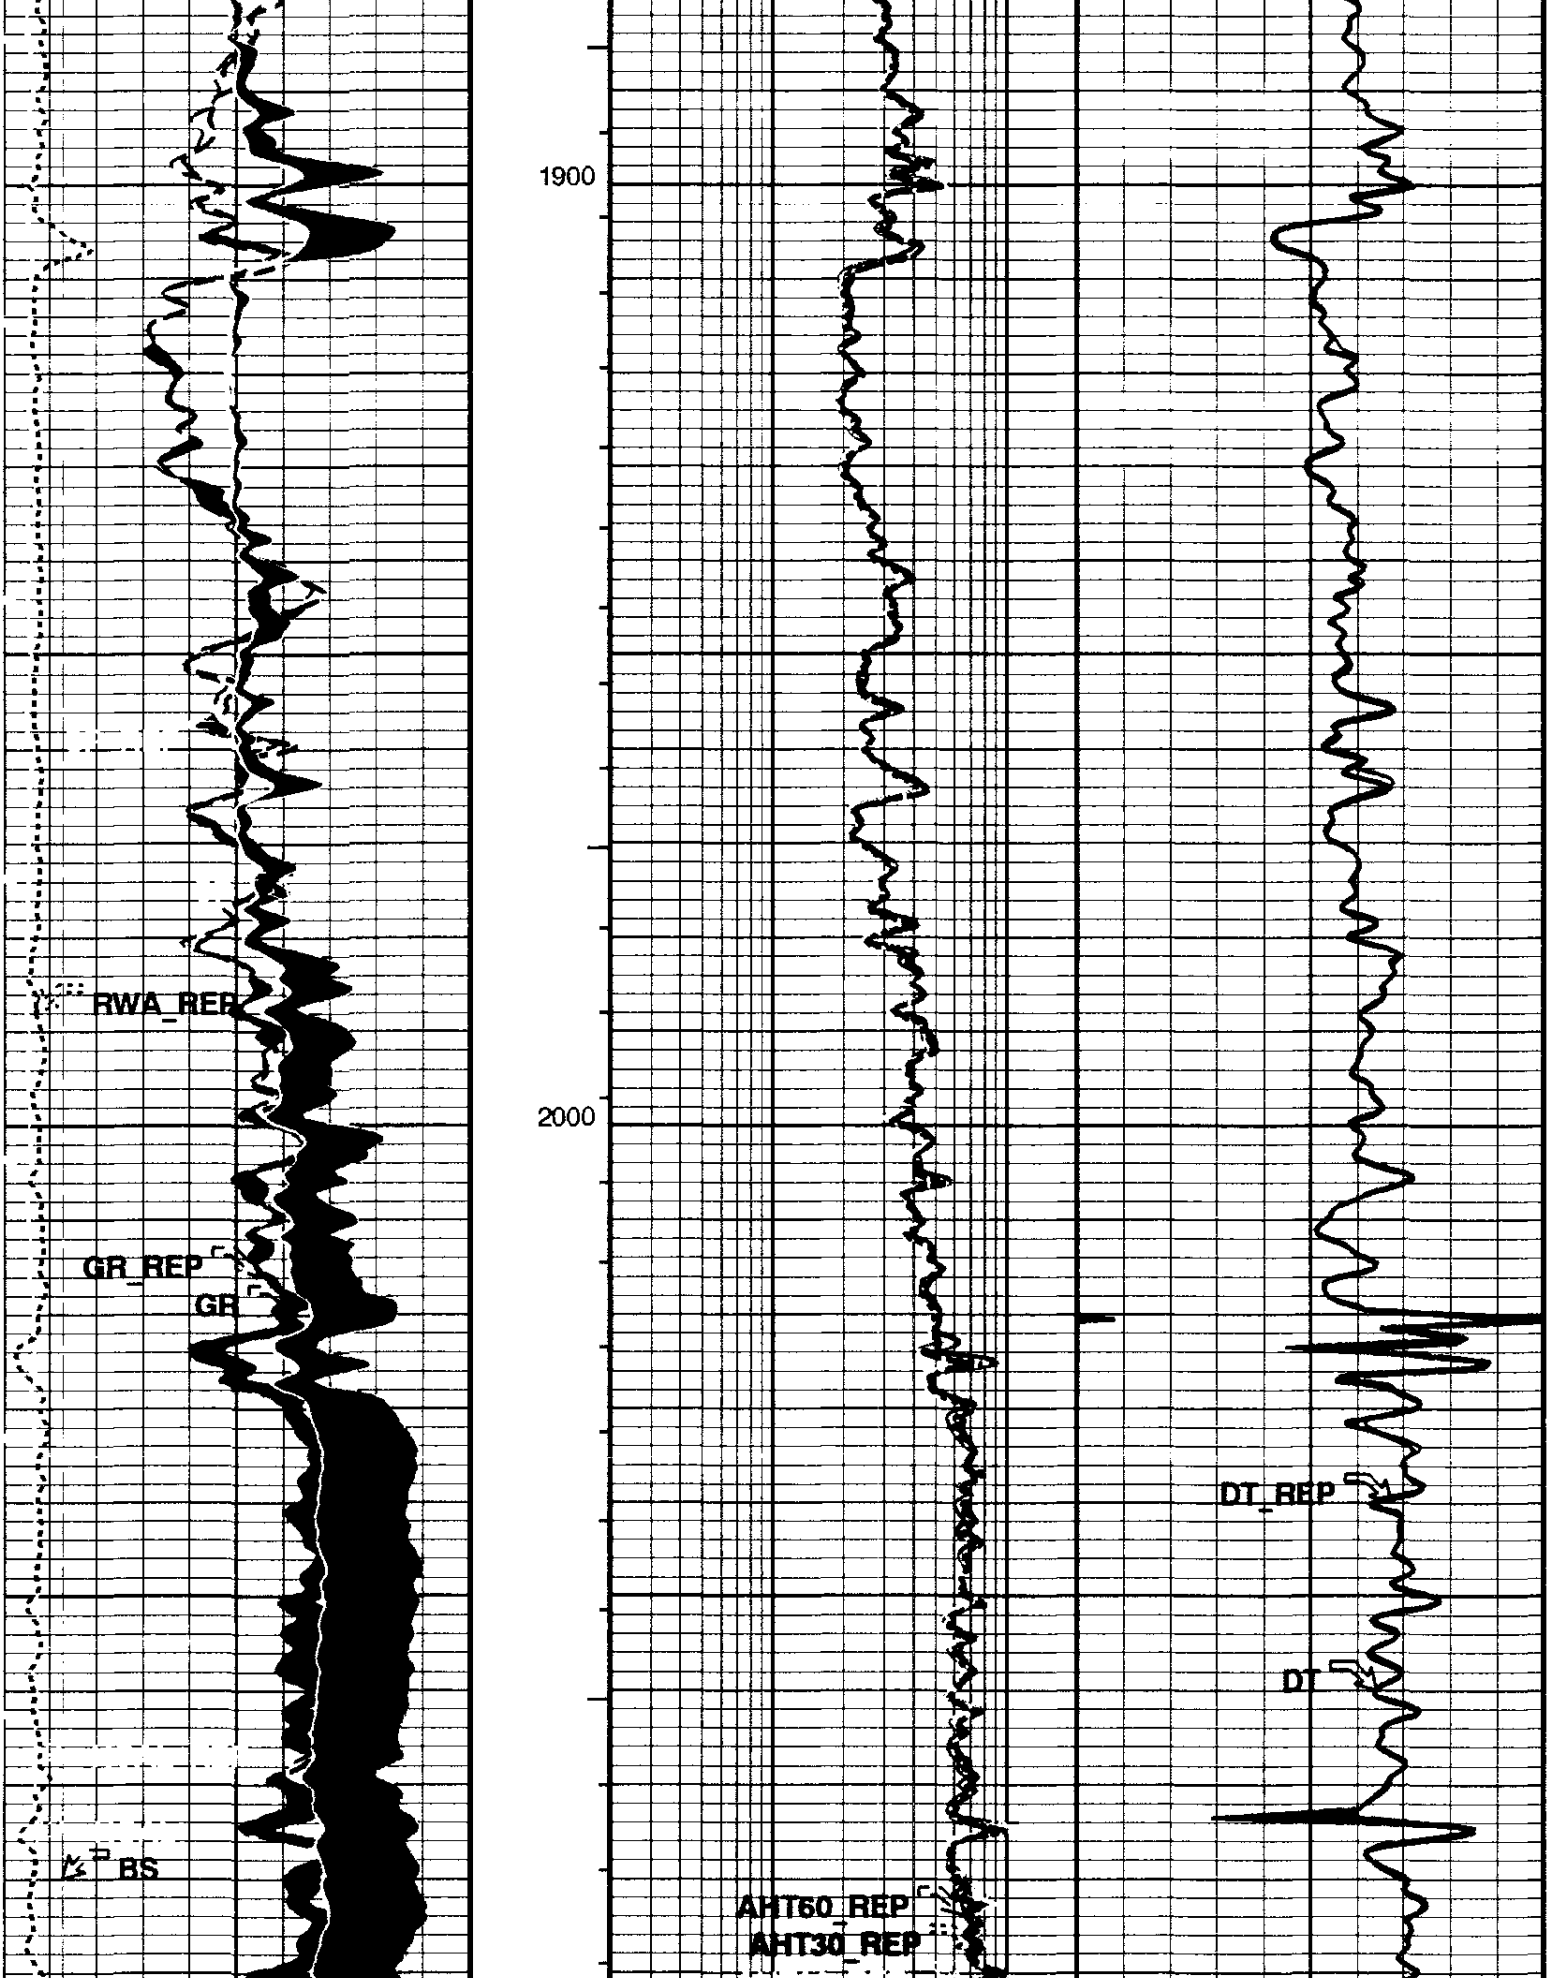

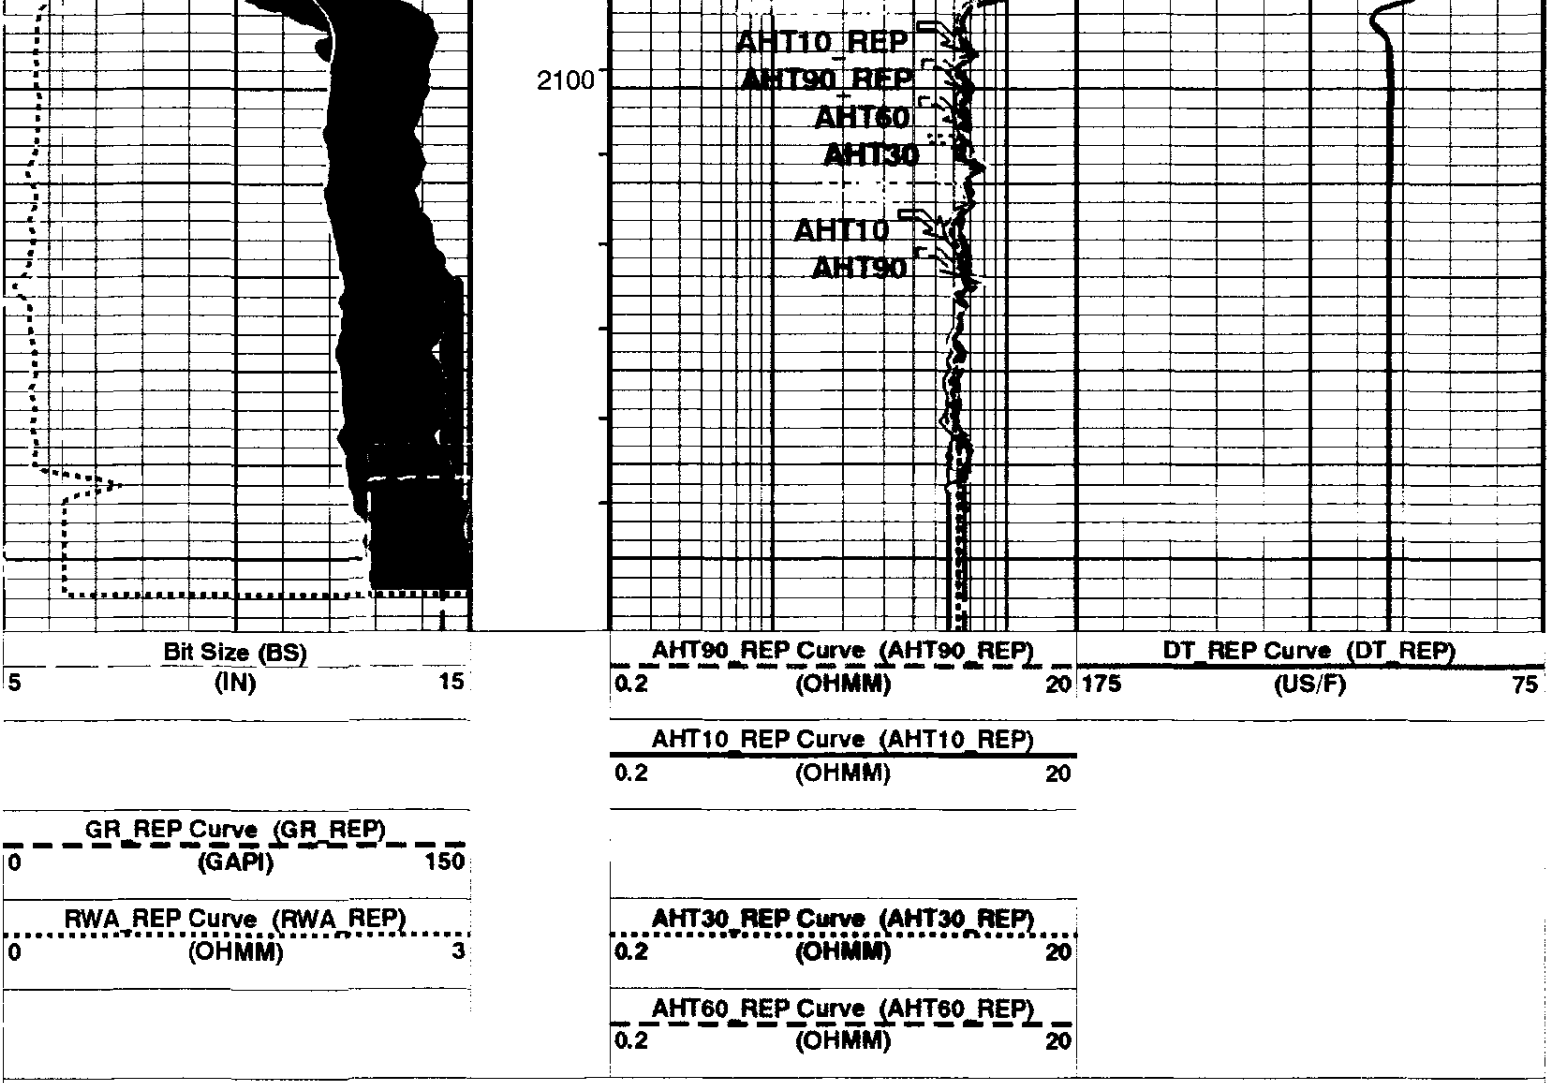

PIP SUMMARY

⊣ Integrated Transit Time Minor Pip Every 1 MS

⊣ Integrated Transit Time Major Pip Every 10 MS

■ Time Mark Every 60 S

Parameters

DLIS Name	Description	Value	
AHBHM	Array Induction Borehole Correction Mode	2_ComputeStandoff	
AHBHV	Array Induction Borehole Correction Code Version Number	870	
AHBLM	Array Induction Basic Logs Mode	6_One_Two_and_Four	
AHBLV	Array Induction Basic Logs Code Version Number	973	
AHBPO	Array Induction Basic Logs Processing Option	Standard_Processing	
AHCDE	Array Induction Casing Detection Enable	Yes	
AHCEN	Array Induction Tool Centering Flag (in Borehole)	Eccentered	
AHCSED	Array Induction Casing Shoe Estimated Depth	-50000	FT
AHFRSV	Array Induction Response Set Version for Four ft Resolution	30.66.23.11	
AHMRF	Array Induction Mud Resistivity Factor	1	
AHORSV	Array Induction Response Set Version for One ft Resolution	30.66.23.11	
AHRFV	Array Induction Radial Profiling Code Version Number	700	
AHRPV	Array Induction Radial Parametrization Code Version Number	710	
AHSTA	Array Induction Tool Standoff	1.5	IN
AHTRSV	Array Induction Response Set Version for Two ft Resolution	30.66.23.11	
BHT	Bottom Hole Temperature (used in calculations)	86	DEGF
BS	Bit Size	6.250	IN
DFD	Drilling Fluid Density	8.90	LB/G
DO	Depth Offset for Logical Unit 1	5.0	FT
DORL	Depth Offset Repeat Analysis	5.0	FT
DTCM	Delta-T Computation Mode	FULL	
FEXP	Form Factor Exponent	2	
FNUM	Form Factor Numerator	1	
GCSE	Generalized Caliper Selection	HCAL	
GDEV	Average Angular Deviation of Borehole from Normal	12	DEG
GGRD	Geothermal Gradient	0.01	DF/F
GRSE	Generalized Mud Resistivity Selection	AITH_RESIST	
GTSE	Generalized Temperature Selection	LINEAR_ESTIMATE	
HSCM	HILT Speed Correction Mode	NO_SC	
HSTI	STI Uses HILT Acceleration	YES	
MODE	Sonic Firing Mode	BHC	
MST	Mud Sample Temperature	76.00	DEGF
PP	Playback Processing	NORMAL	
SHT	Surface Hole Temperature	68	DEGF
SPNV	SP Next Value	0	MV
TD	Total Depth	2151	FT

Format: AITSON_REP Vertical Scale: 5" per 100' Graphics File Created: 21-May-2000 13:31

OP System Version: 9C1-303

MCM

HILTB-DTB	**OP91-KP1a**	**DSLT-TCC**	**OP91-KP1a**
TCC-BF	**OP91-KP1a**		

Input DLIS Files

DEFAULT	**HILTB .006**	**FN:5**	**PRODUCER**	**21-May-2000 12:08**	**2148.0 FT**	**0.0 FT**
DEFAULT	**HILTB .004**	**FN:3**	**PRODUCER**	**21-May-2000 11:50**	**2154.0 FT**	**1826.2 FT**

Output DLIS Files

DEFAULT	**HILTB .007**	**FN:6**	**PRODUCER**	**21-May-2000 13:30**

Schlumberger

CALIBRATIONS

MAXIS 500 Field Log

Calibration and Check Summary

Measurement	Nominal	Master	Before	After	Change	Limit	Units
High resolution Integrated Logging Tool-CTS Wellsite Calibration - Electronics Calibration Check - Thru Cal Mag. & Phase							
Master: Calibration out of date 20-JAN-2000 11:39 Before: 21-MAY-2000 11:23							
Thru Cal Magnitude - 0	0	0.6214	0.6342	N/A	N/A	N/A	V
Thru Cal Magnitude - 1	0	1.274	1.300	N/A	N/A	N/A	V
Thru Cal Magnitude - 2	0	0.6329	0.6459	N/A	N/A	N/A	V
Thru Cal Magnitude - 3	0	0.7152	0.7301	N/A	N/A	N/A	V
Thru Cal Magnitude - 4	0	1.335	1.362	N/A	N/A	N/A	V
Thru Cal Magnitude - 5	0	1.943	1.983	N/A	N/A	N/A	V
Thru Cal Magnitude - 6	0	1.947	1.987	N/A	N/A	N/A	V
Thru Cal Magnitude - 7	0	1.371	1.401	N/A	N/A	N/A	V
Phase - 0	0	64.91	65.66	N/A	N/A	N/A	DEG
Phase - 1	0	63.80	64.55	N/A	N/A	N/A	DEG
Phase - 2	0	60.03	60.78	N/A	N/A	N/A	DEG
Phase - 3	0	59.25	60.01	N/A	N/A	N/A	DEG
Phase - 4	0	52.91	53.69	N/A	N/A	N/A	DEG
Phase - 5	0	50.96	51.75	N/A	N/A	N/A	DEG
Phase - 6	0	50.92	51.71	N/A	N/A	N/A	DEG
Phase - 7	0	47.08	47.97	N/A	N/A	N/A	DEG
High resolution Integrated Logging Tool-CTS Wellsite Calibration - Electronics Calibration Check - Auxilliary							
Master: Calibration out of date 20-JAN-2000 11:39 Before: 21-MAY-2000 11:23							
Array Induction SPA Plus	990.5	989.8	990.4	N/A	N/A	N/A	MV
Array Induction SPA Zero	0	0.1083	0.1083	N/A	N/A	N/A	MV
Array Induction Temperature Pl	0.9150	0.9169	0.9175	N/A	N/A	N/A	V
Array Induction Temperature Ze	0	0.0001095	0.0001059	N/A	N/A	N/A	V
High resolution Integrated Logging Tool-CTS Wellsite Calibration - Test Loop Gain Correction							
Master: Calibration out of date 20-JAN-2000 11:39							
Test Loop Gain Magnitude - 0	0	1.042	N/A	N/A	N/A	N/A	V
Test Loop Gain Magnitude - 1	0	1.011	N/A	N/A	N/A	N/A	V
Test Loop Gain Magnitude - 2	0	1.012	N/A	N/A	N/A	N/A	V
Test Loop Gain Magnitude - 3	0	1.010	N/A	N/A	N/A	N/A	V
Test Loop Gain Magnitude - 4	0	0.9940	N/A	N/A	N/A	N/A	V
Test Loop Gain Magnitude - 5	0	0.9835	N/A	N/A	N/A	N/A	V
Test Loop Gain Magnitude - 6	0	0.9934	N/A	N/A	N/A	N/A	V
Test Loop Gain Magnitude - 7	0	0.9945	N/A	N/A	N/A	N/A	V
Phase - 0	0	0.3672	N/A	N/A	N/A	N/A	DEG
Phase - 1	0	-0.6191	N/A	N/A	N/A	N/A	DEG
Phase - 2	0	-0.01578	N/A	N/A	N/A	N/A	DEG
Phase - 3	0	0.1871	N/A	N/A	N/A	N/A	DEG
Phase - 4	0	0.1325	N/A	N/A	N/A	N/A	DEG
Phase - 5	0	-0.1680	N/A	N/A	N/A	N/A	DEG
Phase - 6	0	0.2889	N/A	N/A	N/A	N/A	DEG
Phase - 7	0	-0.2642	N/A	N/A	N/A	N/A	DEG

High resolution Integrated Logging Tool-CTS Wellsite Calibration - Sonde Error Correction

Master: Calibration out of date 20-JAN-2000 11:39

R Sonde Error Correction - 0	0	-121.4	N/A	N/A	N/A	N/A	MM/M
R Sonde Error Correction - 1	0	149.7	N/A	N/A	N/A	N/A	MM/M
R Sonde Error Correction - 2	0	113.9	N/A	N/A	N/A	N/A	MM/M
R Sonde Error Correction - 3	0	58.40	N/A	N/A	N/A	N/A	MM/M
R Sonde Error Correction - 4	0	24.16	N/A	N/A	N/A	N/A	MM/M
R Sonde Error Correction - 5	0	11.87	N/A	N/A	N/A	N/A	MM/M
R Sonde Error Correction - 6	0	7.431	N/A	N/A	N/A	N/A	MM/M
R Sonde Error Correction - 7	0	-3.605	N/A	N/A	N/A	N/A	MM/M
X Sonde Error Correction - 0	0	34.14	N/A	N/A	N/A	N/A	MM/M
X Sonde Error Correction - 1	0	-240.4	N/A	N/A	N/A	N/A	MM/M
X Sonde Error Correction - 2	0	67.33	N/A	N/A	N/A	N/A	MM/M
X Sonde Error Correction - 3	0	81.72	N/A	N/A	N/A	N/A	MM/M
X Sonde Error Correction - 4	0	-1.172	N/A	N/A	N/A	N/A	MM/M
X Sonde Error Correction - 5	0	-10.09	N/A	N/A	N/A	N/A	MM/M
X Sonde Error Correction - 6	0	10.78	N/A	N/A	N/A	N/A	MM/M
X Sonde Error Correction - 7	0	0.3313	N/A	N/A	N/A	N/A	MM/M

High resolution Integrated Logging Tool-CTS Wellsite Calibration - Mud Gain Correction

Master: Calibration out of date 20-JAN-2000 11:39

Coarse - Mag, Real, Imag - 0	0	1.013	N/A	N/A	N/A	N/A	
Coarse - Mag, Real, Imag - 1	0	1.013	N/A	N/A	N/A	N/A	
Coarse - Mag, Real, Imag - 2	0	1.013	N/A	N/A	N/A	N/A	
Fine - Mag, Real, Imag - 0	0	1.011	N/A	N/A	N/A	N/A	
Fine - Mag, Real, Imag - 1	0	1.011	N/A	N/A	N/A	N/A	
Fine - Mag, Real, Imag - 2	0	1.011	N/A	N/A	N/A	N/A	

High resolution Integrated Logging Tool-CTS Wellsite Calibration - Stab Measurement Summary

Before: 7-MAY-2000 5:52

BS Window Ratio	1.033	N/A	1.022	N/A	N/A	N/A	
BS Window Sum	14310	N/A	14410	N/A	N/A	N/A	CPS
SS Window Ratio	0.5004	N/A	0.5048	N/A	N/A	N/A	
SS Window Sum	11490	N/A	11420	N/A	N/A	N/A	CPS
LS Window Ratio	0.2862	N/A	0.2864	N/A	N/A	N/A	
LS Window Sum	1163	N/A	1156	N/A	N/A	N/A	CPS

High resolution Integrated Logging Tool-CTS Wellsite Calibration - Photo-multiplier High Voltages Calibrations

Before: 7-MAY-2000 5:52

BS PM High Voltage (Command)	1614	N/A	1634	N/A	N/A	N/A	V
SS PM High Voltage (Command)	1916	N/A	1955	N/A	N/A	N/A	V
LS PM High Voltage (Command)	1966	N/A	1974	N/A	N/A	N/A	V

High resolution Integrated Logging Tool-CTS Wellsite Calibration - Crystal Quality Resolutions Calibration

Before: 7-MAY-2000 5:52

BS Crystal Resolution	12.26	N/A	12.52	N/A	N/A	N/A	%
SS Crystal Resolution	11.63	N/A	12.18	N/A	N/A	N/A	%
LS Crystal Resolution	10.59	N/A	10.66	N/A	N/A	N/A	%

High resolution Integrated Logging Tool-CTS Wellsite Calibration - MCFL Calibration

Before: 21-MAY-2000 11:23

Raw B0 Resistivity	3875	N/A	3845	N/A	N/A	N/A	OHMM
Raw B1 Resistivity	3830	N/A	3806	N/A	N/A	N/A	OHMM
Raw B2 Resistivity	3830	N/A	3815	N/A	N/A	N/A	OHMM

High resolution Integrated Logging Tool-CTS Wellsite Calibration - HILT Caliper Calibration

Before: 21-MAY-2000 11:17

HILT Caliper Zero Measurement	8.000	N/A	7.179	N/A	N/A	N/A	IN
HILT Caliper Plus Measurement	16.00	N/A	15.34	N/A	N/A	N/A	IN

High resolution Integrated Logging Tool-CTS Wellsite Calibration - Detector Calibration

Before: 7-MAY-2000 5:47

Gamma Ray Background	30.00	N/A	23.06	N/A	N/A	N/A	GAPI
Gamma Ray (Jig - Bkg)	193.6	N/A	193.6	N/A	N/A	17.60	GAPI
Gamma Ray (Calibrated)	165.0	N/A	173.7	N/A	N/A	15.00	GAPI

High resolution Integrated Logging Tool-CTS Wellsite Calibration - Zero Measurement

Master: 6-APR-2000 4:31 Before: 7-MAY-2000 5:49

CNTC Background	27.31	27.31	26.03	N/A	N/A	4.096	CPS
CFTC Background	28.31	28.31	30.62	N/A	N/A	4.247	CPS

High resolution Integrated Logging Tool-CTS Wellsite Calibration - Accelerometer Calibration

Before: Calibration not done

Z-Axis Acceleration	32.19	N/A	32.19	N/A	N/A	N/A	F/S2

The GLS-VJ source activity is acceptable.

The HGNS Neutron Master Calibration was done with the following parameters :

NCT-B Water Temperature	90.0	DEGF.
Thermal Housing Size	3.375	IN.

High resolution Integrated Logging Tool-CTS / Equipment Identification

Primary Equipment:

Array Induction Tool - H	AIT - H	
Rm/SP Bottom Nose	AHRM - A	
Array Induction Sonde	AHIS - BA	112
HILT high-Resolution Mechanical Sonde	HRMS - B	723
HILT Rxo Gamma-ray Device	HRGD -	723
HILT Nuclear Back-Scatter Detector	HILT -	
HILT Nuclear Short-Spacing Detector	HILT -	
HILT Nuclear Long-Spacing Detector	HILT -	

Auxiliary Equipment:

High resolution Integrated Logging Tool-CTS Wellsite Calibration

Electronics Calibration Check - Thru Cal Mag. & Phase

Idx	Phase	Value	Thru Cal Magnitude V	Nominal	Value	Phase DEG	Nominal
0	Master	0.6214		0.6050	64.91		71.00
	Before	0.6342			65.66		
1	Master	1.274		1.270	63.80		70.00
	Before	1.300			64.55		
2	Master	0.6329		0.6230	60.03		66.00
	Before	0.6459			60.78		
3	Master	0.7152		0.7040	59.25		65.00
	Before	0.7301			60.01		
4	Master	1.335		1.337	52.91		59.00
	Before	1.362			53.69		
5	Master	1.943		1.955	50.96		57.00
	Before	1.983			51.75		
6	Master	1.947		1.955	50.92		57.00
	Before	1.987			51.71		
7	Master	1.371		1.415	47.08		53.00
	Before	1.401			47.97		
			60.00 % (Minimum) (Nominal) 140.0 % (Maximum)			Nom -60.00 (Minimum) (Nominal) Nom + 60.00 (Maximum)	

Master: Calibration out of date 20-JAN-2000 11:39 Before: 21-MAY-2000 11:23

High resolution Integrated Logging Tool-CTS Wellsite Calibration

Electronics Calibration Check - Auxilliary

Phase	Array Induction SPA Plus MV	Value	Phase	Array Induction SPA Zero MV	Value
Master		989.8	Master		0.1083
Before		990.4	Before		0.1083
	941.0 (Minimum) 990.5 (Nominal) 1040 (Maximum)			-50.00 (Minimum) 0 (Nominal) 50.00 (Maximum)	

Phase	Array Induction Temperature Plus V	Value	Phase	Array Induction Temperature Zero V	Value
Master		0.9169	Master		0.0001095
Before		0.9175	Before		0.0001059
	0.8700 (Minimum) 0.9150 (Nominal) 0.9600 (Maximum)			-0.05000 (Minimum) 0 (Nominal) 0.05000 (Maximum)	

Master: Calibration out of date 20-JAN-2000 11:39 Before: 21-MAY-2000 11:23

High resolution Integrated Logging Tool-CTS Wellsite Calibration

Test Loop Gain Correction

Idx	Value	Test Loop Gain Magnitude V	Value	Phase DEG
0	1.042		0.3672	
	0.9500 (Minimum)	1.000 (Nominal) 1.050 (Maximum)	-3.000 (Minimum)	0 (Nominal) 3.000 (Maximum)
1	1.011		-0.6191	
	0.9500 (Minimum)	1.000 (Nominal) 1.050 (Maximum)	-3.000 (Minimum)	0 (Nominal) 3.000 (Maximum)
2	1.012		-0.01578	
	0.9500 (Minimum)	1.000 (Nominal) 1.050 (Maximum)	-3.000 (Minimum)	0 (Nominal) 3.000 (Maximum)
3	1.010		0.1871	
	0.9500 (Minimum)	1.000 (Nominal) 1.050 (Maximum)	-3.000 (Minimum)	0 (Nominal) 3.000 (Maximum)
4	0.9940		0.1325	
	0.9500 (Minimum)	1.000 (Nominal) 1.050 (Maximum)	-3.000 (Minimum)	0 (Nominal) 3.000 (Maximum)
5	0.9835		-0.1680	
	0.9500 (Minimum)	1.000 (Nominal) 1.050 (Maximum)	-3.000 (Minimum)	0 (Nominal) 3.000 (Maximum)
6	0.9934		0.2889	
	0.9500 (Minimum)	1.000 (Nominal) 1.050 (Maximum)	-3.000 (Minimum)	0 (Nominal) 3.000 (Maximum)
7	0.9945		-0.2642	
	0.9500 (Minimum)	1.000 (Nominal) 1.050 (Maximum)	-3.000 (Minimum)	0 (Nominal) 3.000 (Maximum)

Master: Calibration out of date 20-JAN-2000 11:39

High resolution Integrated Logging Tool-CTS Wellsite Calibration

Sonde Error Correction

Idx	Value	R Sonde Error Correction MM/M	Value	X Sonde Error Correction MM/M
0	-121.4		34.14	
	-231.0 (Minimum)	-56.00 (Nominal) 119.0 (Maximum)	-2250 (Minimum)	0 (Nominal) 2250 (Maximum)
1	149.7		-240.4	
	114.0 (Minimum)	159.0 (Nominal) 204.0 (Maximum)	-625.0 (Minimum)	0 (Nominal) 625.0 (Maximum)
2	113.9		67.33	
	66.00 (Minimum)	111.0 (Nominal) 156.0 (Maximum)	-350.0 (Minimum)	0 (Nominal) 350.0 (Maximum)
3	58.40		81.72	
	39.00 (Minimum)	64.00 (Nominal) 89.00 (Maximum)	-250.0 (Minimum)	0 (Nominal) 250.0 (Maximum)
4	24.16		-1.172	
	15.00 (Minimum)	25.00 (Nominal) 35.00 (Maximum)	-63.00 (Minimum)	0 (Nominal) 63.00 (Maximum)
5	11.87		-10.09	
	4.000 (Minimum)	14.00 (Nominal) 24.00 (Maximum)	-50.00 (Minimum)	0 (Nominal) 50.00 (Maximum)
6	7.431		10.78	
	5.000 (Minimum)	10.00 (Nominal) 15.00 (Maximum)	-30.00 (Minimum)	0 (Nominal) 30.00 (Maximum)
7	-3.605		0.3313	
	-5.000 (Minimum)	0 (Nominal) 5.000 (Maximum)	-30.00 (Minimum)	0 (Nominal) 30.00 (Maximum)

Master: Calibration out of date 20-JAN-2000 11:39

High resolution Integrated Logging Tool-CTS Wellsite Calibration

Mud Gain Correction

Idx	Value	Coarse - Mag, Real, Imag	Value	Fine - Mag, Real, Imag
0	1.013		1.011	
	0.8000 (Minimum)	1.000 (Nominal) 1.200 (Maximum)	0.8000 (Minimum)	1.000 (Nominal) 1.200 (Maximum)
1	1.013		1.011	
	0.8000 (Minimum)	1.000 (Nominal) 1.200 (Maximum)	0.8000 (Minimum)	1.000 (Nominal) 1.200 (Maximum)
2	1.013		1.011	
	0.8000 (Minimum)	1.000 (Nominal) 1.200 (Maximum)	0.8000 (Minimum)	1.000 (Nominal) 1.200 (Maximum)

Master: Calibration out of date 20-JAN-2000 11:39

High resolution Integrated Logging Tool-CTS Wellsite Calibration

Stab Measurement Summary

Phase	BS Window Ratio	Value	Phase	SS Window Ratio	Value	Phase	LS Window Ratio	Value
Before		1.022	Before		0.5048	Before		0.2864
0.9818 (Minimum)	1.033 (Nominal)	1.085 (Maximum)	0.4754 (Minimum)	0.5004 (Nominal)	0.5255 (Maximum)	0.2719 (Minimum)	0.2862 (Nominal)	0.3005 (Maximum)

Phase	BS Window Sum CPS	Value	Phase	SS Window Sum CPS	Value	Phase	LS Window Sum CPS	Value
Before		14410	Before		11420	Before		1156
13590 (Minimum)	14310 (Nominal)	15020 (Maximum)	10920 (Minimum)	11490 (Nominal)	12070 (Maximum)	1105 (Minimum)	1163 (Nominal)	1221 (Maximum)

Before: 7-MAY-2000 5:52

High resolution Integrated Logging Tool-CTS Wellsite Calibration

Photo-multiplier High Voltages Calibrations

Phase	BS PM High Voltage (Command) V	Value	Phase	SS PM High Voltage (Command) V	Value	Phase	LS PM High Voltage (Command) V	Value
Before		1634	Before		1955	Before		1974
1514 (Minimum)	1614 (Nominal)	1714 (Maximum)	1816 (Minimum)	1916 (Nominal)	2016 (Maximum)	1866 (Minimum)	1966 (Nominal)	2066 (Maximum)

Before: 7-MAY-2000 5:52

High resolution Integrated Logging Tool-CTS Wellsite Calibration

Crystal Quality Resolutions Calibration

Phase	BS Crystal Resolution %	Value	Phase	SS Crystal Resolution %	Value	Phase	LS Crystal Resolution %	Value
Before		12.52	Before		12.18	Before		10.66
11.26 (Minimum)	12.26 (Nominal)	13.26 (Maximum)	10.63 (Minimum)	11.63 (Nominal)	12.63 (Maximum)	9.591 (Minimum)	10.59 (Nominal)	11.59 (Maximum)

Before: 7-MAY-2000 5:52

High resolution Integrated Logging Tool-CTS Wellsite Calibration

MCFL Calibration

Phase	Raw B0 Resistivity OHMM	Value	Phase	Raw B1 Resistivity OHMM	Value	Phase	Raw B2 Resistivity OHMM	Value
Before		3845	Before		3806	Before		3815
3565 (Minimum)	3875 (Nominal)	4185 (Maximum)	3524 (Minimum)	3830 (Nominal)	4136 (Maximum)	3524 (Minimum)	3830 (Nominal)	4136 (Maximum)

Before: 21-MAY-2000 11:23

High resolution Integrated Logging Tool-CTS Wellsite Calibration

HILT Caliper Calibration

Phase	HILT Caliper Zero Measurement IN	Value	Phase	HILT Caliper Plus Measurement IN	Value
Before		7.179	Before		15.34
6.000 (Minimum)	8.000 (Nominal)	10.00 (Maximum)	12.00 (Minimum)	16.00 (Nominal)	20.00 (Maximum)

Before: 21-MAY-2000 11:17

High resolution Integrated Logging Tool-CTS Wellsite Calibration

Detector Calibration

Phase	Gamma Ray Background GAPI	Value	Phase	Gamma Ray (Jig - Bkg) GAPI	Value	Phase	Gamma Ray (Calibrated) GAPI	Value
Before		23.06	Before		193.6	Before		173.7
0 (Minimum)	30.00 (Nominal)	120.0 (Maximum)	176.0 (Minimum)	193.6 (Nominal)	211.2 (Maximum)	150.0 (Minimum)	165.0 (Nominal)	180.0 (Maximum)

Before: 7-MAY-2000 5:47

High resolution Integrated Logging Tool-CTS Wellsite Calibration

Zero Measurement

Phase	CNTC Background CPS	Value	Phase	CFTC Background CPS	Value
Master		27.31	Master		28.31
Before		26.03	Before		30.62
5.000 (Minimum)	27.31 (Nominal)	40.00 (Maximum)	5.000 (Minimum)	28.31 (Nominal)	40.00 (Maximum)

Master: 6-APR-2000 4:31

Before: 7-MAY-2000 5:49

High resolution Integrated Logging Tool-CTS Wellsite Calibration

Accelerometer Calibration

Phase	Z-Axis Acceleration F/S2	Value
Before		32.19
31.53 (Minimum)	32.19 (Nominal)	32.84 (Maximum)

Before: Calibration not done

COMPANY: **NORTHWEST NATURAL GAS**

WELL: **OM 22-26-65 RD**
FIELD: **MIST**
COUNTY: **COLUMBIA**
STATE: **OREGON**

BOTTOM LOG INTERVAL	2136 ft
SCHLUMBERGER DEPTH	2144 ft
DEPTH DRILLER	2151 ft
KELLY BUSHING	631 ft
DRILL FLOOR	629 ft
GROUND LEVEL	621 ft

Schlumberger

ARRAY INDUCTION
BHC SONIC /SP/GR
SCALE: 5" = 100'
