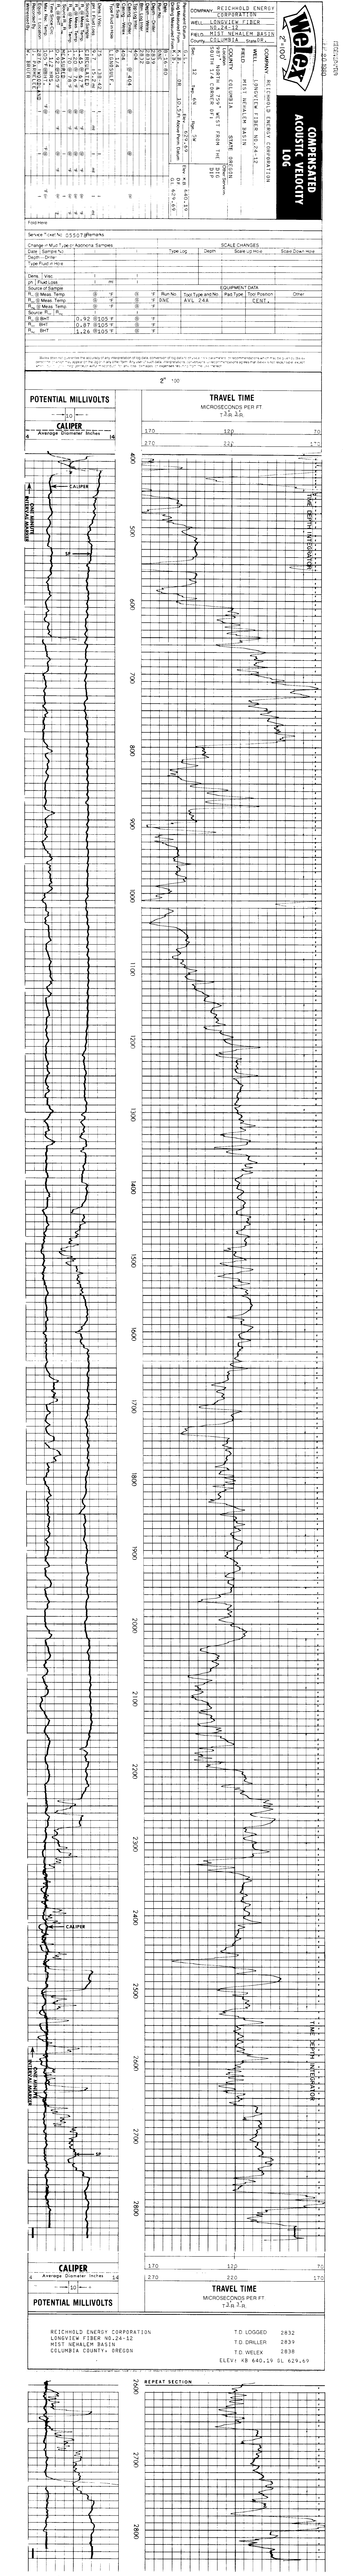
COMPANY REICHOLD ENERGY CORPORATION
WELL LONGVIEW FIBRE
FIELD WEST SCHALLER BASIN
County COLUMBIA State OREG.
COMPANY REICHOLD ENERGY CORPORATION
WELL LONGVIEW FIBRE 32-24-12
FIELD WEST SCHALLER BASIN
COUNTY COLUMBIA STATE OREGON
Location: 1980' FSL & 1980' FEL
Other Services: DIL, CNL, GR, CAL
Permanent Datum: GROUND LEVEL Elev.: 429
Log Measured From: KELLY BUSHING 12 Ft. Above Perm. Datum
Drilling Measured From: KELLY BUSHING
Elev.: K.B. 441 D.F. G.L. 429
Date: 12-2-81
Run No.: ONE
Depth-Driller: 2832
Depth-Logger: 2832
Bottom Logged Interval: 2832
Top Logged Interval: SURFACE
Type Fluid in Hole: LIGNOSULFONATE
Salinity, PPM Cl: 1000
Density: 9.2
Viscosity: 38
Fluid Loss: 8.4
Source of Sample: FLOWLINE
Rm @ Meas. Temp.: 0.92 @ 105 °F
Rmf @ Meas. Temp.: 0.87 @ 105 °F
Rmc @ Meas. Temp.: 1.26 @ 105 °F
Source: Rmf: Rmc:
Rm @ BHT: 0.92 @ 105 °F
Rmf @ BHT: 0.87 @ 105 °F
Rmc @ BHT: 1.26 @ 105 °F
Time Since Circ.: 10 HRS
Max. Rec. Temp.: 105 °F
Equip. Location: 5MK
Recorded By: M. FRAZIER
Witnessed By: MR. SMITH
Schlumberger
Welex
COMPENSATED ACOUSTIC VELOCITY LOG
Field Name
Service Order No. 05507
Remarks
Change of Mud Type / Additional Samples
Date / Sample No.
Depth - Driller
Type Fluid in Hole
Dens. / Visc.
pH / Fluid Loss
Source of Sample
Rm @ Meas. Temp.
Rmf @ Meas. Temp.
Rmc @ Meas. Temp.
Source: Rmf: Rmc:
Rm @ BHT
Rmf @ BHT
Rmc @ BHT
SCALE CHANGES
Type Log
Depth
Scale up Hole
Scale Down Hole
EQUIPMENT DATA
Run No.
Tool Type and No.
Pad Type
Tool Position
Other
DIL 5760
AVG. CAL
CENT.
2" /100
POTENTIAL MILLIVOLTS
CALIPER
Average Diameter Inches
BOREHOLE AVERAGE
TRAVEL TIME
MICROSECONDS PER FT
156.86
170
270
120
220
70
170
TIME DEPTH INTEGRATION
CALIPER
POTENTIAL MILLIVOLTS
TRAVEL TIME
MICROSECONDS PER FT
156.86
REICHOLD ENERGY CORPORATION
LONGVIEW FIBRE 32-24-12
WEST SCHALLER BASIN
COLUMBIA COUNTY, OREGON
T.D. LOGGED 2832
T.D. DRILLER 2839
T.D. WELEX 2838
ELEV.: KB 441.19 DL 429.69
REPEAT SECTION
