02-23-345

Schlumberger

DUAL INDUCTION-SFL-SONIC
WITH LINEAR CORRELATION LOG

COMPANY NAHAMA AND WEAGANT ENERGY CO.
WELL SASQUATCH 23-31-65
FIELD MST
COUNTY COLUMBIA
STATE OREGON
Other Services: SFL

Permanent Datum: GL Elevation 936.0 F
Log Measured From: KB 2.0 F Above Permanent Datum
Drilling Measured From: KB

Run No.	ONE			
Date	06-JUN-92			
Depth-Driller	2972.0 F			
Depth-Logger	2974.0 F			
Bottom Logged Interval	2974.0 F			
Top Logged Interval	2000.0 F			
Casing-Driller	13.375 IN @ 957.0 F			
Casing-Logger	13.375 IN @ 957.0 F			
Bit Size	12.250 IN			
Type Fluid in Hole	LSND			
Density	9.6 LB/G			
Viscosity	40.0 S			
PH	10.0			
Fluid Loss	6.0 C3			
Source of Sample	FLOWLINE			
Rm @ Meas. Temp	0.910 @ 70.0 F			
Rmf @ Meas. Temp	0.760 @ 70.0 F			
Rmc @ Meas. Temp	1.140 @ 70.0 F			
Source Rmf / Rmc	MEAS / CALC			
Rm @ BHT	0.370 @ 200.0 F			
Time Since Circ.	12.0 HR			
Max. Rec. Temp.	200.0 F			
Equipment Number	5963	5963	5963	
Location	23-31-65	23-31-65	23-31-65	
Recorded By	BOB	BOB	BOB	
Witnessed By	MACKAMAN	MACKAMAN	MACKAMAN	

API SERIAL NO.			
LOCATION Section	23		
LOCATION Township	31N		
LOCATION Range	6W		
FNL			
FEL			
DERRICK FLOOR			
GROUND LEVEL			
PERMANENT DATUM	GL		
ELEVATION	936.0 F		
ELEVATION	934.0 F		
ELEVATION	936.0 F		

"The well name, location and borehole reference data were furnished by the customer."

All interpretations are opinions based on inferences from electrical or other measurements and we cannot, and do not guarantee the accuracy or correctness of any interpretations, and we shall not be liable or responsible for any loss, costs, damages or expenses incurred or sustained by anyone resulting from any interpretation made by any of our officers, agents or employees. These interpretations are also subject to Clause 4 of our General Terms and Conditions as set out in our current Price Schedule.

Run No.	ONE
Service Order No.	88877
Drilling Fluid Level	100 F
Salinity	1800 PPM
Ami @ BHT	3.907 OHMM @ 66.0 DEGF
Amp @ BHT	2.174 OHMM @ 66.0 DEGF
Logging Speed	3600.0 F/HR
EQUIPMENT DATA	
Tool Number 1	DIS-EC 388
Tool Number 2	DIC-EA 1018
Tool Number 3	MCG-B 190
Tool Number 4	SLS-WA 178
Tool Number 5	SLC-MA 189
Tool Number 6	SGT-E 557
Tool Number 7	6M-BD 304
Tool Number 8	SLM-CA 443
Tool Number 9	NLM-BC 456
Tool Number 10	
Tool Number 11	
Tool Number 12	
REMARKS	

TWO 15' STANDOFFS RUN ON DUAL INDUCTION TOOL
TWO CMAC CENTRALIZERS RUN ON SONIC SONDE

LOGGING TOOL STRING SKETCH

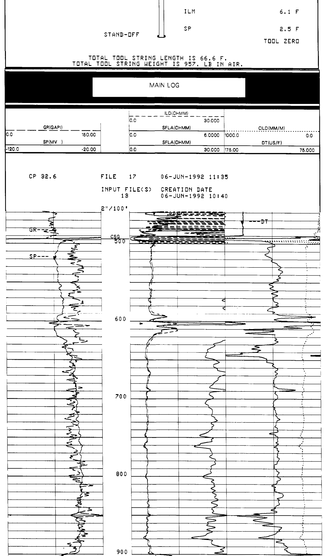

TOTAL TOOL STRING LENGTH IS 66.6 F.
TOTAL TOOL STRING WEIGHT IS 957. LB IN AIR.

MAIN LOG

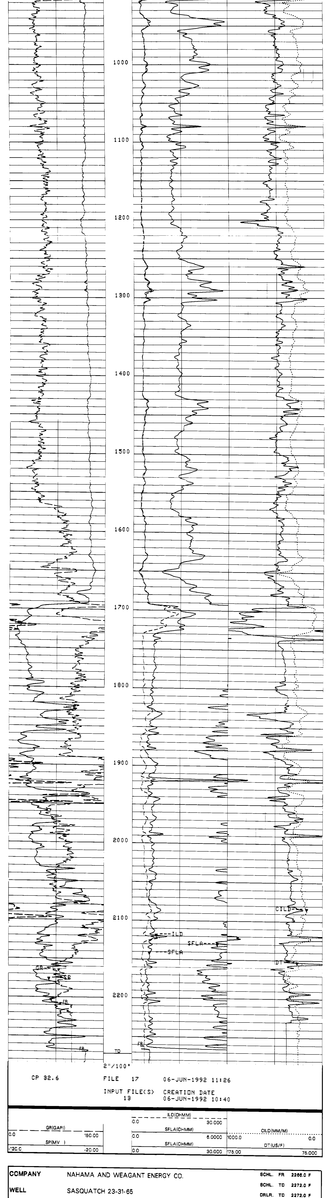

COMPANY	NAHAMA AND WEAGANT ENERGY CO.		
WELL	SASQUATCH 23-31-65		
FIELD	MST		
COUNTY	COLUMBIA	STATE	OREGON

BOML FR	2360.0 F
BOML TO	2372.0 F
DMLR TO	2372.0 F
Elev: KB	936.0 F
DF	934.0 F
GL	936.0 F

Schlumberger

DUAL INDUCTION-SFL-SONIC
WITH LINEAR CORRELATION LOG
