Recreation Pre-Operations Report

Project Name:	Black Rock MTB Trail Construction #3 and #4		
County:	Polk	**District:**	West Oregon
Legal Description:	T8S R7W Section 13	**Management Basin:**	Luckiamute River

Project Type:	Construction
Project Objective:	Downhill mountain bike trail construction
Project Timeline:	July 1st 2026 - June 30th 2027
Project Lead:	Non-motorized Trails Coordinator

I. PROJECT SUMMARY:

Description of Project:

Project work planned flows from the Black Rock MTB Area Trail Plan and FY27 consists of 1.1 miles of new downhill mountain bike trail construction. Prior to trail construction and improvement ODF REI staff will work with Biologists to finalize trail locations to minimize impacts to T&E Species. Work will be completed by volunteers with guidance from ODF REI staff.

II. PROJECT FUNDING

Table 1.

Funding Source	AOP	Future Costs	Total Cost
FDF Account			
Other	Volunteer labor		$0

III. RELATED OPERATIONS

1. Is this Recreation Project associated with, or in close proximity to any other Recreation Project, Harvest Operation (either planned or sold), or Road Project? ☒ No ☐ Yes, describe coordination needed.

IV. WILDLIFE AND T&E SPECIES CONSIDERATIONS:

1. A portion of the Recreation project is within (Check all that apply):

   ☐ TAS ☒ NSO Circle or Home Range, or Baseline or Elevated Baseline Thiessen

   ☐ MMMA ☐ None If yes, consult with the Area Wildlife Biologist and describe outcome here.

2. Will this Recreation project modify potential habitat (i.e. remove trees over six inches in diameter) that would require habitat review? ☒ No ☐ Yes, please describe:

   - If it is determined that modification of potential habitat is necessary during project implementation, the Area Wildlife Biologist will be consulted.

3. Are there any additional considerations (FPA Resource Sites, Species of Concern sites/Plant)? ☐ No ☒ Yes, please describe: Southern torrent salamander occurrence within a ¼ mile of the new trail construction. Southern torrent salamander are a federal species of concern and state sensitive species. The riparian conservation areas implemented for this Annual Operation Plan address the species' needs at the landscape level, including riparian disturbance avoidance. No additional protections are needed.

V. AQUATIC RESOURCES:

1. Do any streams require additional review for the following?
   - Fish presence ☒ No ☐ Yes
   - Perennial/Seasonal: ☐ No ☒ Yes
   - H.E.R./P.D.F.T: ☒ No ☐ Yes
2. Will this Recreation Project occur within the Riparian Conservation Area of any stream?

   ☐ Unknown ☐ No ☒ Yes, describe the # of crossings, stream classifications, planned crossing types:

Stream Crossings	Stream Classification	New Installation or Replacement	Planned Crossing Type
1	Type N	New Installation	Culvert

SSBT = Salmon Steelhead and Bull Trout

3. Is a portion of the project within an Aquatic Anchor? ☒ No ☐ Yes, name:
4. Are any domestic points of diversion identified in the Oregon Water Resource Department's water rights information search GIS database located downstream within 3,000 feet of the harvest operation?

   ☒ No ☐ Yes, describe protection measures:
5. Are there any unregistered or unknown status domestic points of diversion that have been identified within the harvest operation? ☒ No ☐ Yes, please describe:

VI. SLOPE STABILITY ISSUES:

Table 2. Summary of Slope Stability Assessment

Project	Review Complete	Public Safety Review Complete
Black Rock MTB Trail Construction #3 and #4	Yes	Yes

Geotech Review: Initial geotechnical reviews have been completed. Additional consultation with Geotechnical Specialists will be done as needed.

VII. HISTORIC AND CULTURAL RESOURCES:

1. Has the Recreation Project been reviewed by a qualified archaeologist for potential historic or cultural resource presence? ☐ No ☒ Yes

VIII. SCENIC RESOURCES:

1. Are there scenic resources in the vicinity of this operation that need additional consideration?

   ☒ No ☐ Yes, please describe:

IX. OTHER RESOURCE CONSIDERATIONS:

1. Is this Recreation Project within proximity of a property line? ☐ No ☒ Yes, please describe: A section of trail #4 is in close proximity of a property line.
2. Has a review of the FLMCS layer determined that any resources not mentioned in the report above need additional planning? ☒ No ☐ Yes, describe below
3. Are there any other resources present that need additional consideration? ☒ No ☐ Yes, please describe:

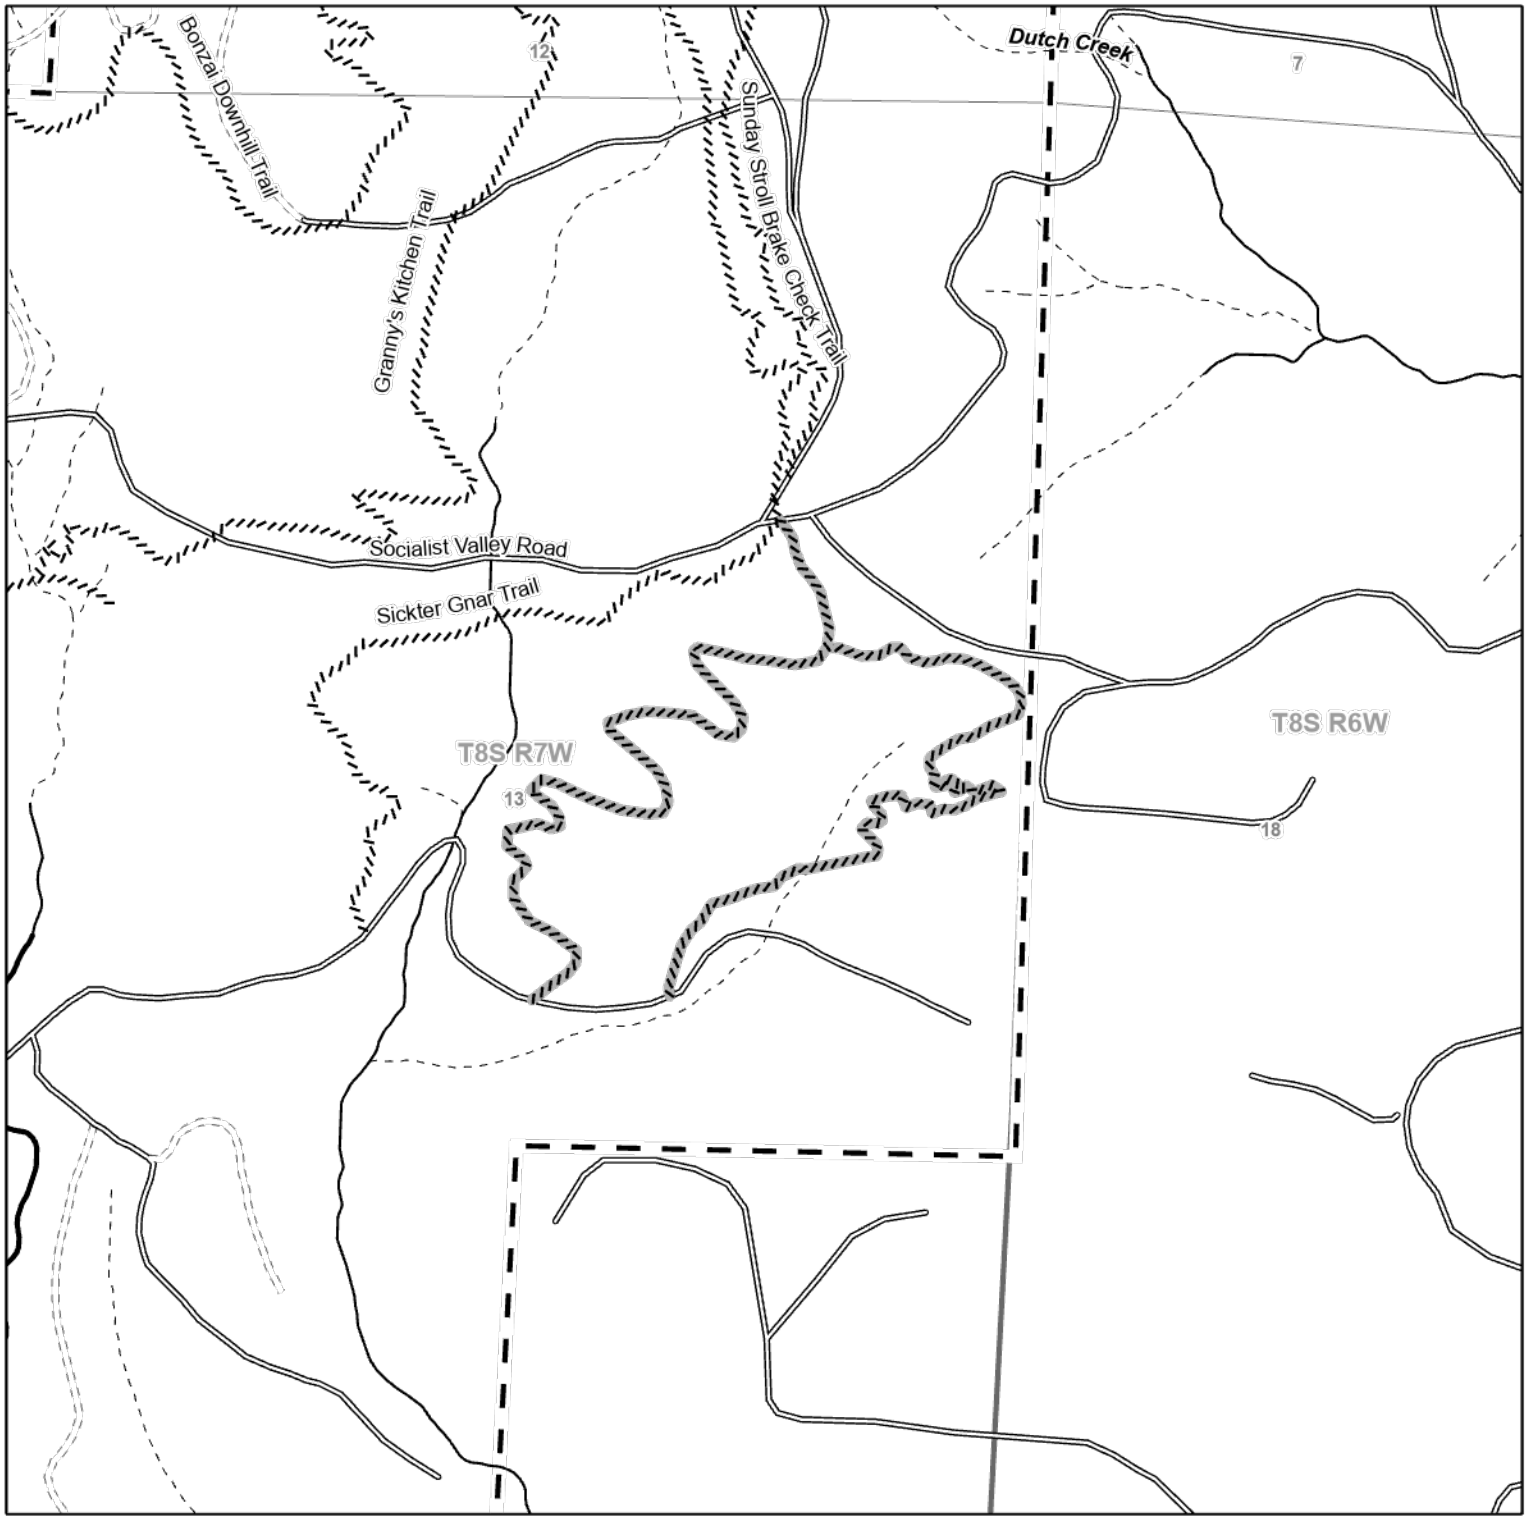

Legend

- Planned FY27 REI Project
- Recreation Trails
- Surfaced Roads
- Unsurfaced Roads
- Perennial Fish Streams
- Perennial Non-Fish Streams
- Seasonal Streams
- Ownership Boundary
- PLSS Townships
- PLSS Sections

FY 2027 - REI
Black Rock MTB Trail Construction #3 & #4
Portions of Section 13, T8S, R7W, W.M.
Polk County

N

State Forest Division
01/02/2026
This product is for informational use and may not be suitable for legal, engineering, or surveying purposes.

1:6,000

500 250 0 500 Feet
